


Arizona State Transportation Board South Central District Update



Presentation by Rod Lane
South Central District Engineer
October 16, 2020


Southcentral District Boundaries NO CHANGES!

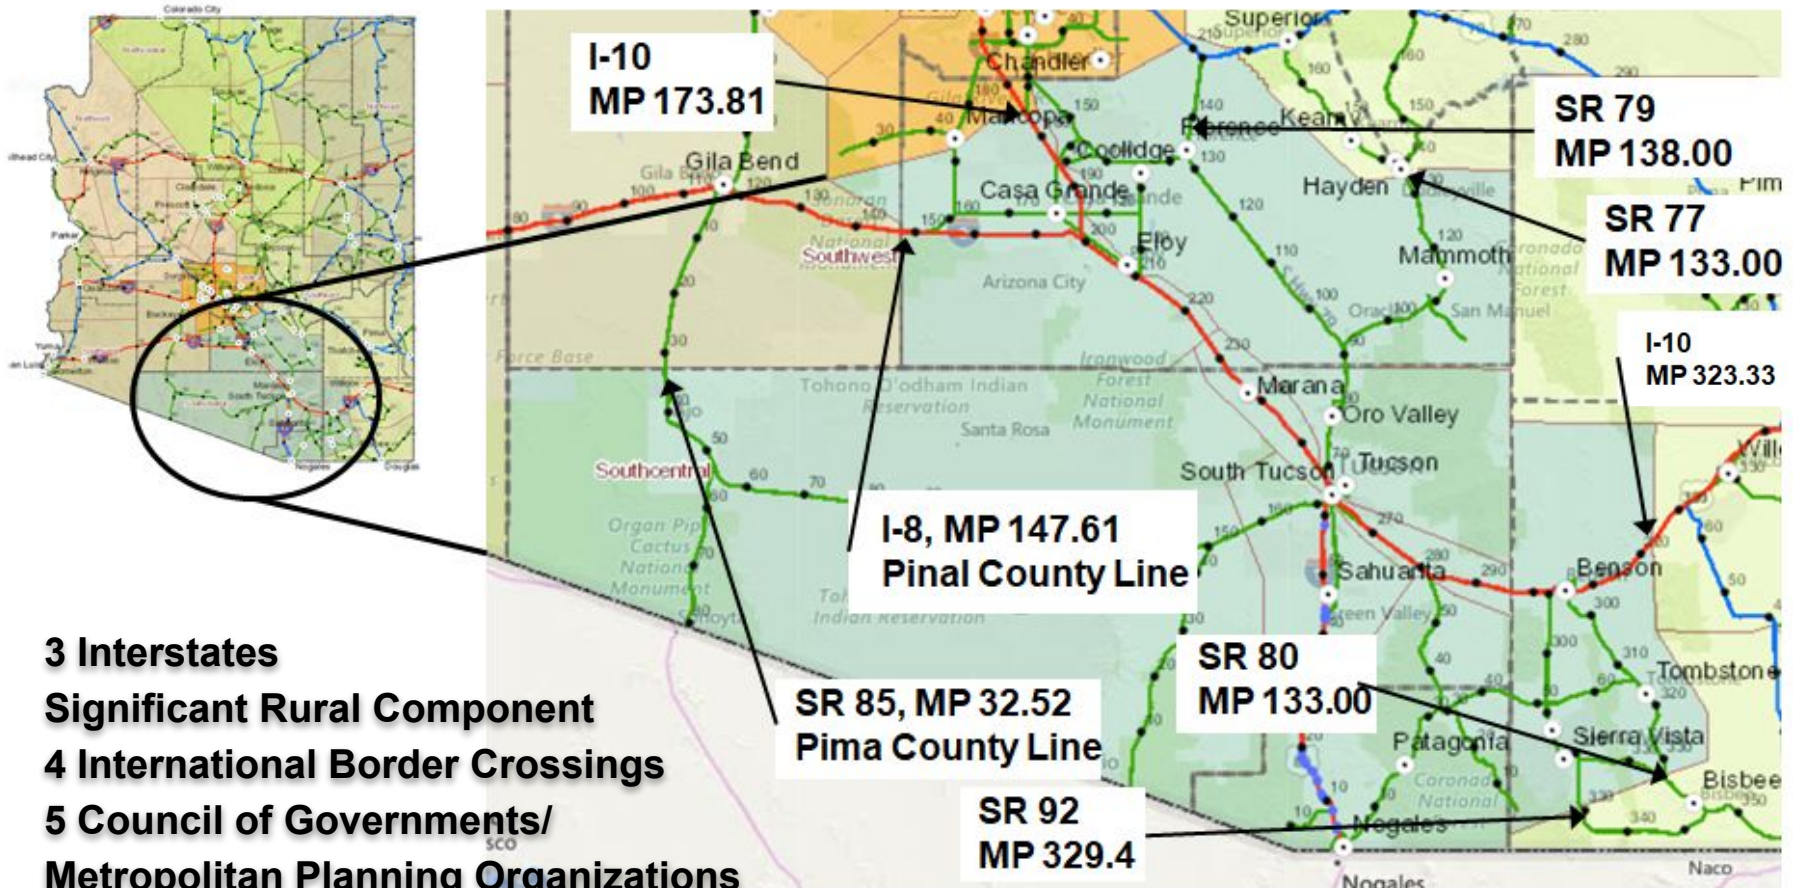

- 3 Interstates
- Significant Rural Component
- 4 International Border Crossings
- 5 Council of Governments/
Metropolitan Planning Organizations
- 5 Tribal Nations

I-19/Ajo T.I.

- Contractor: FNF Construction
- Contract Value: \$32M
- Complete
- Construct new Santa Cruz River bridge, Irvington Rd Braided off-ramp, noise walls, pedestrian bridge

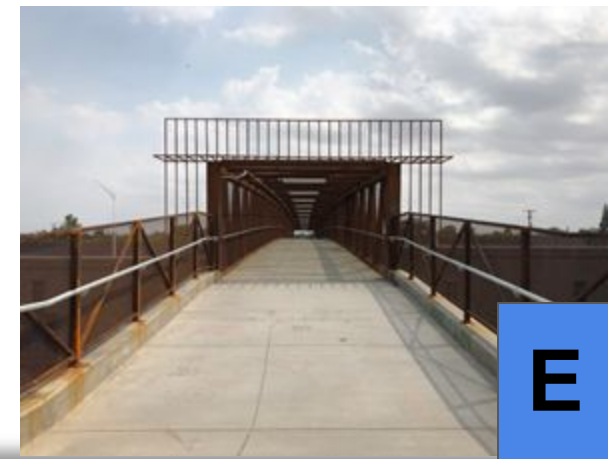


E

I-19, El Toro Rd Bridge

- Contractor: FNF Const
- Contract Value: \$6M
- Delivery Method: LBB
- Expected Completion: Early 2021

Unit 4593 On-Time Project Delivery

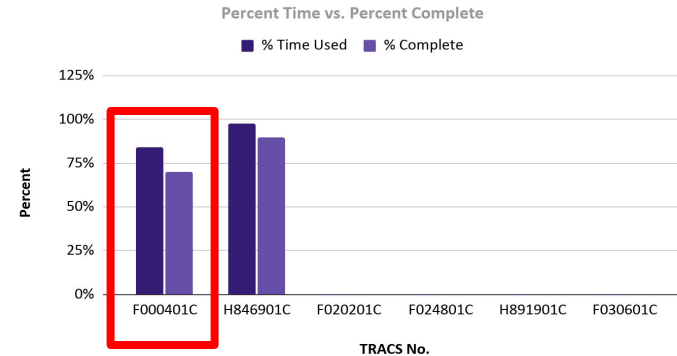


M

SR77, Willow Springs Rd to Old SR77

- Contractor: Granite Const
- Contract Value: \$2.21M
- Delivery Method: LBB
- Expected Completion: wrapping up now




Unit 4592 On-Time Project Delivery

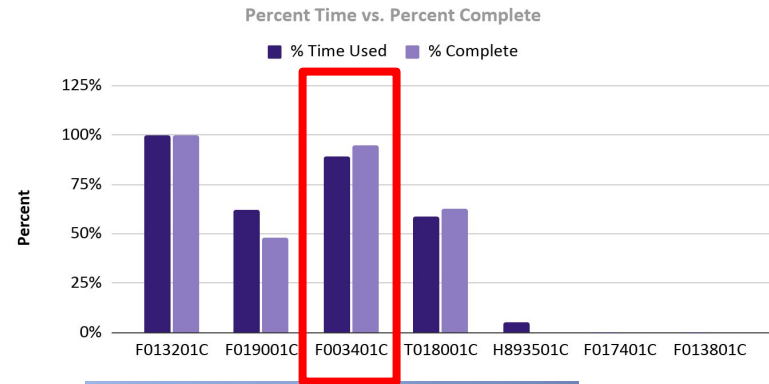

P

SR 189: International Border to Grand Avenue


- Design Build Team: Ames/Horrocks
- Contract Value: \$82M
- Delivery Method: Design Build
- ADOT's GEC: AECOM
- Expected Completion: End of 2021

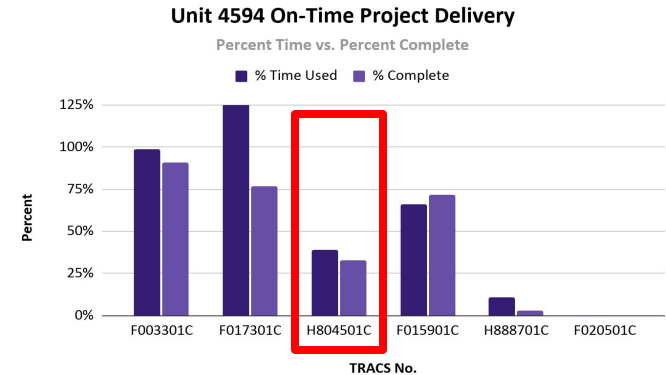

I-10/Ruthrauff Rd T.I.

- Contractor: Sundt Const.
- Contract Value: \$80M
- Delivery Method: LBB, A+B
- Expected Completion: End of 2021
- New Diamond interchange with bridge over UPRR and Highway Drive.

Unit 4591 On-Time Project Delivery

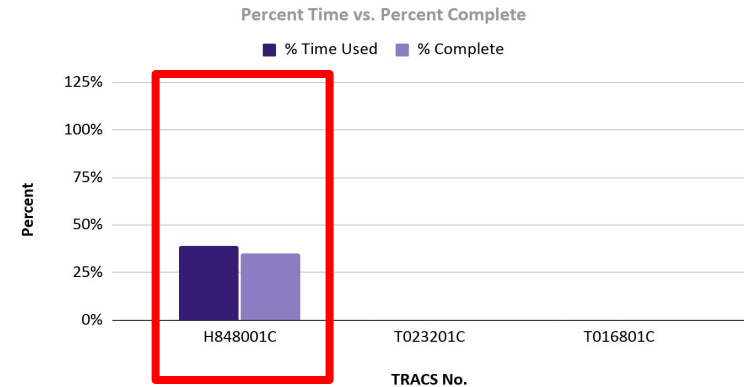


SR86, Fresno to Gap

- Contractor: Granite Const
- Contract Value: \$13.8M
- Delivery Method: LBB
- Expected Completion: Late 2020

Unit 4593 On-Time Project Delivery


Percent Time vs. Percent Complete

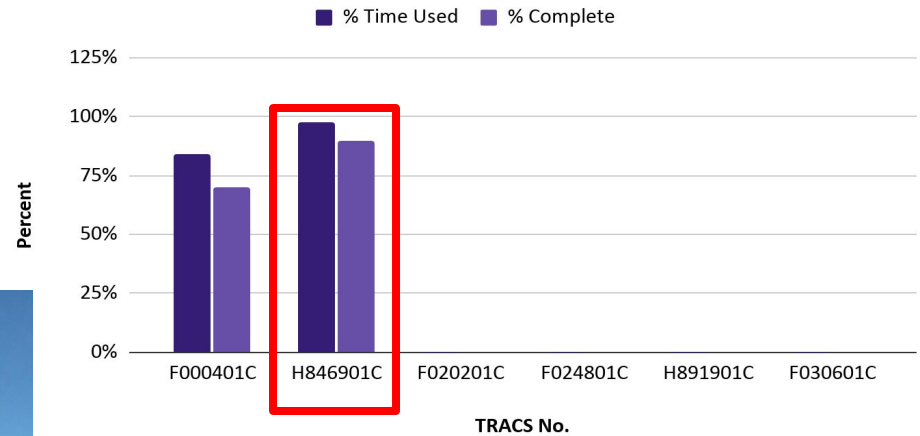


P

I-10/Houghton Rd T.I.

- Contractor: Ames Const
- Contract Value: \$23.4M
- Delivery Method: LBB
- Expected Completion: Late 2021

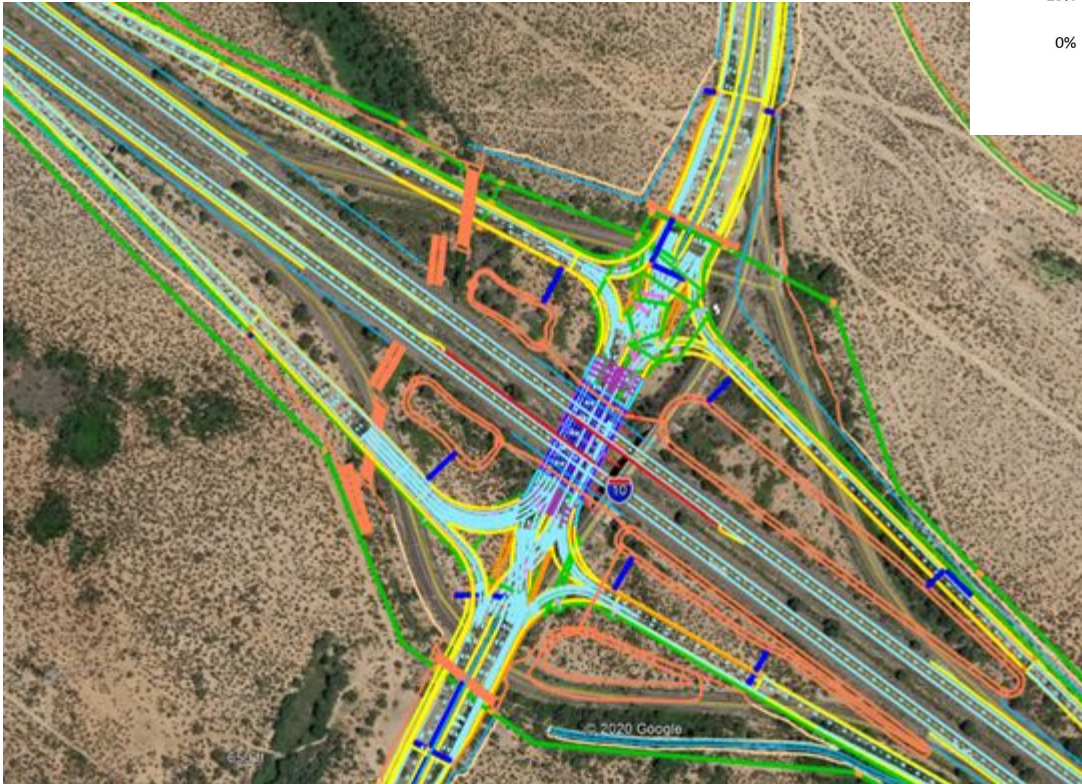


Unit 4594 On-Time Project Delivery

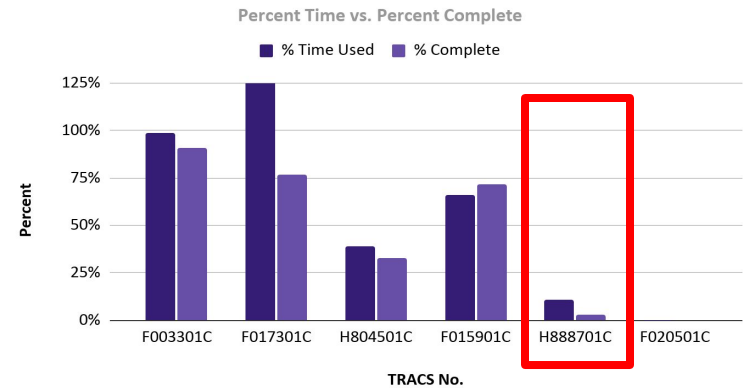

E

- Contractor: Fisher Sand and Gravel
- Contract Value: \$17.26M
- Delivery Method: LBB
- Expected Completion: Late 2021

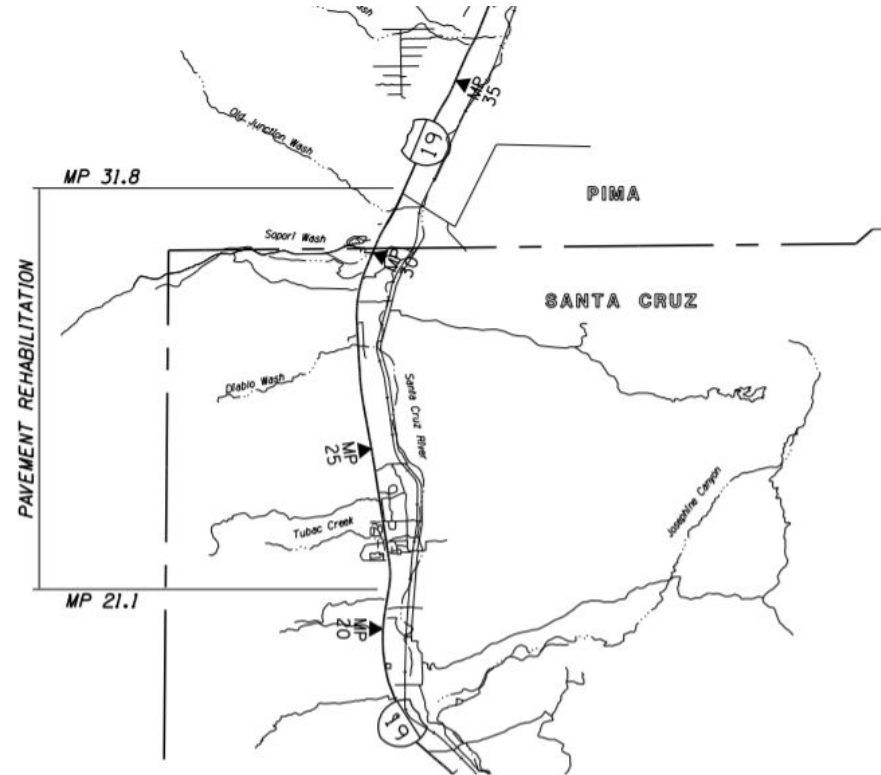


TUBAC – WEST ARIVACA RD

PROJECT NO. 019 SC 021 H8935 01C

FEDERAL AID NO. 019-A(232)T

P

- Apparent Contractor: Granite Const.
- Contract Value: \$.685M
- Delivery Method: LBB
- Expected Completion: April 2021

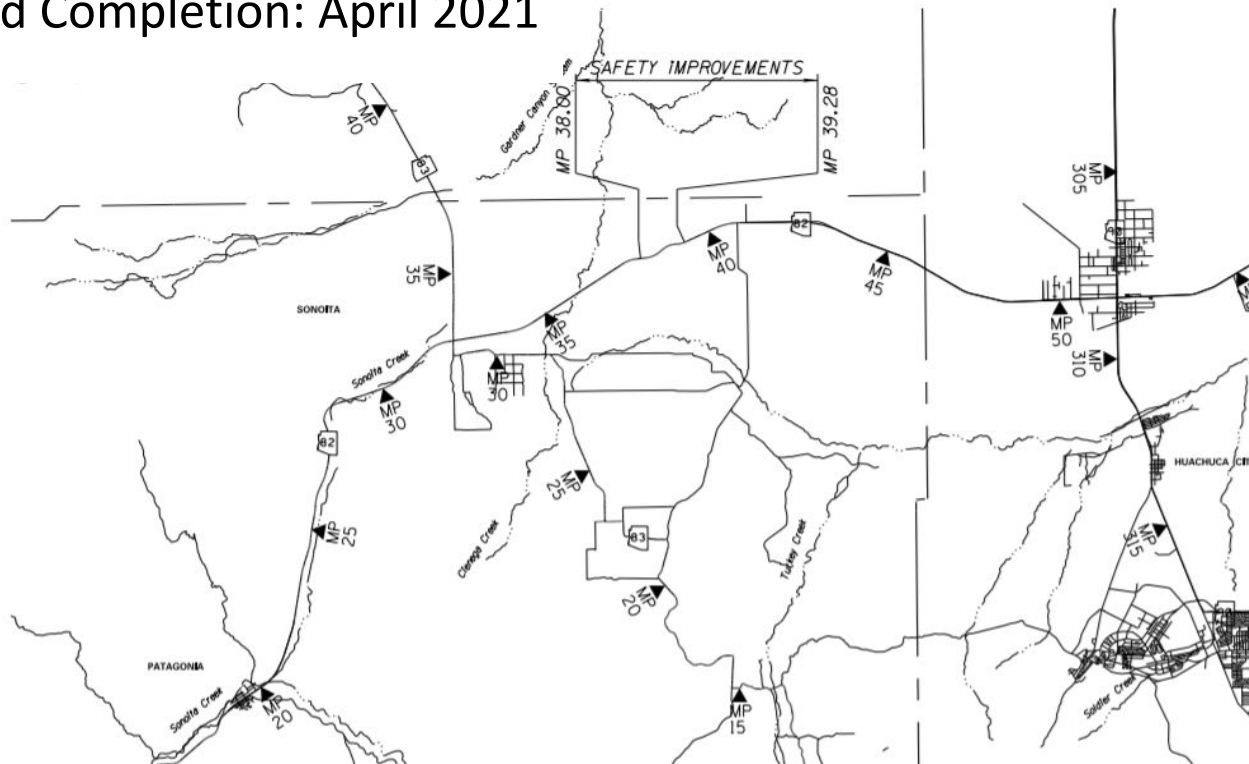

MP 38 – UPPER ELGIN ROAD, SONOITA


PROJECT NO. 082 SC 038 F0202 01C

FEDERAL AID NO. 082-A(207)T

P

- Currently Advertised
- Bid Opening Date: 10/30/2020
- Programmed Amount: \$9.8M
- Delivery Method: LBB
- Expected Completion: Mid 2021

**STATE HIGHWAY
BENSON – STEINS PASS HWY
INTERSTATE 10**

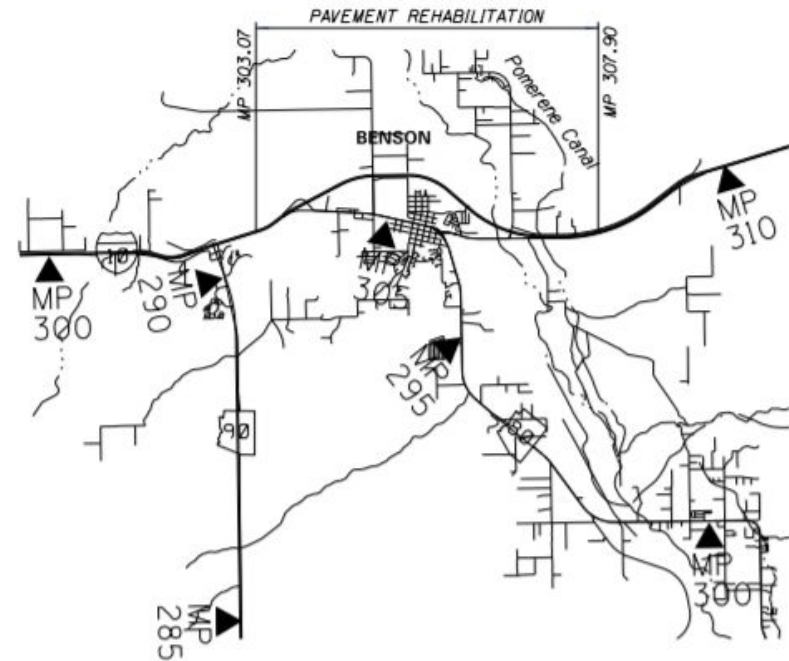

BENSON BYPASS

**PROJECT NO. 010 CH 303 F0205 01 C
FEDERAL AID NO. 010-E(229)T**

P


- Currently Advertised
- Bid Opening Date: 11/20/2020
- Programed Amount: \$40.0M
- Delivery Method: LBB
- Expected Completion: Early 2022

**STATE HIGHWAY
TUCSON-ORACLE JCT-GLOBE HWY
SR 77**



JCT I-10 - RIVER ROAD
PROJECT NO.077 PM 068 F0248 01C
FEDERAL AID NO.077-A(218)T

**STATE HIGHWAY
TUCSON - ORACLE JCT - GLOBE HWY
SR 77**


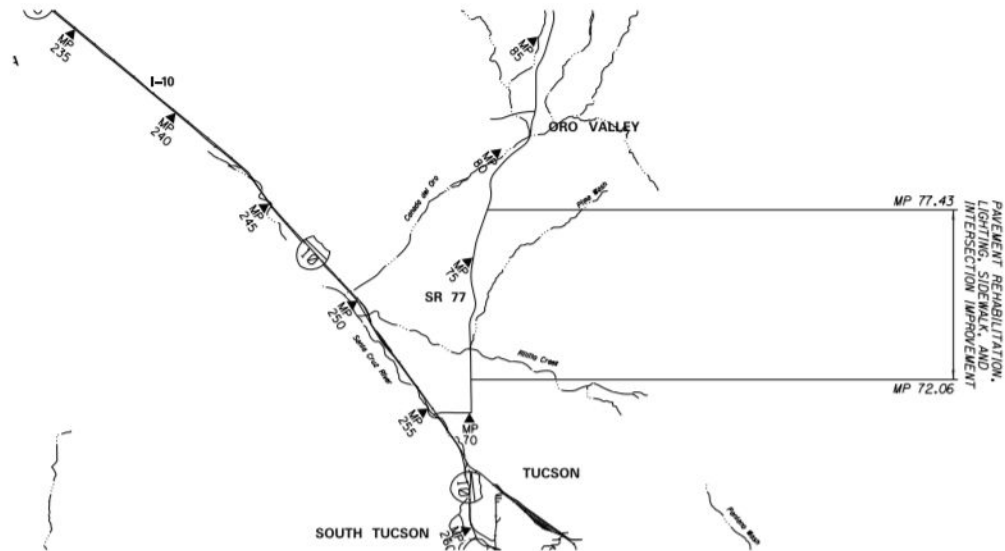


RIVER ROAD TO CALLE CONCORDIA
PROJECT NO.077 PM 072 H8919 01C
FEDERAL AID NO.077-A(215)T

P

SR79 over the Gila River

- Project will use CMAR Delivery method.
- Design Firm, AECOM.
- CMAR, FNF Const.

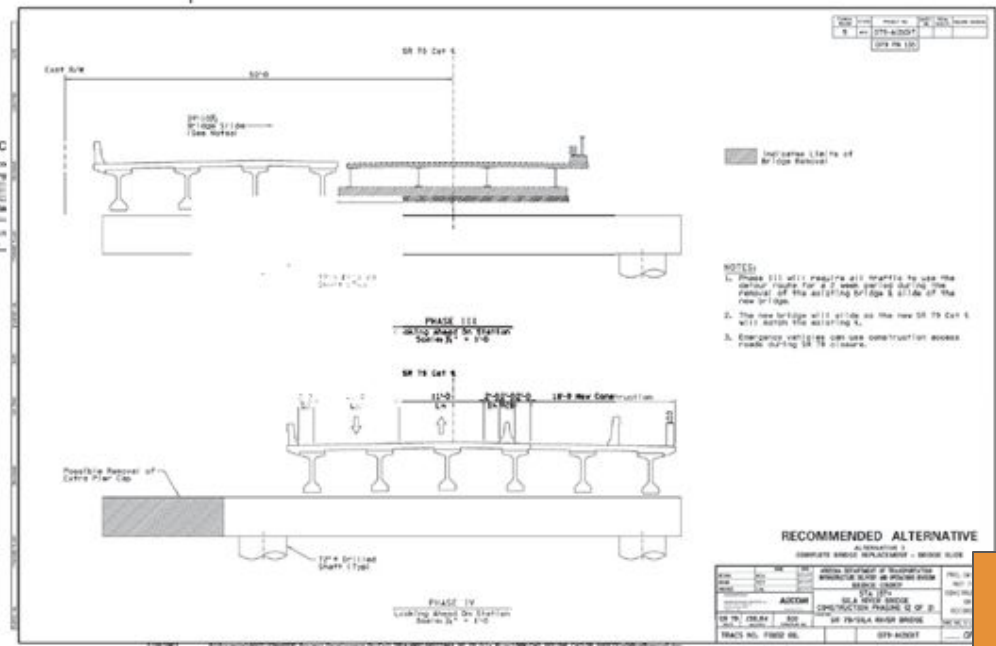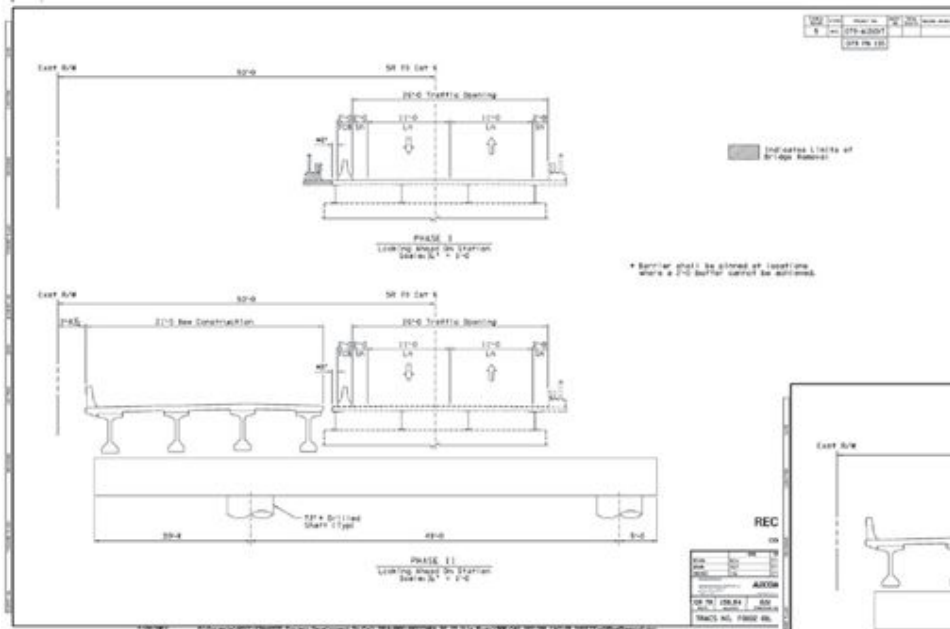

M

Project Name	Location		Contract Time			Project Dollars			Up Coming Activities	Estimated Completion
	Route and Mile Post	Contractor	Contract Time	Time Used	% Compl	Contract \$	\$ Spent	% Spent	(paving, bridge forming, sign installation, other)	(year/month)
I-10 RUTHRAUFF TRAFFIC INTERCHANGE	I10, 252	SUNDT	690	264	38%	\$78,995,365	\$29,116,511	37%	RUTHRAUFF FILLS EAST OF I-10, UPRR GIRDERS, DAVIS RD UNDERPASS	2021/DEC
Santa Cruz County Chip Seal Dirt Roads	SANTA CRUZ COUNTY	EARTH RESOURCES	30	2	7%	\$714,530	\$15,810	2%	CHIP SEAL DIRT ROADS	2020/NOV
I-19 - AJO WAY, PH. II	I19, 62	FNF CONST	715	713	100%	\$31,991,712	\$34,249,396	107%	N/A	2020/MAY
SR-87 Signals	SR-87	Contractors West	240	170	71%	\$1,197,488	\$586,083	49%	install underground for the traffic signals	20-Dec
SR 77 Willow Spgs Rd to Old 77	SR-77	Granite	90	80	89%	\$2,210,477	\$2,130,019	96%		
Peart Rd: Jimmie K-Avendia Ell.	Local	CS Const	135	80	59%	\$113,369	\$71,557	63%		
SR 189, International Border to Grand Ave	SR-189, I-19	AMES/HORROCKS	548	157	29%	\$82,146,114	\$21,398,858	26%	FROM SOUTH END TO LA QUINTA AND INCLUDED THE ROUNDABOUT AT TARGET RANGE RD.	2021/SEPT
I-19/EL TORO RD BRIDGES	MP 45.88	FNF CONST	571	471	82%	\$5,978,331	\$5,456,282	91%	PHASE III SB I-19 BRIDGE DECK UNDER CONSTRUCTION INCLUDING BARRIER AND PAVING THE APPROCHES.	20-Jan
SR 86 - FRESNAL TO MP 123.9	SR 86, 120.5-123.9	GRANITE CONST	440	429	98%	\$13,870,714	\$13,110,709	95%	LANDSCAPE ESTABLISHMENT (in Progress) & PUNCH LIST ITEMS.	2020/OCT
I-10 VAIL RD. TI UP EB 744 MOUNTAIN	I-10,	GRANITE CONST	550	479	87%	\$3,658,776	\$3,751,177	103%	PLACE MOUNTAIN VIEW BARRIER	20-Sep
SR86-MP88 - QUIJOTOA	SR86 88.25-90.37	FALCONE BROTHER'S	105	10	10%	\$1,030,000	\$198,288	19%	INSTALL GUARDRAIL	20-Dec
I-10 HOUGHTON ROAD	274 - 276	AMES CONST	450	0	0%	\$23,427,902	\$0	0%	CLEAR AND GRUB	21-Dec

Questions?

Thank You

rlane@azdot.gov
