

WELCOME TO THE SOUTH CENTRAL DISTRICT Transportation Board Presentation



Presentation by Rod Lane, P.E.
South Central District Engineer
March 16, 2018

I-19 Ajo Traffic Interchange

Contractor: Ames Construction

E

Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
700	746	107%	\$39,973,370	\$39,761,755	99%	2018/March



Ina Road Traffic Interchange

Contractor: Sundt/Kiewit Joint Venture

E

Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
885	396	45%	\$85,628,517	\$39,238,593	46%	2019/JUNE
885	396	45%	\$22,504,912	\$9,899,398	44%	2019/JUNE



SR 86 Kinney to Valencia

Contractor: Ashton

E

Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
917	746	81%	\$40,960,323	\$38,600,145	94%	2018/AUG



I-10 over Wilmot

Contractor: Pulice Construction

M

Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
380	105	28%	\$3,979,255	\$832,746	21%	2018/DEC



I-19 over Pima Mine Rd

Contractor: KE&G Construction

M

Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
385	338	88%	\$4,748,522	\$3,221,960	68%	2018/APRIL




I-19, Canoa Ranch to Duval

Contractor: Ashton

P


Contract Time			Project Dollars			Estimated Completion
Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(year/month)
420	122	29%	\$9,477,799	\$578,299	6%	2018/DEC

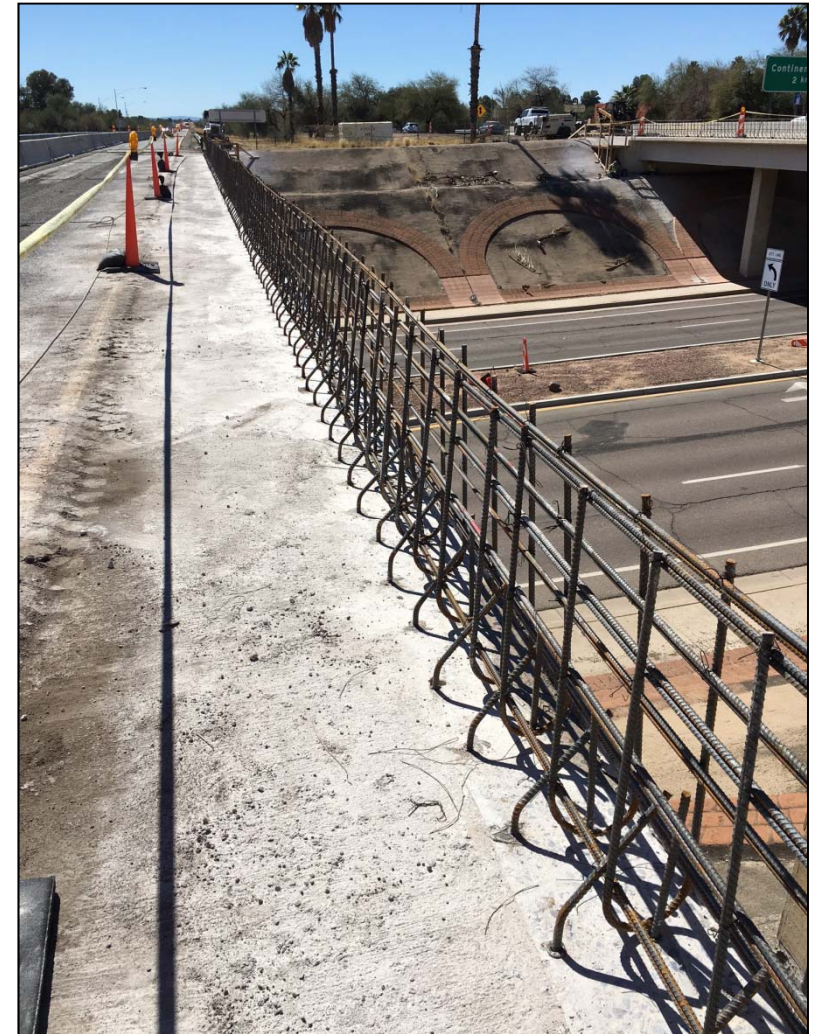


I-10/SR87 in Picacho

- Contractor: Coffman Specialties
- Contract Value: \$58.5M
- Mainline Widening and New T.I.
- New Dust Detection and warning system

E

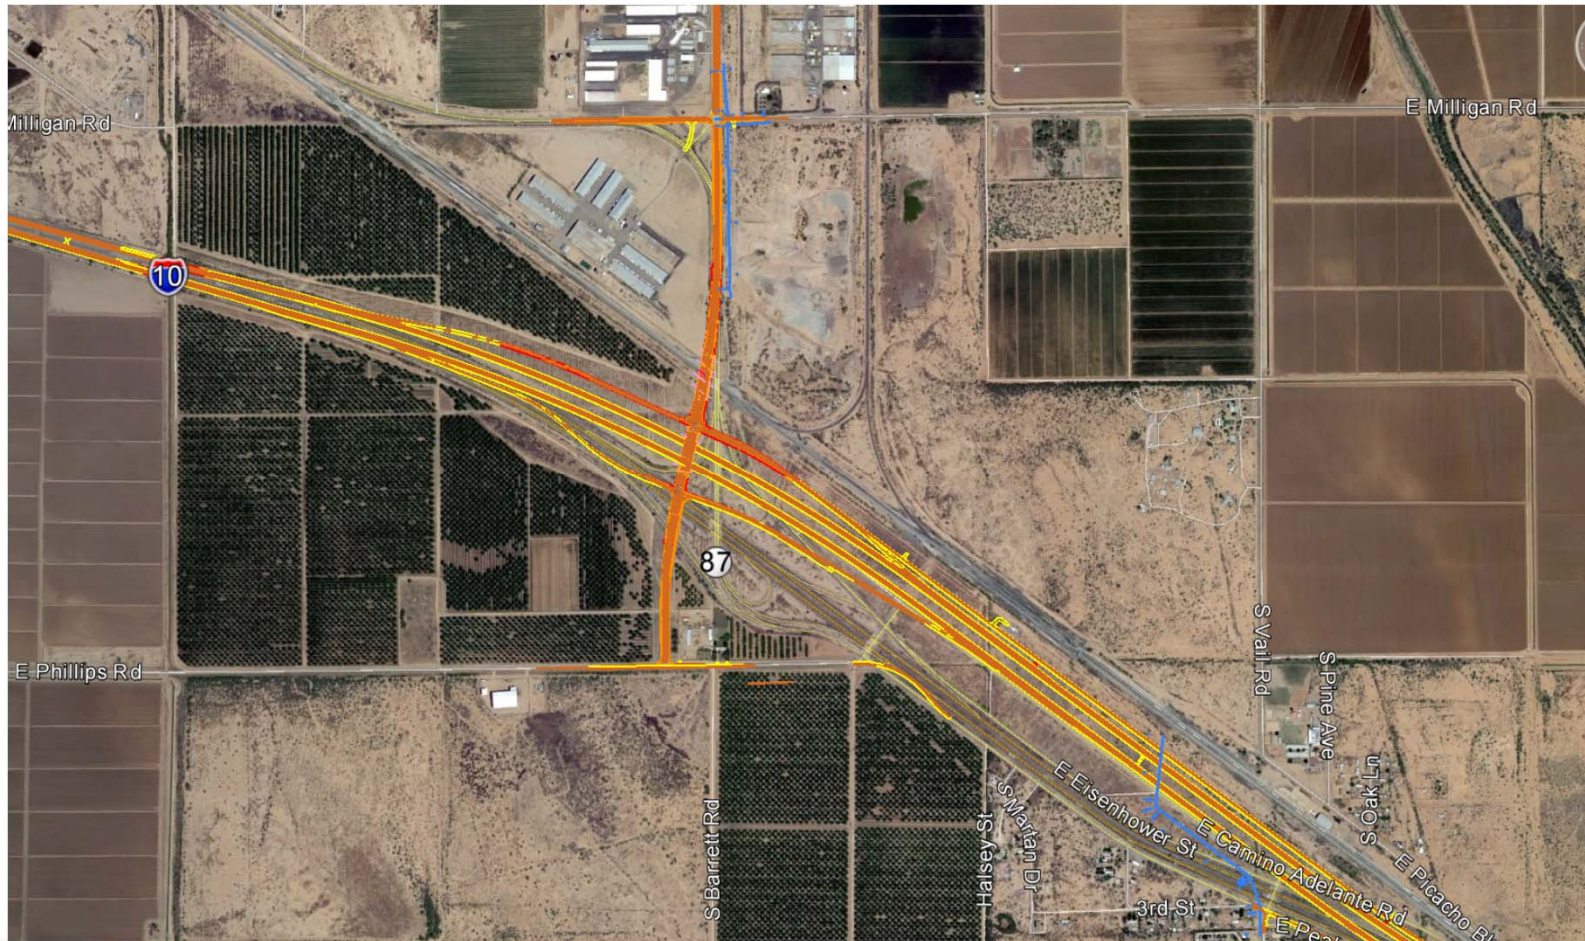

**A+B Contract
bid is 482 days**

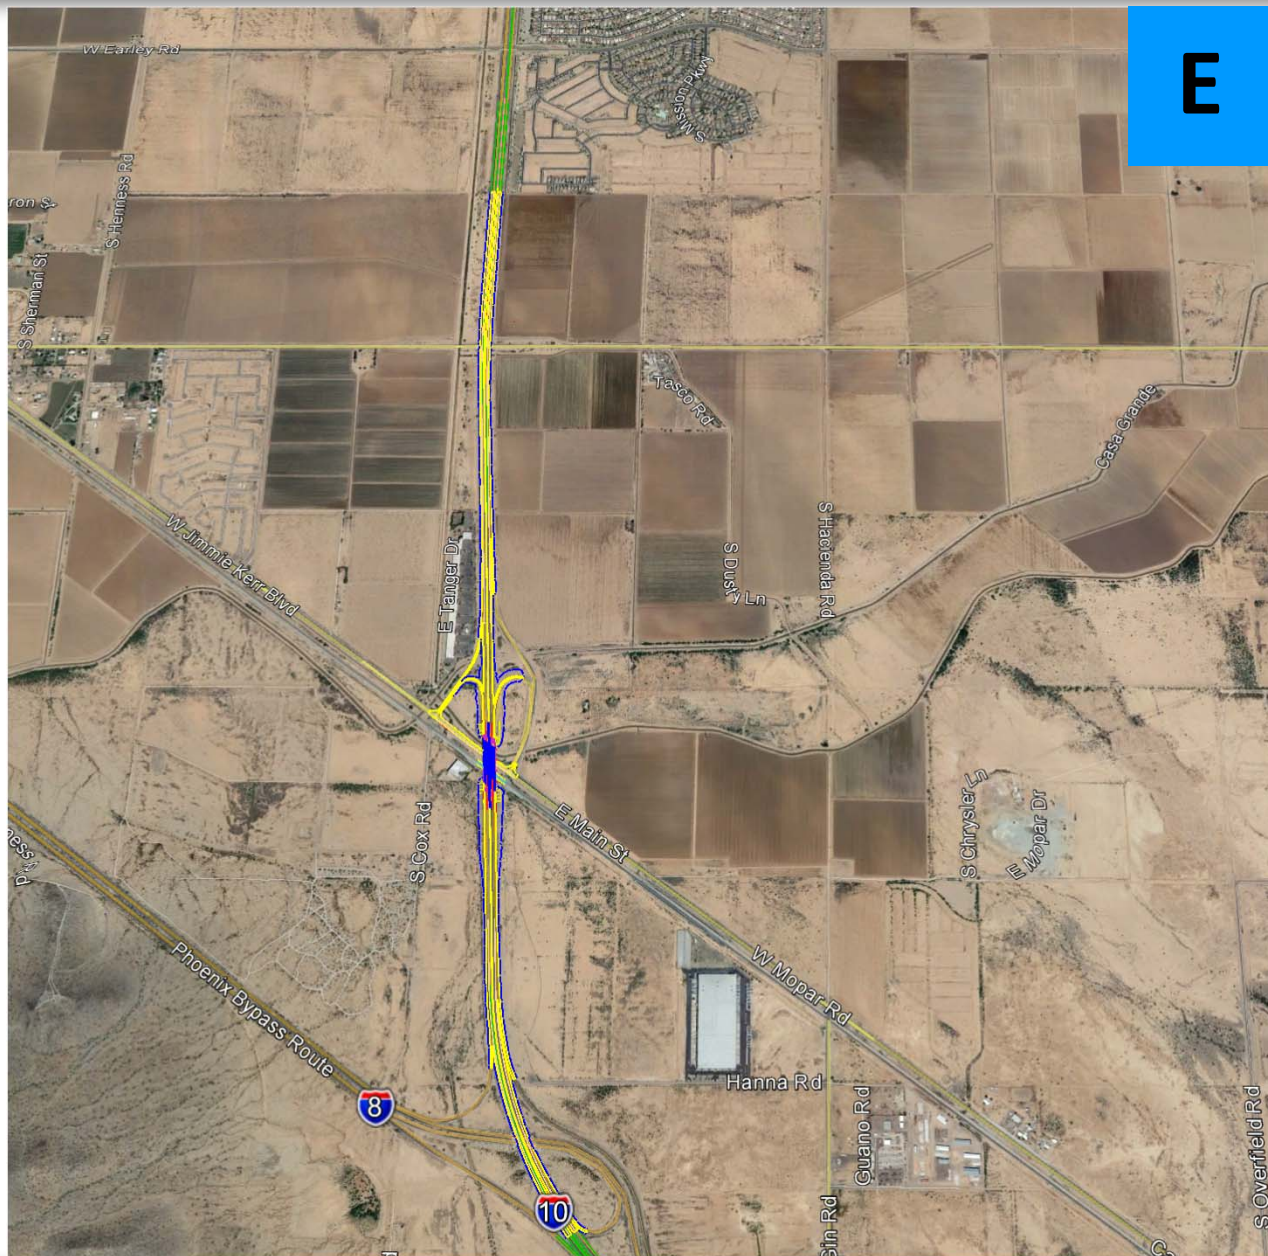

Current Construction

Project Name		Contractor	Location	Contract Time			Project Dollars			Up-Coming Activities	Estimated Completion
			Route and Mile Post	Contract Time Days	Time Used Days	% Complete	Contract \$	\$ Spent	% Spent	(paving, bridge forming, sign installation, other)	(year/month)
H847901C - INA ROAD TI	E	SKJV	I-10, MP 248	885	396	45%	\$85,628,517	\$39,238,593	46%	UPRR BRIDGE GIRDERS, DRAINAGE STRUCTURES, MSE WALLS, PCCP PAVING	2019/JUNE
SB413 - INA ROAD, SILVERBELL TO STARCOMMERCE	E	SKJV	INA ROAD, MARANA	885	396	45%	\$22,504,912	\$9,899,398	44%	GRADING, CURB, GUTTER, SIDEWALK, COLUMNS AND PIER CAPS FOR NEW WB BRIDGE	2019/JUNE
CANOA RANCH TO DUVAL H871601C	P	Ashton	I19, 31.8-42.5	420	122	29%	\$9,477,799	\$0	0%	BRIDGE BARRIER CONSTRUCTION, BRIDGE DECK JOINTS	2018/DEC
H846701C SR 86 AND I-19 TI	E	Ames	SR 86 AND I-19	700	746	107%	\$39,973,370	\$39,761,755	99%	WORKING ON ELECTRICAL AND FMS, FENCEING, AND MEDIAN ISLANDS AND PAINTING	2018/March
H817801C, PIMA MINE ROAD TI	M	KE&G	I-19 AND PIMA MINE ROAD	385	338	88%	\$4,748,522	\$3,221,960	68%	FORM NB I-19 BRIDGE DECK PHASE III AND PLACE REBARPOUR DECK 3/22/18	2018/May
H879101C, TUCSON-ORCLE-GLOBE HWY	P	FNF	OLD TIGER RD-MIGUEL RD	120	88	73%	\$4,319,274	\$3,875,621	90%	PAVING MISCELLANEOUS AC. WINTER SHUT DOWN START NEXT WEEK	2018/APRIL
F013001C/TANGERINE RD FIRST AVE_SR (77)	P	Cactus	FIRST AVE-SR 77	70	13	19%	\$522,772	\$0	0%	WORKING ON ADA RAMPS AND MICRO MILLINGS	2018/May
F006301C, TUCSON - BENSON HWY I-10	M	Pulice	WILMOT TI OP AND EARP WASH	380	105	28%	\$3,979,255	\$832,746	21%	POURING EAST BACK WALL, HAUL IN TEMPORARY BRIDGE	2018/DEC
F002301C, BENSON - STEINS PASS HWY I-10	P	FNF	DRAGOON ROAD TO JOHNSON ROAD	230	106	46%	\$1,635,585	\$710,426	43%	POUR BARRIER WALL - GUARDRAIL	2018/JUL
H821301C, Rest Areas	M	Ashton	I-10, I-91	360	62	17%	\$4,355,955	\$54,073	1%	SACATON RESIDENTIAL - SIDEWALK / CANOA WATERLINE	2018/DEC
H879001C, SR 84	P	Grey Mountain	BURRIS TO FIVE POINT	230	141	61%	\$1,747,683	\$1,728,478	99%	PUNCH LIST - SMOOTHNESS	2018/JUNE
H880301C - E. BUFFALO SOLDIER TRAIL - HATFIELD ST	M	KE&G	SR 90 / MP 316	300	151	50%	\$2,633,000	\$1,208,094	46%	ROADWAY WIDENING, MEDIAN CONSTRUCTION, SIGNAGE, STRIPING	2018/AUG
H680601C - VALENCIA RD - KINNEY RD (SR 86)	E	Ashton	SR 86 / MP 159.0 - 166.6	700	740	106%	\$40,960,323	\$38,600,145	94%	ROADWAY, BANK PROTECTIONS, SEWER, ELECTRICAL, SIDESTREETS, SIGNAGE, STRIPING	2018/AUG

Questions?

Thank You

rlane@azdot.gov
