

Item 6 – State Engineer's Report

August 21, 2020

Summary of Active and Finalized Projects

- **84 projects under construction** **\$935 Million**
 65% Spent - Remaining= **\$324 Million**
- **11 projects finalized in July** **\$35.7 Million**
- **Fiscal Year to date:** **11 projects finalized**

Item 6 – State Engineer's Report

August 21, 2020

Summary of Other Activities

- SR 82 and SR 90 Constituent Inquiry - Crack Seal and “Gators”
- I-17 McGuireville - Re-Striping occurred this week



Item 7 – New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3b	SR 69	\$569,280.75	\$601,236.00	(\$31,955.25)	-5.3%
3c	US 93	\$7,377,460.17	\$6,725,508.00	\$651,952.17	9.7%
3d	SR 95	\$1,748,305.00	\$1,696,064.40	\$52,240.60	3.1%
3e	SR 95	\$533,976.26	\$582,344.95	(\$48,368.69)	-8.3%
3f	US 191	\$2,522,954.46	\$2,393,433.00	\$129,521.46	5.4%
3g	SR 95	\$980,000.00	\$1,123,040.00	(\$143,040.00)	-12.7%
3h	Local	\$714,530.00	\$676,514.60	\$38,015.40	5.6%
7a	US 89	\$892,802.89	\$704,612.90	\$188,189.99	26.7%
7b	Local	\$1,273,127.10	\$1,160,053.00	\$113,074.10	9.7%
7c*	Local	\$615,289.48	\$525,516.18	\$89,773.30	17.1%
7d	Local	\$522,600.32	\$629,670.00	(\$107,069.68)	-17.0%
TOTAL THIS MONTH		\$17,135,036.95	\$16,292,476.85	\$842,560.10	5.2%
TOTAL FY TO DATE		\$29,468,970.06	\$31,504,758.91	(\$2,035,788.85)	-6.5%


*Item 7c is "Postpone" and is not included in the totals.

Low Bid	\$892,803
State Estimate	\$704,613
Difference	\$188,190
% Difference	26.7%

Recommendation: Award

Reason for Difference:

- Remove Lead-Based Striping
- Roadway Excavation
- Aggregate Base
- Cover Material
- Mobilization

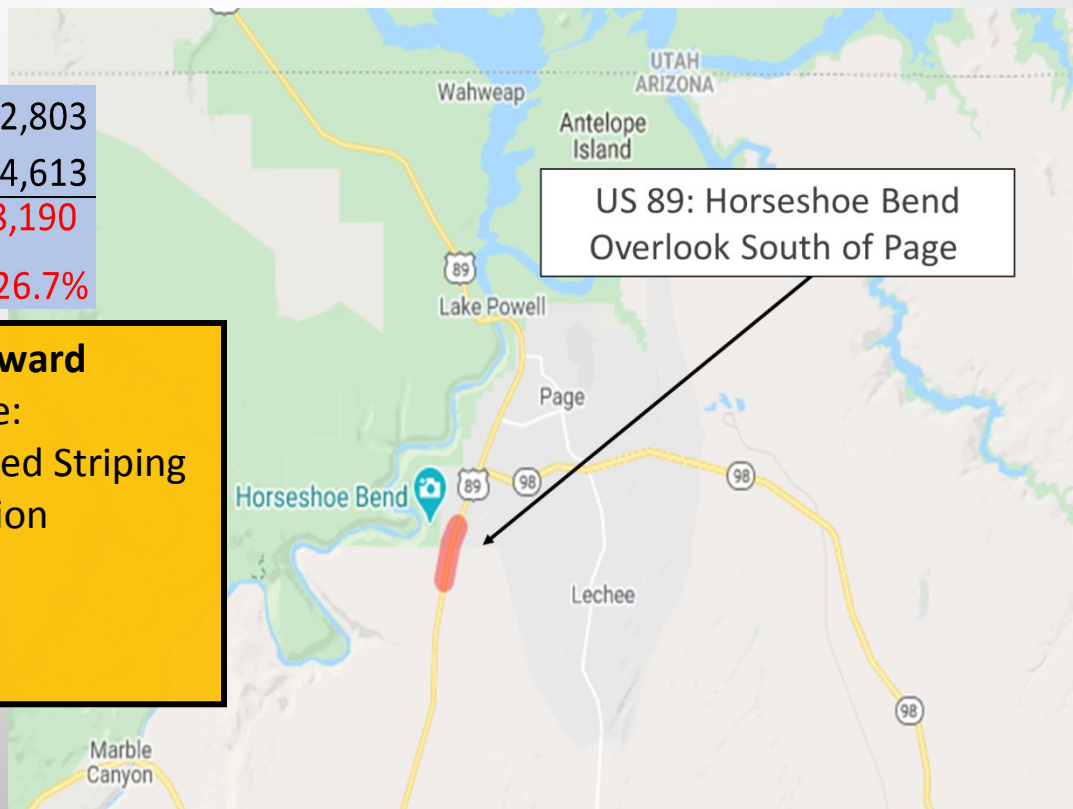


Low Bid	\$1,273,127
State Estimate	\$1,160,053
Difference	\$113,074
% Difference	9.7%

Recommendation: Award

Reason for Difference:

- Remove Lead-Based Paint
- Asphaltic Concrete
- Bridge Containment System

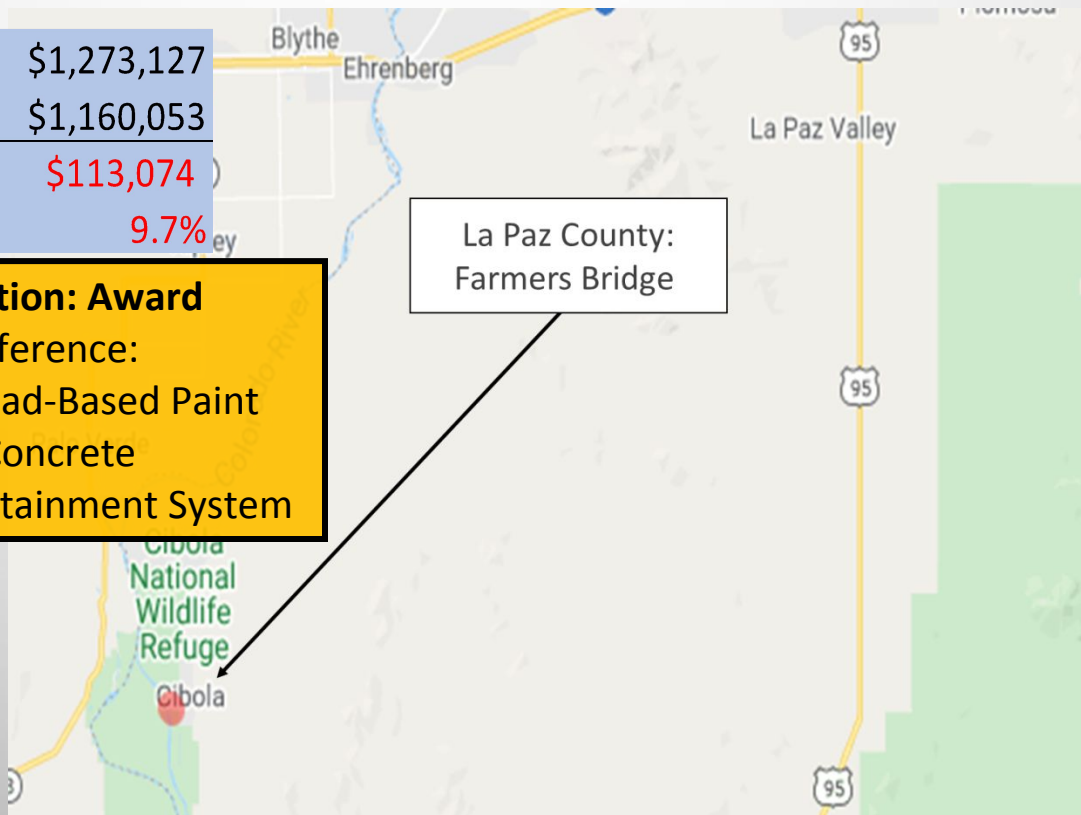

Low Bid	\$615,289
State Estimate	\$525,516
Difference	\$89,773
% Difference	17.1%

Recommendation: Postpone

Reason for Difference:

- Conductor
- Video Detection System
- Temporary Traffic Signal
- Mobilization



City of Kingman:
Stockton Hill Road

Low Bid	\$522,600
State Estimate	\$629,670
Difference	(\$107,070)
% Difference	-17.0%

Recommendation: Award
Reason for Difference:

- Rumble Strip

