

Arizona State Transportation Board Meeting

District Report - Southeast District

Todd Emery

September 18, 2026


Current Construction Projects

North of Florence to Queen Valley
SR 79, MP 140 to MP 148
Contractor: SEMA Construction, Inc.
18% Complete, 17% Time Spent

Queen Creek Bridge
US 60, MP 227.7
Contractor: Ames Construction, Inc.
62% Complete, 59% Time Spent

Waterfall Canyon Bridge
US 60, MP 229.5
Contractor: Ames Construction, Inc.
78% Complete, 59% Time Spent

MP 256.5 to Old San Carlos Rd
US 70, MP 256.5 to MP 259.4
Contractor: Show Low Construction, Inc.
70% Complete, 38% Time Spent

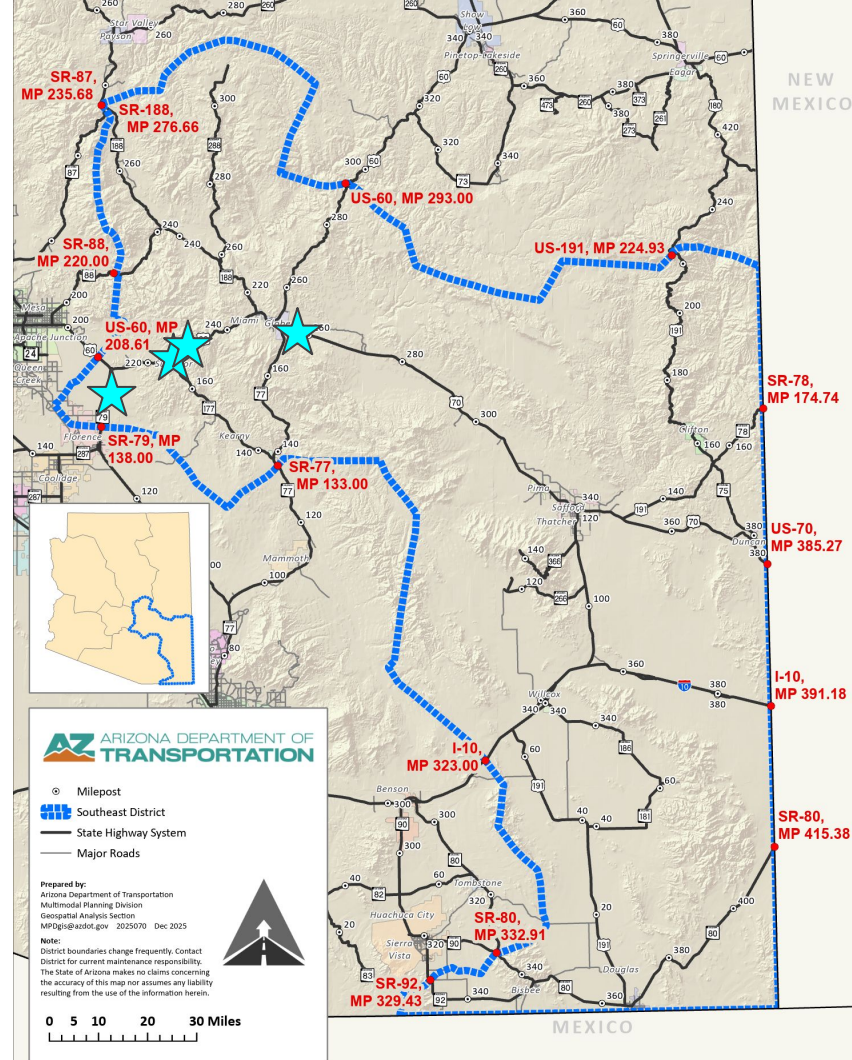

US 60, Queen Creek Bridge



US 60, Waterfall Canyon Bridge



Current Construction Projects

Cottonwood Wash to Reay Lane

US 70, MP 330 to MP 335

Contractor: W. W. Clyde & CO.

0% Complete, 0% Time Spent

US 70 to MP 134

US 191, MP 132 to MP 134

Contractor: Show Low Construction, Inc.

21% Complete, 15% Time Spent

Jct SB I-10 to MP 356.49

I-10, MP 345.5 to MP 356.49

Contractor: FNF Construction, Inc.


98% Complete, 51% Time Spent

Cochise Railroad Overpass

US 191, MP 62.5 to MP 63.2

Contractor: SEMA Construction, Inc.

13% Complete, 32% Time Spent

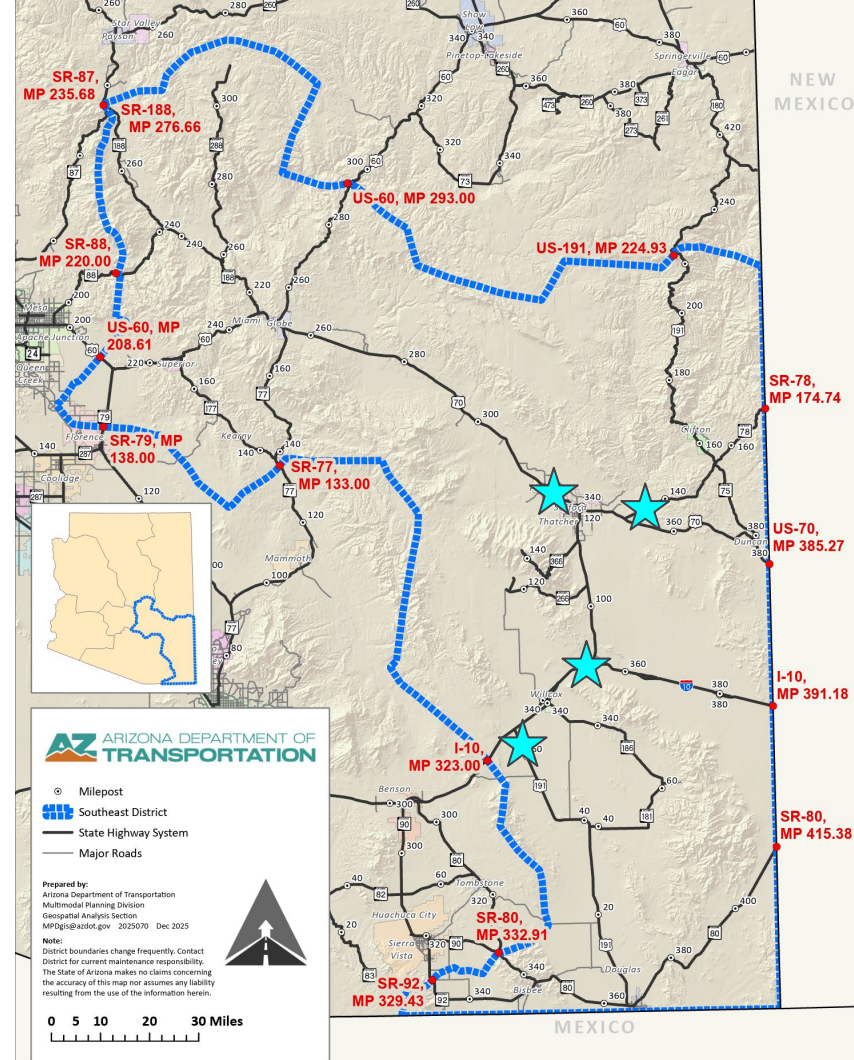

Current Construction Projects

White Mountain Ave (San Carlos Apache Tribe)

Contractor: Show Low Construction, Inc.

56% Complete, 37% Time Spent

Moon Canyon Bridge (City of Bisbee)


Contractor: CS Construction, Inc.

55% Complete, 96% Time Spent

Chino Rd Extension Phase 2 (City of Douglas)

Contractor: ISX Construction, LLC.

30% Complete, 55% Time Spent

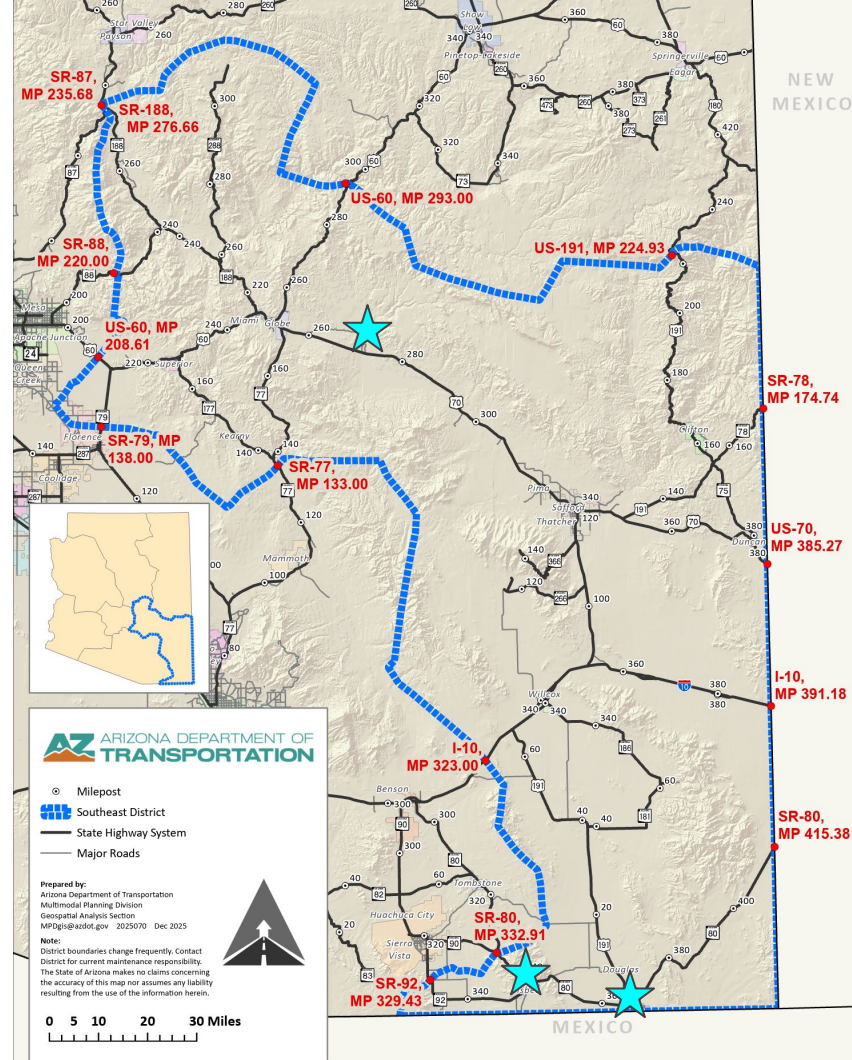

US 70, County Rd 220 to Yellowjacket Rd



US 70, Medicine Way Rd to MP 275.7



Thank You Questions?
