


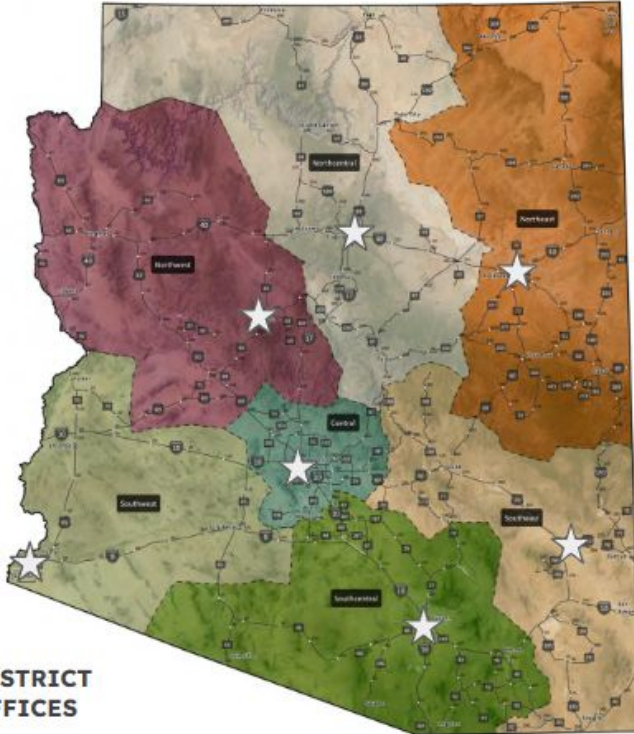

★ **DISTRICT
OFFICES**

State Engineer's Report September 2026

Summary of Active and Finalized Projects

117 Projects Under Construction

\$3.4 Billion

6 Projects Finalized in September


\$248.1 Million

Fiscal Year to Date

17 Projects Finalized



★ **DISTRICT OFFICE**

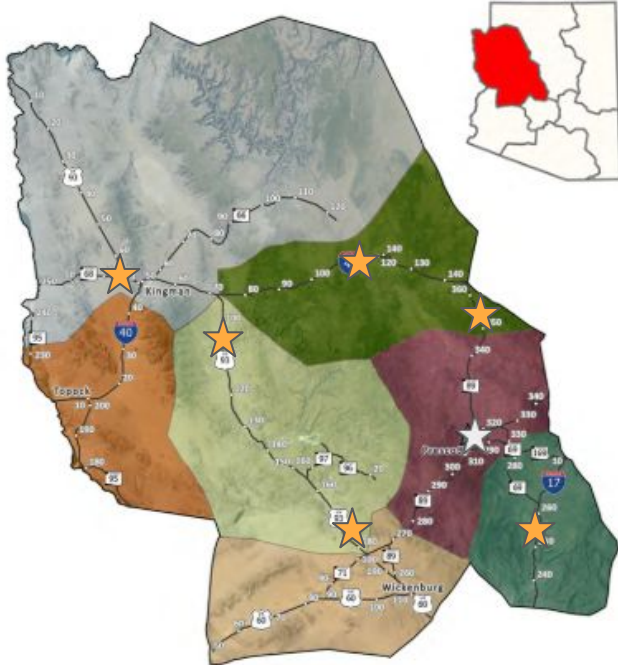

South of Date Creek

US 93, MP 175.5 - MP 177.0

Contractor: Fann Contracting, Inc.

31% Complete, 26% Time Spent

I-40/US 93 West Kingman TI

I-40, MP 48.87 - MP 51.56

Contractor: Fisher Sand & Gravel Co.

82% Complete, 89% Time Spent

Cane Springs

US 93, MP 105.99 - MP 109.42

Contractor: FNF Construction, Inc.

91% Complete, 76% Time Spent

Markham Wash to Seligman (EB)



I-40, MP 107.7 - MP 122.7

Contractor: Fann Contracting, Inc.

54% Complete, 33% Time Spent

North of Drake

SR 89, MP 353.67 to MP 354.62

Contractor: Earth Resources Corporation

18% Complete, 34% Time Spent


Sunset Point to SR 69



I-17, MP 252 to MP 262

Contractor: Asphalt Paving & Supply, Inc.

74% Complete, 60% Time Spent

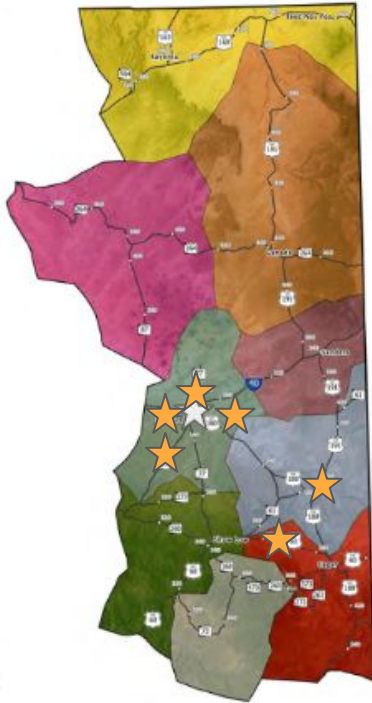

US 180 Apache Dr to MP 407

US 180 MP 402.7 - MP 407.0

Contractor: VSS International, Inc.

98% Complete, 72% Time Spent



Perkins Valley TI

I-40, MP 283.0

Contractor: SEMA Construction, Inc.

64% Complete, 61% Time Spent

SR 260 Linden to Show Low

SR 260, MP 331.9 - MP 340.06

Contractor: Combs Construction Company, LLC.

104% Complete, 74% Time Spent



MP 8 to Phoenix Park Wash

SR 377, MP 8 - MP 13

Contractor: SEMA Construction, Inc.

39% Complete, 91% Time Spent



24th West to US 191

US 180, MP 366.92 to MP 368.93

Contractor: WW Clyde & Co

53% Complete, 91% Time Spent




**Little Colorado River & Five Mile Wash
Bridges**

US 180, MP 309.05 to MP 310.6

Contractor: Vastco, Inc

2% Complete, 5% Time Spent

★ **DISTRICT OFFICE**

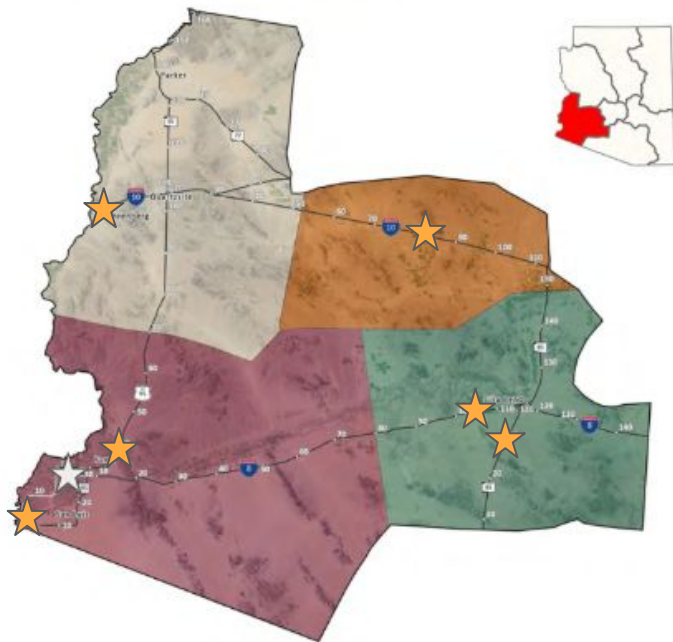

US 95, Imperial Dam Road-Aberdeen Road

US 95, MP 43.40-55

Contractor: Fisher Sand & Gravel, Co.

49% Complete, 50% Time Spent

SR 85 South, Qilotosa Wash-Thayer Road

SR 85S, MP 4.39-6.02

Contractor: J. Banicki Construction, Inc.

8% Complete, 16% Time Spent

I-10, Burnt Well Rest Area Truck Parking

I-10, MP 86

Contractor: Rummel Construction, Inc.

0% Complete, 0% Time Spent

I-8 & I-10 DMS & Queue Warning System

I-8, MP 100.7-112.7 & I-10, MP 0.5-6.4 & 20.9

Contractor: C S Construction, Inc.

3% Complete, 0% Time Spent

I-10 CA Border-Dome Rock Road Pavement Preservation

I-10, MP 0-11.71

Contractor: FNF Construction, Inc.

0% Complete, 0% Time Spent

Cesar Chavez Boulevard

City of San Luis

Contractor: DPE Construction, Inc.

22% Complete, 30% Time Spent


County 11th Street & Avenue G

Yuma County

Contractor: DPE Construction, Inc.

99% Complete, 89% Time Spent

★ **DISTRICT OFFICE**

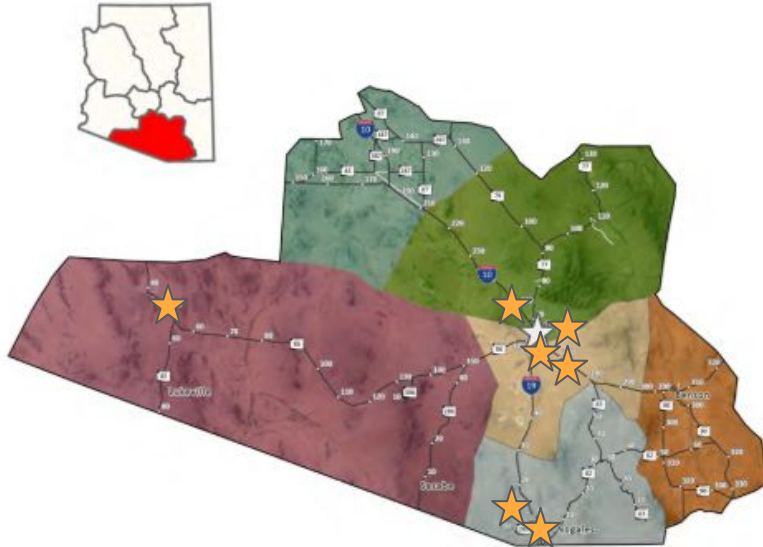

Elota Avenue

SR 85, MP 42.40 - MP 60

Contractor: Granite Construction

26% Complete, 49% Time Spent

Kino to Country Club (DB)

I-10, MP 262 - MP 264.5

Design Builder: Sundt/Jacobs

70% Complete, 43% Time Spent

Irvington Road TI

I-19, MP 60.83

Contractor: AMES Construction

8% Complete, 13% Time Spent

Amole Railroad Overpass

I-10, MP 292

Contractor: Granite Construction

113% Complete, 119% Time Spent

Western Avenue TI

I-19, MP 0.94 - MP 1.26

Contractor: Granite Construction


94% Complete, 162% Time Spent

Pena Blanca Lake

SR 289, MP 0 - MP 10.83

Contractor: Granite Construction

94% Complete, 92% Time Spent

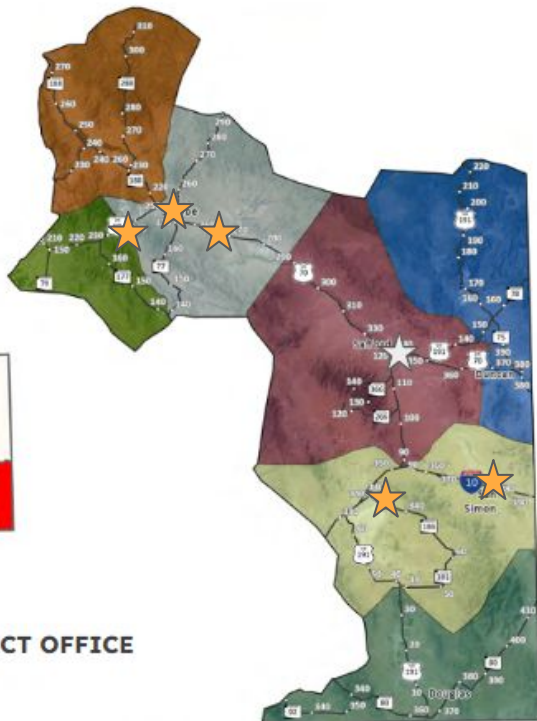

★ DISTRICT OFFICE

North of Florence to Queen Valley

SR 79, MP 140 - MP 148

Contractor: SEMA Construction, Inc.

28% Complete, 24% Time Spent

Queen Creek Bridge

US 60, MP 227 - MP 228

Contractor: Ames Construction, Inc.

73% Complete, 60% Time Spent

US 70 to MP 134

US 191, MP 132 - MP 134

Contractor: Show Low Construction, Inc.

38% Complete, 25% Time Spent

Jct SB I-10 to MP 356.49

I-10, MP 345.5 - MP 356.49

Contractor: FNF Construction, Inc.


99% Complete, 58% Time Spent

Cochise Railroad Overpass

US 191, MP 62.5 - MP 63.2

Contractor: SEMA Construction, Inc.

14% Complete, 35% Time Spent

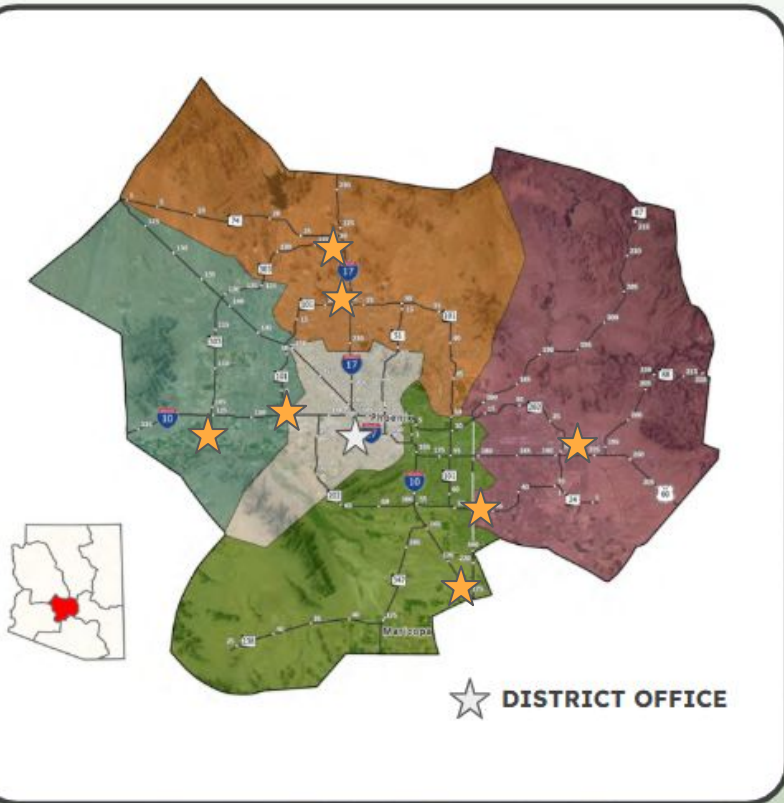

I-17/SR303 to 51st Ave

New system ramps and widening in Phoenix
MP 136.6 - MP 139
Contractor: Pulice Construction, Inc.
28% Complete, 37% Time Spent



SR101 I-17 to 75th Ave

Loop 101 Expansion in Phoenix/Glendale
MP 16.53 - MP 25.1
Contractor: Coffman Specialties, Inc.
82% Complete, 94% Time Spent

I-10 Gila River Bridge

Bridge Replacement
MP 161.00 - MP 172.80
Contractor: Pulice Construction, Inc.
99% Complete, 99% Time Spent



I-10/SR101

New DHOV Ramp
MP 1.19 - MP 3.87
Contractor: FNF Construction, Inc.
13% Complete, 21% Time Spent

SR202 Val Vista to SR101L

Loop 202 Expansion in Chandler/Gilbert
MP 40.8 - MP 50.60
Contractor: Sundt Construction, Inc. (JV) C S Construction, Inc.
86% Complete, 95% Time Spent



SR303 MC85 to Van Buren

New Freeway
MP 99.14 - MP 103.23
Contractor: Pulice Construction, Inc.
10% Complete, 7% Time Spent

ITEM 8 - New Construction Contracts

ITEM	HIGHWAY	LOW BID	DEPARTMENT ESTIMATE	DIFFERENCE	PERCENT
3h	I 40	\$860,106.49	\$831,400.00	\$28,706.49	3.5%
3i	I 40	\$1,316,995.00	\$1,423,145.00	-\$106,150.00	-7.5%
3j	I 10	\$2,887,280.61	\$2,699,793.55	\$187,487.06	6.9%
8a	I 10	\$654,116.20	\$927,150.00	-\$273,033.80	-29.4%
TOTAL THIS MONTH		\$5,718,498.30	\$5,881,488.55	-\$162,990.25	-2.8%
TOTAL FY TO DATE		\$149,237,950.30	\$175,773,305.55	-\$26,535,355.25	-15.1%

Monthly Totals for Construction Contracts

MONTH	NO. OF BIDS	AWARDS	LOW BID	DEPARTMENT ESTIMATE	DIFFERENCE	PERCENT
Jul-26	3	2	\$4,844,007.00	\$6,183,254.00	-\$1,339,247.00	-21.7%
Aug-26	10	10	\$80,742,878.00	\$91,622,349.00	-\$10,879,471.00	-11.9%
Sep-26	10	11	\$57,932,567.00	\$72,086,214.00	-\$14,153,647.00	-19.6%
Oct-26	4	4	\$5,718,498.30	\$5,881,488.55	-\$162,990.25	-2.8%
Fiscal YTD	27	27	\$149,237,950.30	\$175,773,305.55	-\$26,535,355.25	-15.1%

District 1

CCTV INSTALLATION
I-10: I 10; SR 51 ; SR 202
F076501C

ITEM 8a

Low Bid	\$654,116
Department Estimate	\$927,150
Difference	-\$273,034
% Difference	-29.4%

Recommendation: AWARD

Reasons for Difference:

- Maintenance of Traffic
- Contractor Owned Equipment
- Mobilization



ITEMS
3h-3j

CONSENT AGENDA ITEMS

District 5

CMAR PROJECT : GMP 1
I 40: METEOR CRATER REST AREA
F077501X

ITEM 3h

Low Bid	\$860,106
Department Estimate	\$831,400
Difference	\$28,706
% Difference	3.5%

Recommendation: AWARD



METEOR CRATER REST AREA
FRAGSTAFF - HOOBROOK HIGHWAY(I-40)
040 CN 235 F0nnS 01 C
040-D(253) T

District 6


SAFETY IMPROVEMENTS

I 40: I 40 AT MP 75.09 & SR 89 AT MP 363.39

F070301C

Low Bid	\$1,316,995
Department Estimate	\$1,423,145
Difference	-\$106,150
% Difference	-7.5%

Recommendation: AWARD

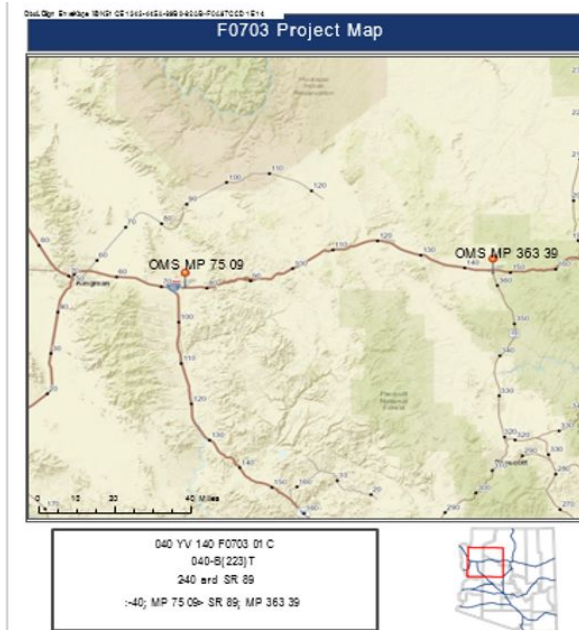

District 1

**CMAR PROJECT: GMP 1
I 10: SR 85 - CITRUS ROAD
F066001C**

ITEM 3j

Low Bid	\$2,887,281
Department Estimate	\$2,699,794
Difference	\$187,487
% Difference	6.9%

Recommendation: AWARD



SR 85 TO CITRUS ROAD
EHRENBURG-PHOENIX HIGHWAY (I-10)
W1W1M A 113 PW68V WIC
W1W1B(223) T
