

Arizona State Transportation Board South Central District Update




Presentation by Rod Lane
South Central District Engineer
December 18, 2020

I-19, El Toro Rd Bridge

- Contractor: FNF Const
- Contract Value: \$6M
- Delivery Method: DBB
- Expected Completion: Early 2021


Unit 4593 On-Time Project Delivery

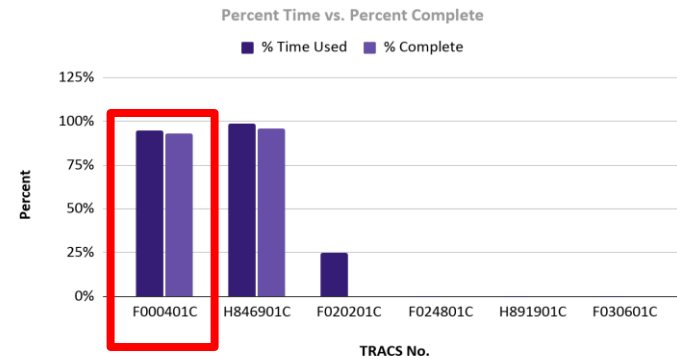

M

SR 189: International Border to Grand Avenue


- Design Build Team: Ames/Horrocks
- Contract Value: \$82M
- Delivery Method: Design Build
- ADOT's GEC: AECOM
- Expected Completion: End of 2021

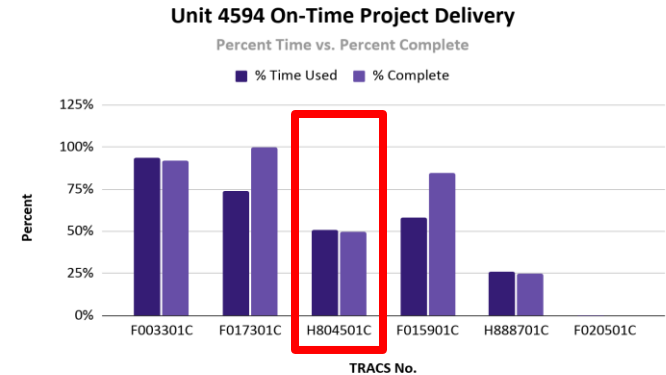

E

I-10/Ruthrauff Rd T.I.

- Contractor: Sundt Const.
- Contract Value: \$80M
- Delivery Method: DBB, A+B
- Expected Completion: End of 2021
- New Diamond interchange with bridge over UPRR and Highway Drive.

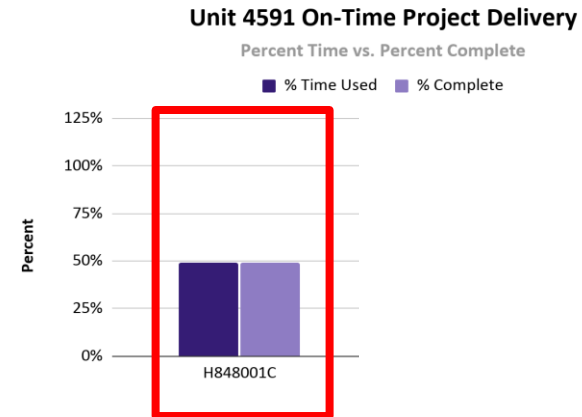


E

I-10/Houghton Rd T.I.

- Contractor: Ames Const
- Contract Value: \$23.4M
- Delivery Method: DBB
- Expected Completion: Late 2021

Unit 4594 On-Time Project Delivery

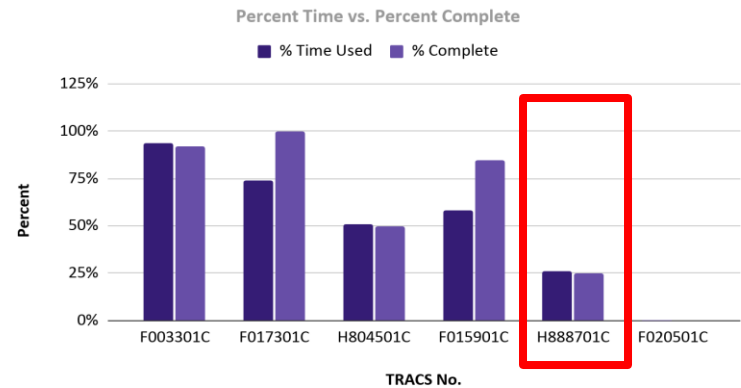



E

I-19: Tubac to West Arivaca Rd

- Contractor: Fisher Sand and Gravel
- Contract Value: \$17.26M
- Delivery Method: DBB
- Expected Completion: Late 2021

Unit 4592 On-Time Project Delivery



Percent Time vs. Percent Complete

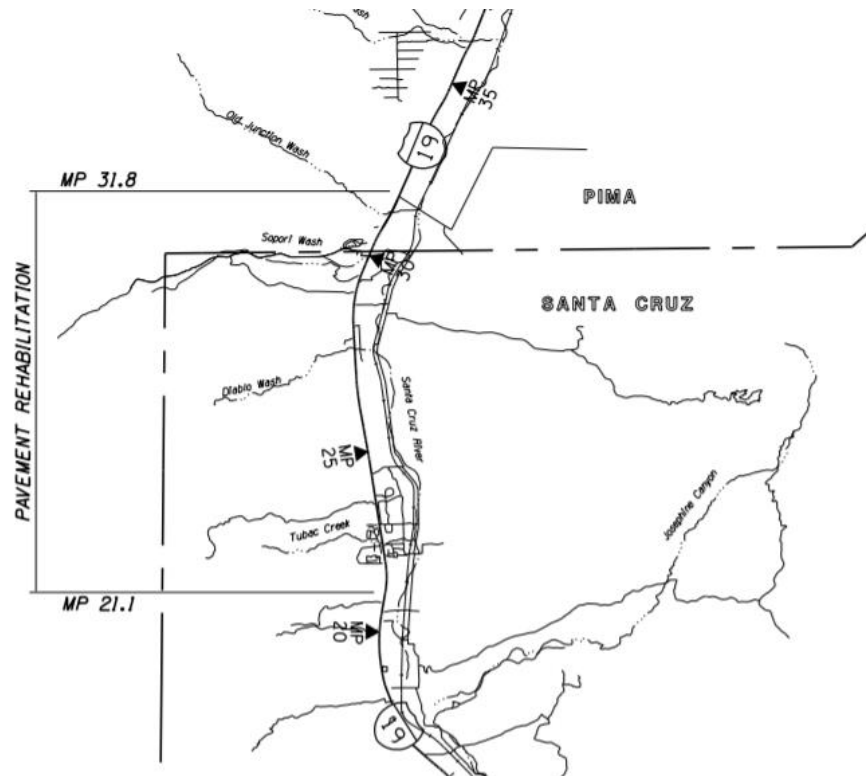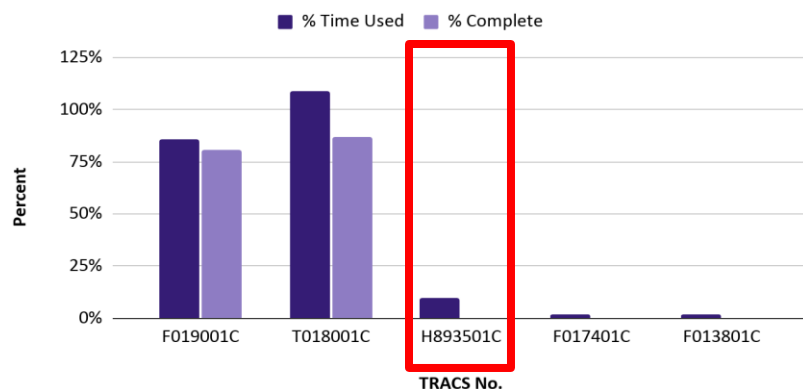

I-19/Sahuarita Rd: Deck Rehab

I-19 MP 42.5 - MP 50.3: Pvmnt Pres

- Contractor: Fisher Sand and Gravel
- Contract Value: \$13.12M
- Delivery Method: DBB
- Expected Completion: Early 2022

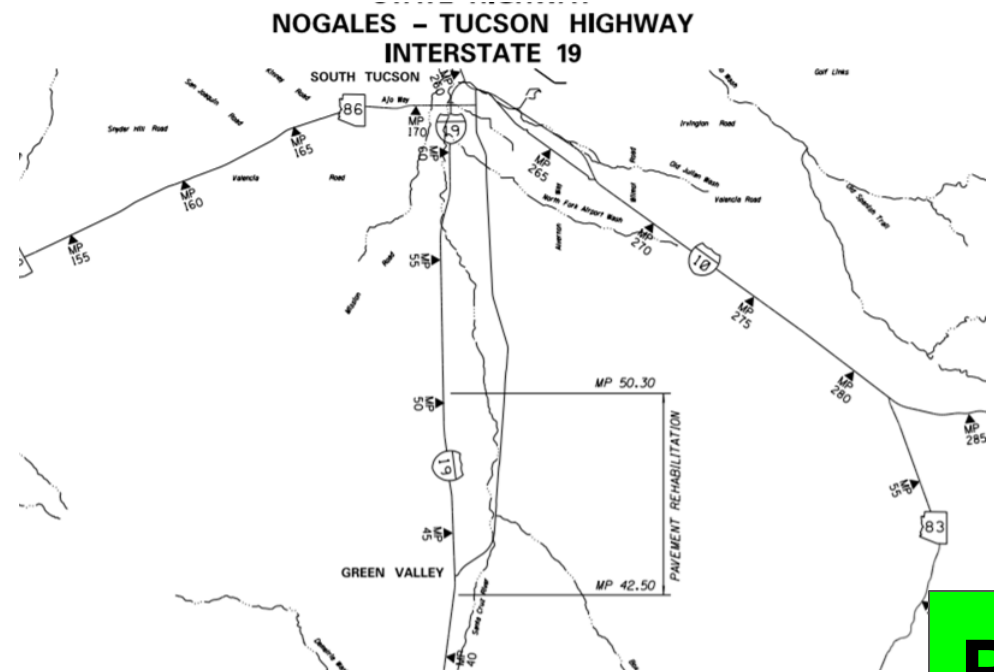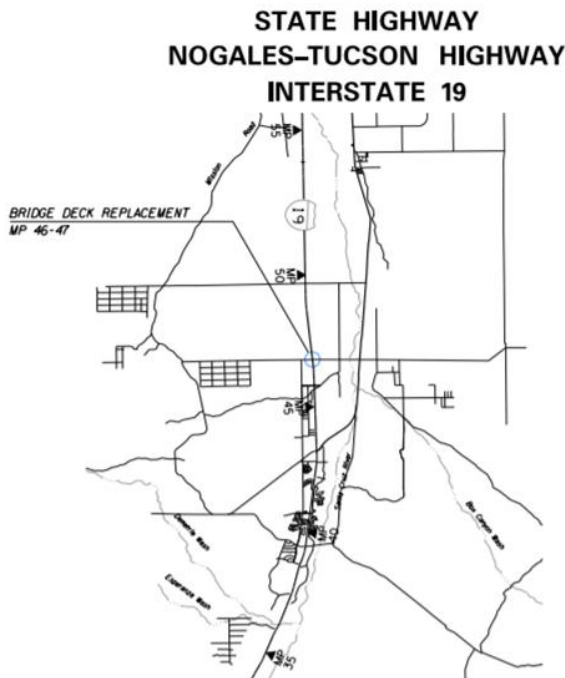

P

Upcoming Projects we hope to see soon


- Programed Amount: \$40.0M
- Delivery Method: DBB
- Expected Completion: Early 2022

STATE HIGHWAY
TUCSON-ORACLE JCT-GLOBE HWY
SR 77



JCT I-10 – RIVER ROAD
PROJECT NO. 077 PM 068 F0248 01C
FEDERAL AID NO. 077-A(218)T

STATE HIGHWAY
TUCSON – ORACLE JCT – GLOBE HWY
SR 77

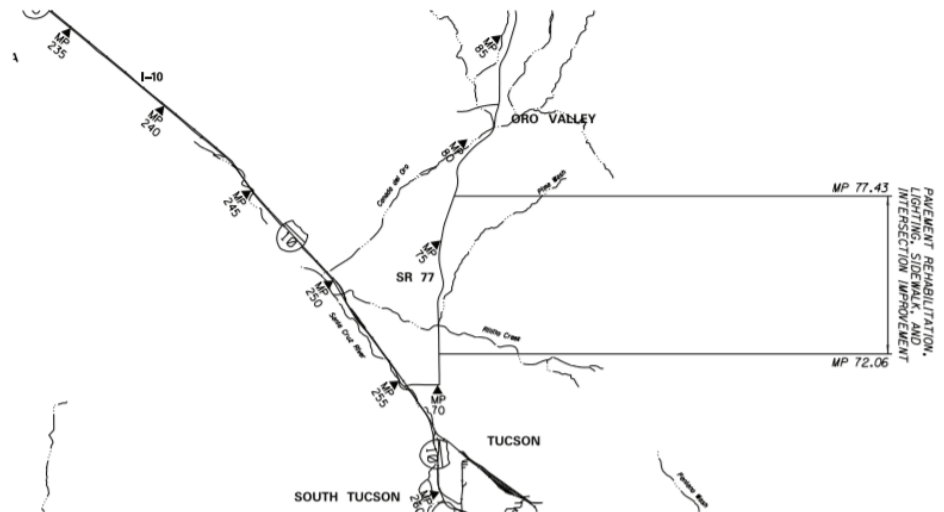

RIVER ROAD TO CALLE CONCORDIA
PROJECT NO. 077 PM 072 H8919 01C
FEDERAL AID NO. 077-A(215)T

P

Project Name	Location		Contract Time			Project Dollars			Up-Coming Activities	Estimated Completion
	Route and Mile Post	Contractor	Contract Time	Time Used	% Comp	Contract \$	\$ Spent	% Spent	(paving, bridge forming, sign installation, other)	(year/month)
I-10 RUTHRAUFF TRAFFIC INTERCHANGE	I10, 252	SUNDT	690	320	46%	\$78,995,365	\$38,300,081	48%	WB I-10 DEMO, WB EARTHWORK, UPRR BRIDGE DECK, MSE WALL ON RUTHRAUFF, DAVIS ROAD UNDERPASS	2021/DEC
CITY OF ELOY - JIMMIE KERR BLVD Rumble Strips & Warning Lights	JIMMIE KERR BLVD	AJP ELECTRIC	180	0	0%	\$288,239	\$0	0%	PARTNERING, PRECONSTRUCTION, SUBMITTALS	2021/JUNE
SR-87 Signals	SR-87	Contractors West	240	205	85%	\$1,197,488	\$860,572	72%	install underground for the traffic signals	2020/Dec
Pearl Rd: Earley Rd. & Upland Trail TI Rumblestrips, Illumination	Local	CS Const	135	115	85%	\$113,369	\$98,527	87%		
SR 189, International Border to Grand Ave	SR-189, I-19	AMES/HORROCKS	548	266	49%	\$82,146,114	\$40,797,308	50%	DRILLED SHAFTS, COLUMNS, AND PIER CAPS FOR COMBO BRIDGE.	2021/SEPT
I-19/EL TORO RD BRIDGES	MP 45.88	FNF CONST	571	534	94%	\$5,978,331	\$6,202,903	104%	UPRR FENCE UNDER CONSTRUCTION, PAINTING BRIDGES & PATCHING BARRIERS .	20-Jan
SR 86 - FRESNAL TO MP 123.9	SR 86, 120.5-123.9	GRANITE CONST	440	435	99%	\$13,870,714	\$13,165,779	95%	LANDSCAPE ESTABLISHMENT - ENDS 12/5/2020	2020/OCT
MP-38 UPPER ELGIN ROAD SONOITA	SR82 MP38	GRANITE CONST	120	17	14%	\$685,530	\$16,571	2%	CLEAR AND GRUB	
I-10 VAIL RD. TI UP EB 744 MOUNTAIN	I-10,	GRANITE CONST	550	549	100%	\$4,204,833	\$3,882,450	92%	Close out	20-Sep
SR86-MP88 - QUIJOTOA	SR86 88.25-90.37	FALCONE BROTHER'S	105	101	96%	\$1,340,000	\$1,132,808	85%	Install Wattles Seeding	20-Dec
I-10 HOUGHTON ROAD	274 - 276	AMES CONST	450	108	24%	\$23,427,902	\$5,823,695	25%	Girder Installation Deck Forming	21-Dec

Questions?

Thank You

rlane@azdot.gov
