


Item 9 – State Engineer's Report January 17, 2025 Summary of Active and Finalized Projects

94 projects under construction \$2.9 B

2 projects finalized in December \$8.4 M

Fiscal Year to date: 47 projects finalized



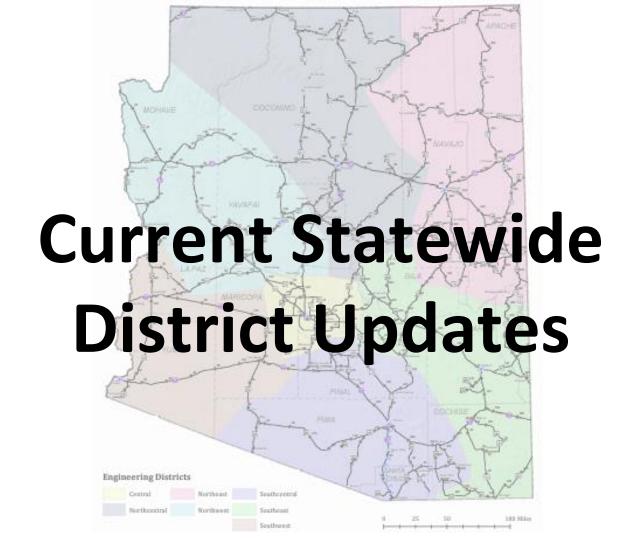

South Central District Current

ARIZONA

— DEPARTMENT OF

TRANSPORTATION


SR87 and Skousen Traffic Signal

I-10 Widening: Ina to Ruthrauff, MP 248.03-MP 251.85

Country Club to Kino (Design Build Procurement), I-10, MP 262-MP 264.5

Irvington TI (Design), I-19, MP 60.83

Border Patrol Station to Moson Rd., SR 90, MP 304.4-MP 325.9

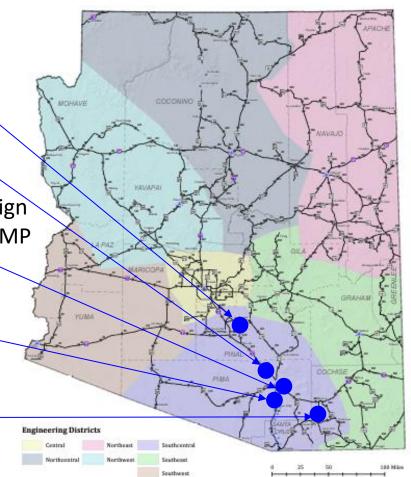


North Central District Current Projects

Broadband, I-40, CA

State Line to I-17/I
40 TI


Variable Speed Limit System, I-40, Transwestern Rd to I-17/I-40 TI

Pavement Rehabilitation, SR87, Indian Rd to Houston Mesa Rd, MP 250.9 to MP 254.5

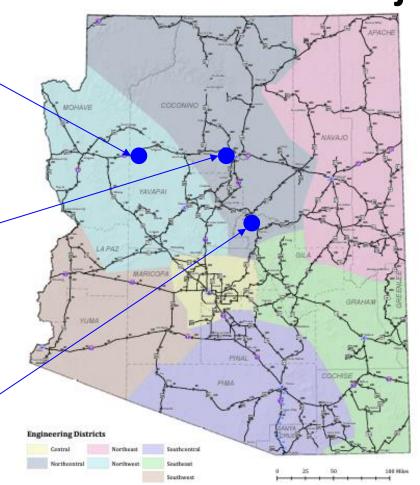

Southwest District's Current Projects



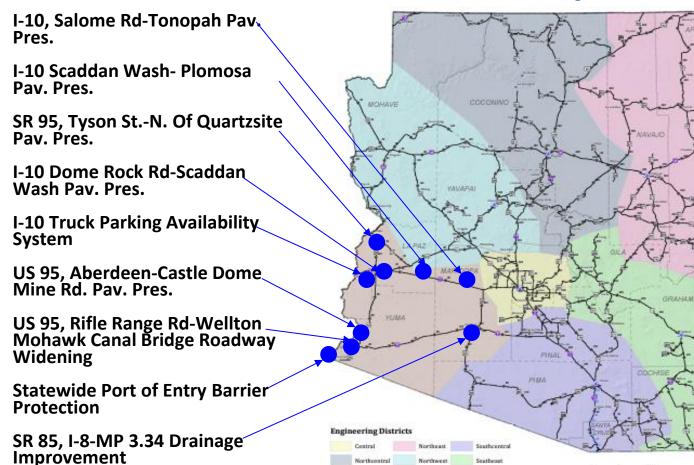

Southwest


Southeast District Current Projects



US 191 at SR 75 and SR 78 US 191, MP 154 Construct Roundabout

County Rd 220 - Yellowjacket Rd (Design)
US 70, MP 288.1 to MP 289.3
Construct WB Passing Lane

East Willcox TI UP _ I-10, MP 344.5 Bridge Rehabilitation

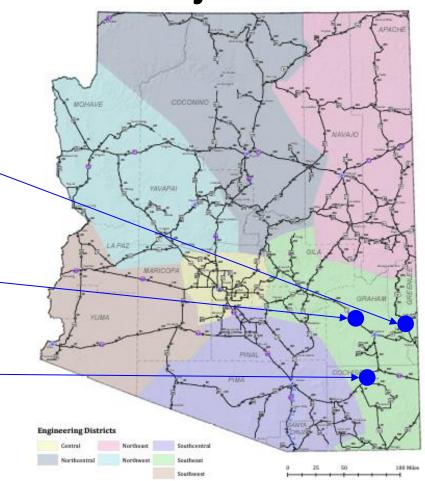





W Kingman TI


I-40/US 93, MP 49 - MP 52 Contractor: Fisher Sand and Gravel 3% Complete, 5% Time Spent

Needle Mtn TI - Lake Havasu TI

I-40, MP 2.4 - MP 8.3 Contractor: FNF Construction 14% Complete, 21% Time Spent

Prescott Lakes Pkwy to Heather Heights

SR 69, MP 293 - 296 Contractor: Fann Contracting 33% Complete, 54% Time Spent

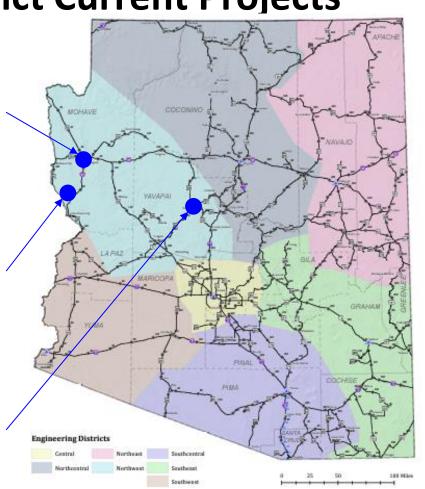


Northeast District Current Projects



8th Ave Bridge Holbrook I 40 MP 286 - MP 287

Taylor to Rodeo Road Snowflake SR 77 MP 358.8 - 359.4

SR 73 at the SR 260 Junction Hon Dah SR 73 MP 357

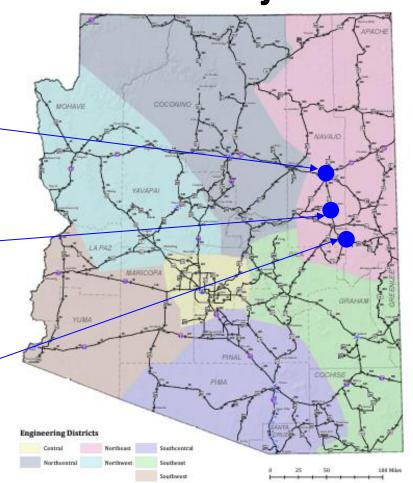

Central District Current Projects

ARIZONA

— DEPARTMENT OF

TRANSPORTATION

I-17 Happy Valley to SR74 Mill and Diamond Grind 99% Complete 76% Time Spent

SR101 Princess to Shea Loop 101 Expansion in Scottsdale 53% Complete 50% Time Spent


SR101 I-17 to 75th Ave Loop 101 Expansion in Phoenix/Glendale 11% Complete 12% Time Spent

SR303 and US60 Interim Interchange Improvements 74% Complete 88% Time Spent

US 60X Sossaman to Meridian Old US60 Highway
41% Complete 45% Time Spent

SR202 Val Vista to SR101L Loop 202 Expansion in Chandler/Gilbert 17% Complete 18% Time Spent

I-10 Gila River Bridge
Bridge Replacement
31% Complete 28% Time Spent

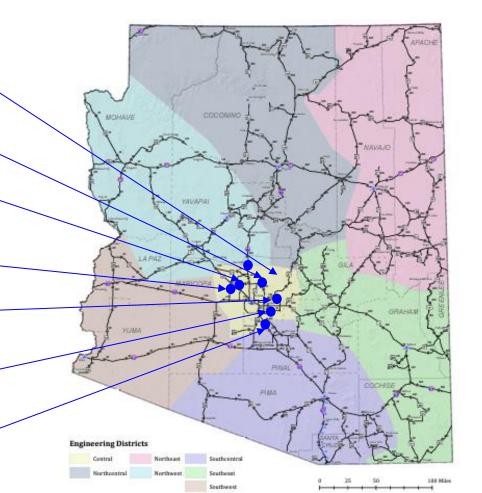

Item 9 – New Construction Contracts



Item	tem Highway Low bid		State Estimate	Difference	Percent
4e US 160		\$19,771,771	\$21,630,643	(\$1,858,871.65)	-8.6%
TOTAL THIS MONTH		\$19,987,719.89	\$18,517,824.15	\$1,469,895.74	7.9%
TOTAL FY TO DATE		\$758,944,107.25	\$661,305,653.60	\$97,638,453.65	14.8%

Monthly Totals for Construction Contracts



Month	No. of Bids	Awards	Low bid	State Estimate	Difference	Perce nt
Jul-24	13	11	\$470,592,427.92	\$354,288,928.30	\$116,303,499.62	32.8%
Aug-24	15	15	\$145,345,706.78	\$141,346,079.15	\$3,999,627.63	2.8%
Sep-24	4	3	\$11,859,517.78	\$12,791,450.10	(\$931,932.32)	-7.3%
Oct-24	11	10	\$91,386,963.88	\$112,730,728.90	(\$21,343,765.02)	-18.9%
Nov-24	5	5	\$19,987,719.89	\$18,517,824.15	\$1,469,895.74	7.9%
Dec-24	1	1	\$19,771,771.00	\$21,630,643.00	(\$1,858,872.00)	-8.6%
Jan-25						
Feb-25						
Mar-25						
Apr-25	·					·
May-25	·					
Jun-25	·					
Fiscal YTD	49	45	\$758,944,107.25	\$661,305,653.60	\$97,638,453.65	14.8%

District 5

PAVEMENT REHABILITATION US 160: SW DENNEHOTSO - MP 440





Low Bid	\$19,771,771		
State Estimate	\$21,630,643		
Difference	-\$1,858,872		
% Difference	-8.6%		

Recommendation: Award

Reasons for Difference:

AC Binder

