


State Transportation Board District Administrator's Report

Presentation By: Randy Everett

Date: February 21, 2025

Senior Staff

- Randy Everett - Senior Division Administrator
 - Sara Howard - Assistant District Engineer
- 

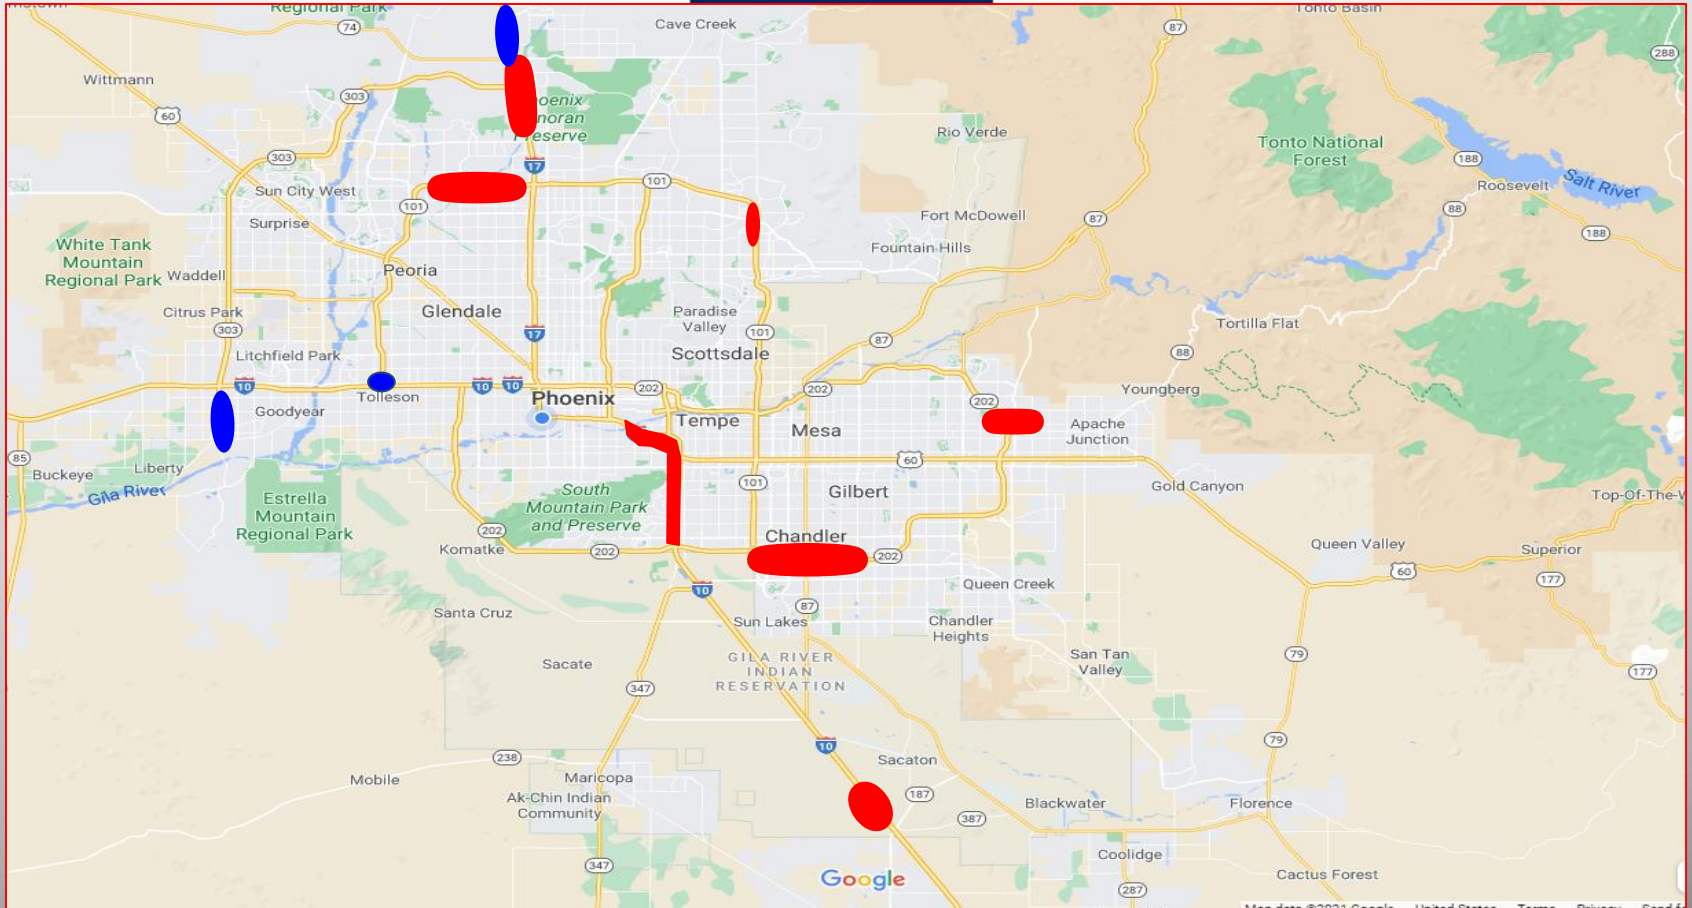

I-17 Happy Valley to SR74

Construction Completion: 99%

Contract Time Completion: 85%

Contractor: Acme Concrete



L101 - I-17 to 75th Ave

Construction Completion: 12%

Contract Time Completion: 15%

Contractor: Coffman Specialties



L202 - Val Vista to L101

Construction Completion: 22%

Contract Time Completion: 21%

Contractor: Sundt/CS JV



SR101 - Princess to Shea

Construction Completion: 57%

Contract Time Completion: 54%

Contractor: FNF Construction



US60X - Sossaman to Meridian

Construction Completion: 43%

Contract Time Completion: 48%

Contractor: Pulice Construction



I-10 Gila River Bridges

Construction Completion: 35%

Contract Time Completion: 32%

Contractor: Pulice



I-10 Split to SR 202 (Broadway Curve)


Construction Completion: 99%

Contract Time Completion: 99%

Contractor: PFFJV



Upcoming District Projects



I-17 Carefree Hwy to Anthem

Construction: May 2025

Construction Cost: \$21M



I-10/SR 101L DHOV

Advertise: May 2025

Construction Cost: \$245M



SR 303 - Van Buren to MC 85

Advertise: July 2025


Construction Cost: \$600M



SR101 - Pima to Shea - Diamond Grind

Advertise: October 2025

Construction Cost: \$15M



Questions

