


## Item 9 – State Engineer's Report July 18, 2025 Summary of Active and Finalized Projects

- **88 projects under construction** **\$2.9 B**
- **5 projects finalized in June** **\$21.4 M**
- **Fiscal Year to date:** **86 projects finalized**

# Current Statewide District Updates

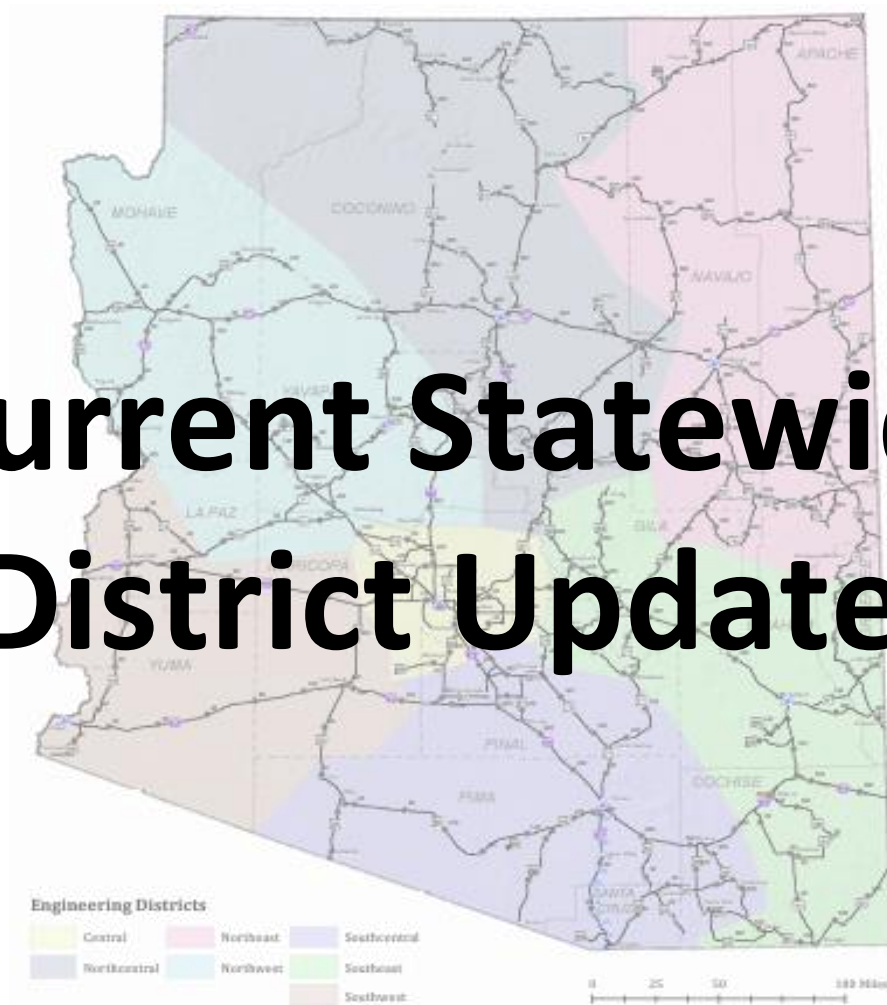

# South Central District Current Projects

## **I-10 Widening Ina to Ruthrauff**

MP 248.03-MP 251.85

Contractor: Granite Construction

86% Complete, 85% Time Spent

## **I-10 Kino to Country Club**

MP 262-MP 264.5 (Design Build Procurement)

Contractor: Sundt/Jacobs

NTP 1 Complete; NTP 2 Issued June 2025

## **I-19 Irvington TI (Design), MP 60.83**

Final Design Firm: WSP

## **SR-90 Border Patrol Station to Moson Rd.**

MP 304.4-MP 325.9


Contractor: FNF Construction

97% Complete, 99% Time Spent

## **SR-83 Black Oak Drive to Lower Elgin Road**

MP 31-MP 29

Project advertised on 5/27. Bid Opening 7/18.

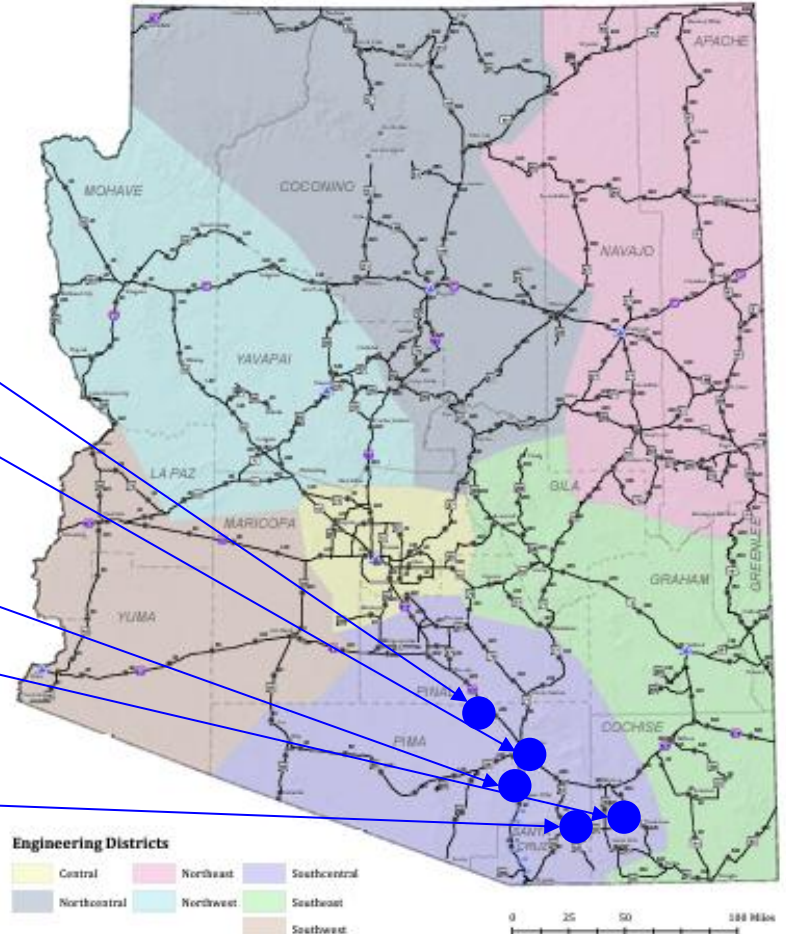

# Northcentral District Current Projects

## Townsend Winona to Sunset Crater Drainage Repairs

US 89 MP 423 - MP 432

Contractor: Granite Construction  
45% Complete, 41% Time Spent

## I-40 Broadband: CA State Line to I-17/I-40 T.I.


Contractor: EX<sup>2</sup> Technologies, LLC  
41% Complete, 35% Time Spent

## Roundabout, City of Flagstaff

Fourth St/Cedar Ave/ Lockett Rd  
Contractor: Fann Contracting  
30% Complete, 46% Time Spent

## Willard Springs Wildlife Overpass

Contractor: SEMA Construction  
23% Complete, 25% Time Spent

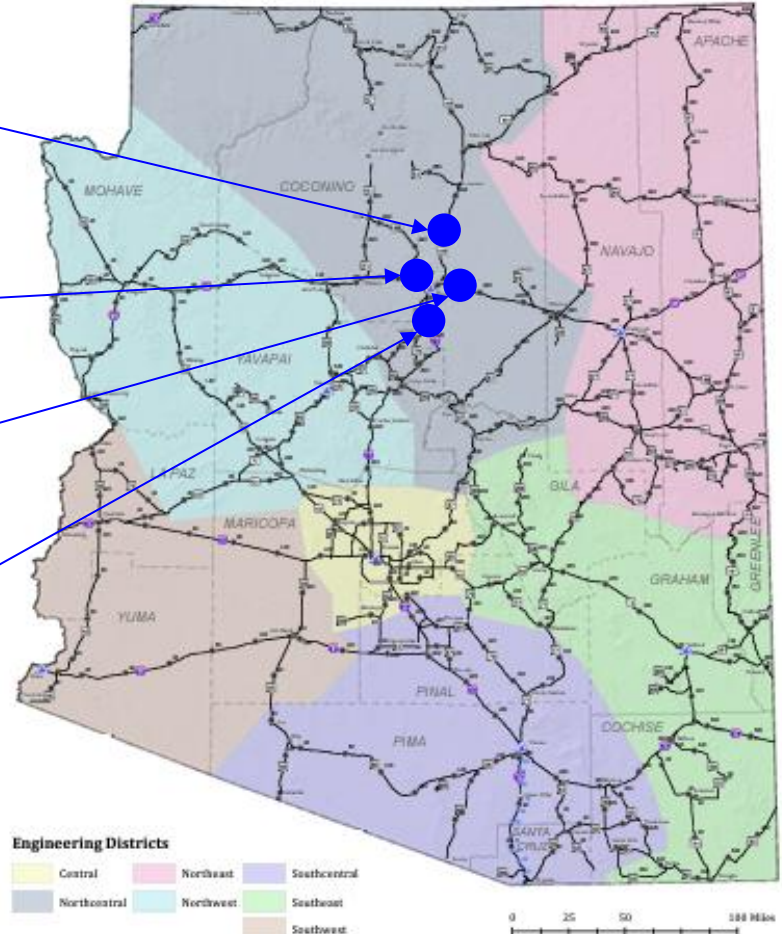

# Southwest District Current Projects

## Statewide Road Weather Info System Upgrade

Contractor: Roadway Electric, LLC.

0% Complete, 0% Time Spent

## I-10, Salome Rd-Tonopah

MP 80 - 90 Pav. Pres.

Contractor: Fisher Sand & Gravel

73% Complete, 56% Time Spent

## SR 95, Tyson St.-N. Of Quartzsite

MP 109 - 111 Pav. Pres.

Contractor: FNF Construction, Inc.

98% Complete, 71% Time Spent

## Yuma County, Co.19th St & Ave G Rumble Strip


Contractor: Pavement Marking, LLC

68% Complete, 33% Time Spent

## Yuma County Pavement Marking

Contractor: Pavement Marking, LLC

81% Complete, 33% Time Spent

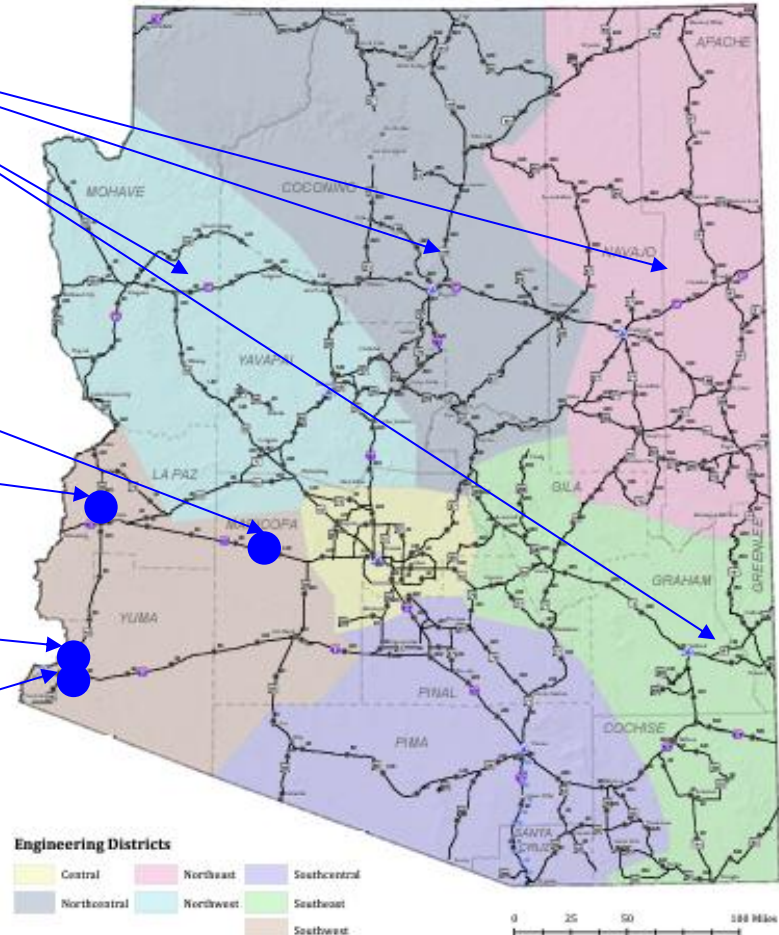



# Southeast District Current Projects

## Schulze Ranch - Town of Miami

US 60, MP 241.4 to MP 242.2

Contractor: Meridian Engineering Company

61% Complete, 83% Time Spent

## Queen Creek Bridge

US 60, MP 227.7

Contractor: Ames Construction


43% Complete, 48% Time Spent

## 7th Street to MP 173

US 191, MP 163 to MP 173

Contractor: FNF Construction

87% Complete, 82% Time Spent

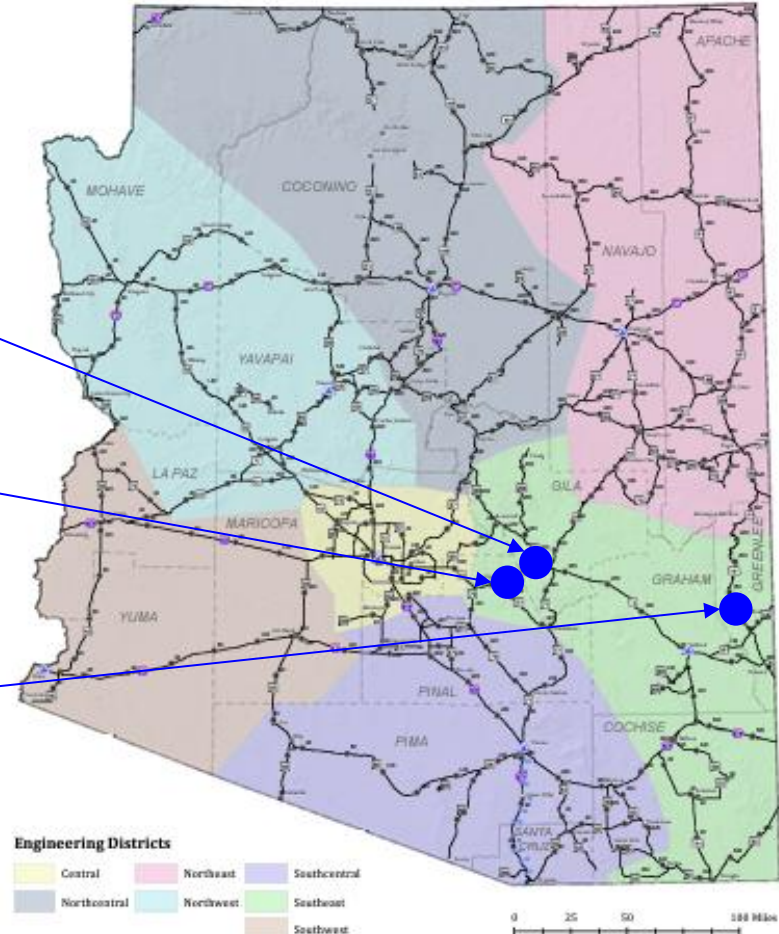

# Northwest District Current Projects

## Rancho Santa Fe Parkway TI

I-40, MP 55 - MP 57

Contractor: Pulice Construction

32% Complete, 35% Time

Spent

## Cane Springs

US 93, MP 106 - MP 110

Contractor: FNF Construction

38% Complete, 21% Time Spent

## Prescott Lake Parkway to Heather Heights

SR 69, MP 293 - MP 296

Contractor: Fann Contracting


70% Complete, 95% Time Spent

## Centennial Wash Bridge

US 60, MP 61 - MP 63

Contractor: FNF Construction

98% Complete, 80% Time Spent

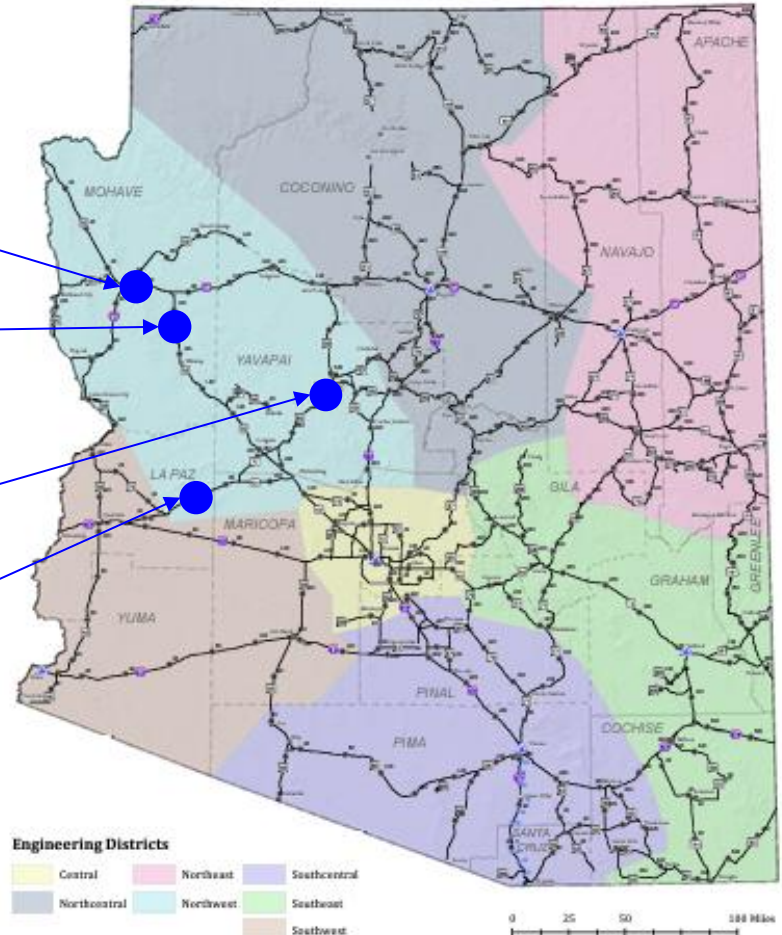

# Northeast District Current Projects

## SW Dennehotso to MP 440

US 160 MP 416 - MP 440

Contractor: Sunland Asphalt

52% Complete, 32% Time Spent

## Cross Canyon to Summit

SR 264 MP 459 - 465

Contractor: Cactus Asphalt

50% Complete, 32% Time Spent

## Little Mormon Lake Rd - Bell Spring

US 60 MP 345.71 - 346.93

Contractor: FANN Contracting


20% Complete, 20% Time Spent

## SR 61 to Wildcat Creek

US 60 MP 352.8 - 369.2

Contractor: W. W. Clyde

2% Complete, 36% Time Spent

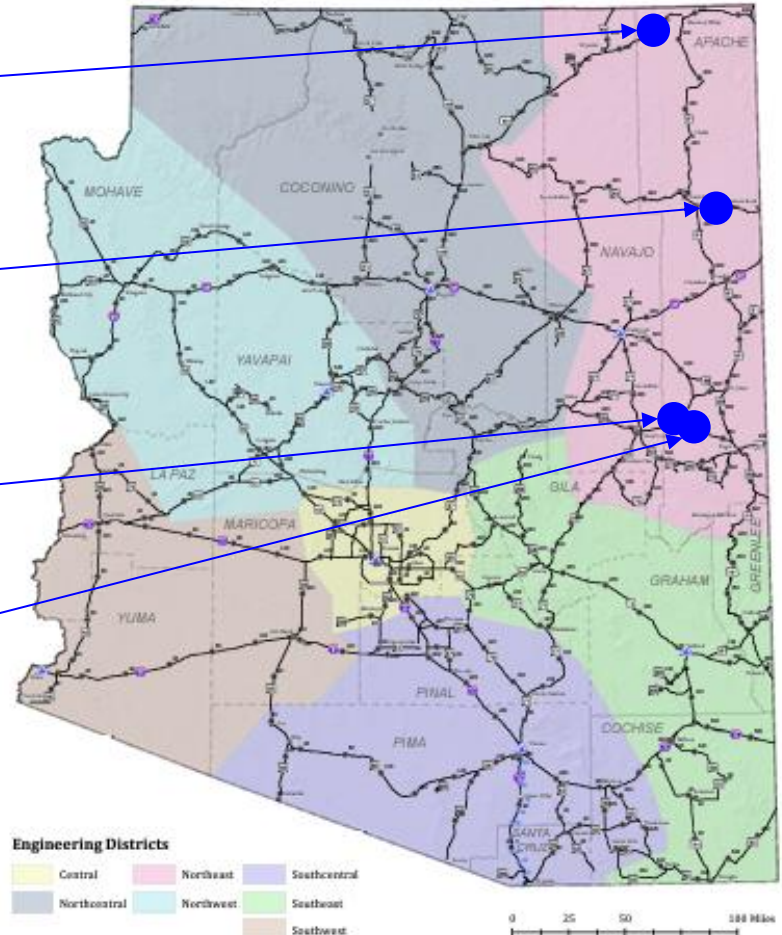



# Central District Current Projects

## SR101 Princess to Shea

Loop 101 Expansion in Scottsdale  
79% Complete 76% Time Spent

## SR101 I-17 to 75th Ave

Loop 101 Expansion in Phoenix/Glendale  
34% Complete 32% Time Spent

## SR303 and US60

Interim Interchange Improvements  
80% Complete 95% Time Spent

## US 60X Sossaman to Meridian


Old US60 Highway  
66% Complete 70% Time Spent

## SR202 Val Vista to SR101L

Loop 202 Expansion in Chandler/Gilbert  
40% Complete 38% Time Spent

## I-10 Gila River Bridge

Bridge Replacement  
57% Complete 50% Time Spent

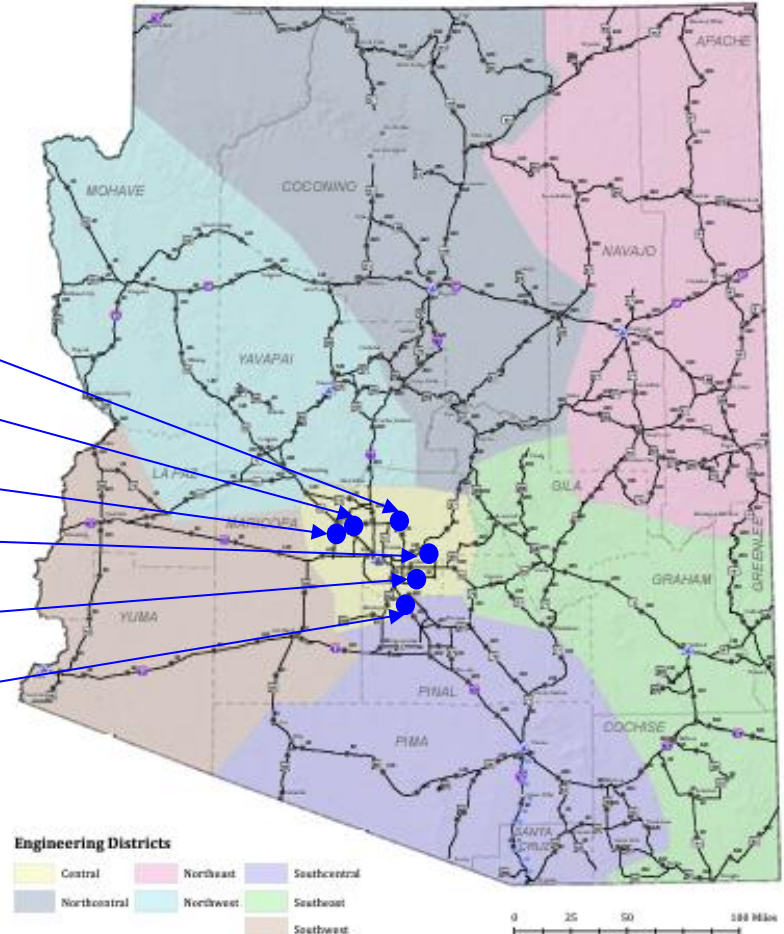

## Item 10 – New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3f	I-17	\$846,841	\$938,282	(\$91,442)	-9.7%
3g	I-40	\$26,445,000	\$30,528,773	(\$4,083,773)	-13.4%
3h	US 70	\$9,594,288	\$10,568,495	(\$974,207)	-9.2%
3i	SR 72	\$8,279,863	\$9,224,009	(\$944,146)	-10.2%
3j	SR 101L	\$3,585,553	\$3,375,577	\$209,976	6.2%
3k	SR 101 & SR202	\$1,372,920	\$1,500,100	(\$127,180)	-8.5%
3l	LOCAL	\$1,150,000	\$1,218,864	(\$68,864)	-5.6%
10a	I-17	\$1,281,556	\$1,538,640	(\$257,084)	-16.7%
10b	LOCAL	\$5,159,094	\$4,098,747	\$1,060,347	25.9%
10c	LOCAL	\$913,270	\$720,000	\$193,270	26.8%
10d	LOCAL	\$1,422,222	\$1,830,323	(\$408,101)	-22.3%
10e	LOCAL	\$2,733,476	\$2,468,919	\$264,557	10.7%
<b>TOTAL THIS MONTH</b>		\$62,784,082	\$68,010,729	(\$5,226,646)	-7.7%
<b>TOTAL FY TO DATE</b>		\$62,784,082	\$68,010,729	(\$5,226,647)	-7.7%

# Monthly Totals for Construction Contracts

Month	No. of Bids	Awards	Low bid	State Estimate	Difference	Percent
Jul-25	12	12	\$62,784,082	\$68,010,729	(\$5,226,647)	-7.7%
Aug-25						
Sep-25						
Oct-25						
Nov-25						
Dec-25						
Jan-26						
Feb-26						
Mar-26						
Apr-26						
May-26						
Jun-26						
Fiscal YTD	12	12	\$62,784,082	\$68,010,729	(\$5,226,647)	-7.7%

## District 1

## ROADWAY WIDENING I-17: SONORAN DESERT DRIVE NB OFF-RAMP

## Item 10a

<b>Low Bid</b>	<b>\$1,281,556</b>
<b>State Estimate</b>	<b>\$1,538,640</b>
<b>Difference</b>	<b>-\$257,084</b>
<b>% Difference</b>	<b>-16.7%</b>

### Recommendation: Award

#### Reasons for Difference:

- Roadway Excavation
- PCCP
- Curb & Gutter





# SIDEWALKS & FLASHING YELLOW ARROWS


## CITY OF GLENDALE

## Item 10b

Low Bid	\$5,159,094
State Estimate	\$4,098,747
Difference	\$1,060,347
% Difference	25.9%

**Recommendation: Award**  
Reasons for Difference:

- Electrical Work

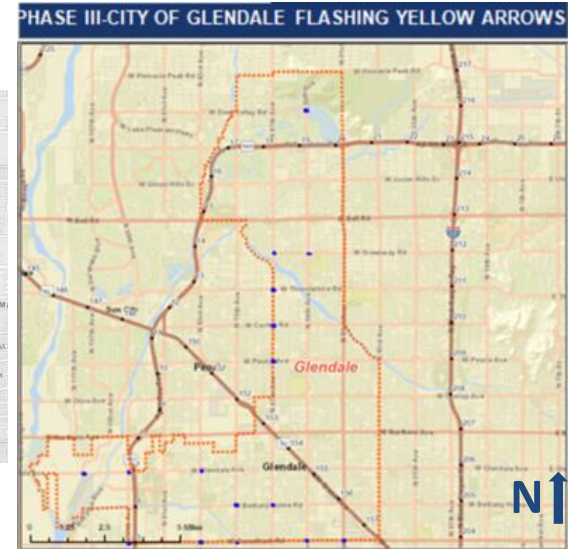

## District 6

## STOP SIGN GAP ASSIST MOHAVE COUNTY

Item 10c

Low Bid	\$913,270
State Estimate	\$720,000
<b>Difference</b>	<b>\$193,270</b>
<b>% Difference</b>	<b>26.8%</b>

### Recommendation: Award

Reasons for Difference:

- Stop Sign Gap Assist System
- Monitoring Software



## District 5


## SIDEWALK IMPROVEMENTS JOSEPH CITY

## Item 10d

<b>Low Bid</b>	<b>\$1,422,222</b>
<b>State Estimate</b>	<b>\$1,830,323</b>
<b>Difference</b>	<b>-\$408,101</b>
<b>% Difference</b>	<b>-22.3%</b>

**Recommendation: Award**  
**Reasons for Difference:**

- Sidewalk

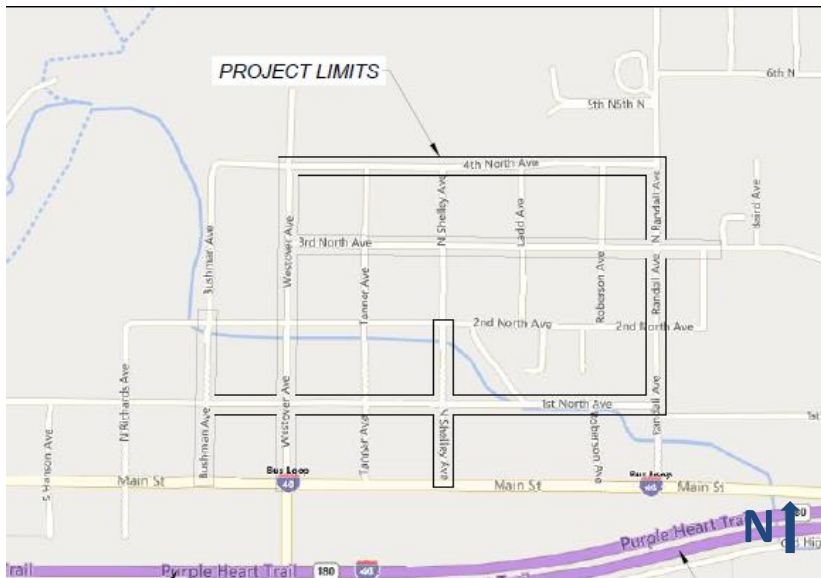

## District 2

## MULTI-USE PATH TOWN OF ORO VALLEY


## Item 10e

Low Bid	\$2,733,476
State Estimate	\$2,468,919
Difference	\$264,557
% Difference	10.7%

### Recommendation: Award

#### Reasons for Difference:

- Retaining Wall

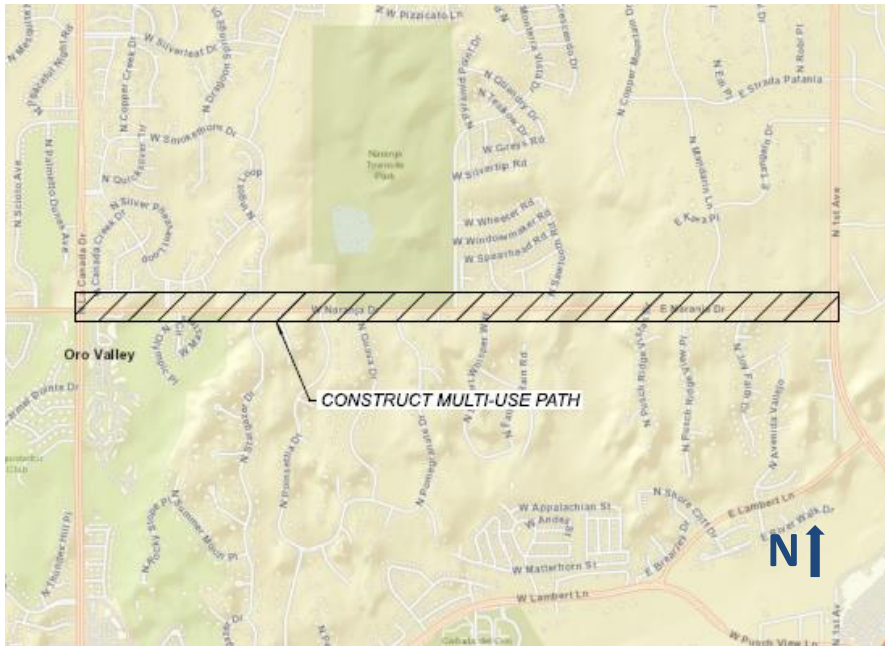



## District 6

## TRUCK SCREENING SENSORS I-17: MCGUIREVILLE REST AREA

Item 3f

Low Bid	\$846,841
State Estimate	\$938,282
Difference	-\$91,442
% Difference	-9.7%

### Recommendation: Award

Reasons for Difference:

- Loops & Sensors



## District 5

## PAVEMENT REHABILITATION I-40: TWO GUNS - DENNISON

## Item 3g

<b>Low Bid</b>	<b>\$26,445,000</b>
<b>State Estimate</b>	<b>\$30,528,773</b>
<b>Difference</b>	<b>-\$4,083,773</b>
<b>% Difference</b>	<b>-13.4%</b>

### Recommendation: Award

#### Reasons for Difference:

- Asphalt Binder
- Asphaltic Concrete
- Sidewalk



# PAVEMENT REHABILITATION

## US 70: REAY LN - 8TH ST

Low Bid	\$9,594,288
State Estimate	\$10,568,495
Difference	-\$974,207
% Difference	-9.2%

- Asphaltic Concrete
- Sidewalk
- Curb & Gutter



## District 6

## PAVEMENT REHABILITATION SR 72: NW OF BOUSE TO SE OF BOUSE


## Item 3i

Low Bid	\$8,279,863
State Estimate	\$9,224,009
Difference	-\$944,146
% Difference	-10.2%

### Recommendation: Award

#### Reasons for Difference:

- Asphalt Binder
- Asphaltic Concrete

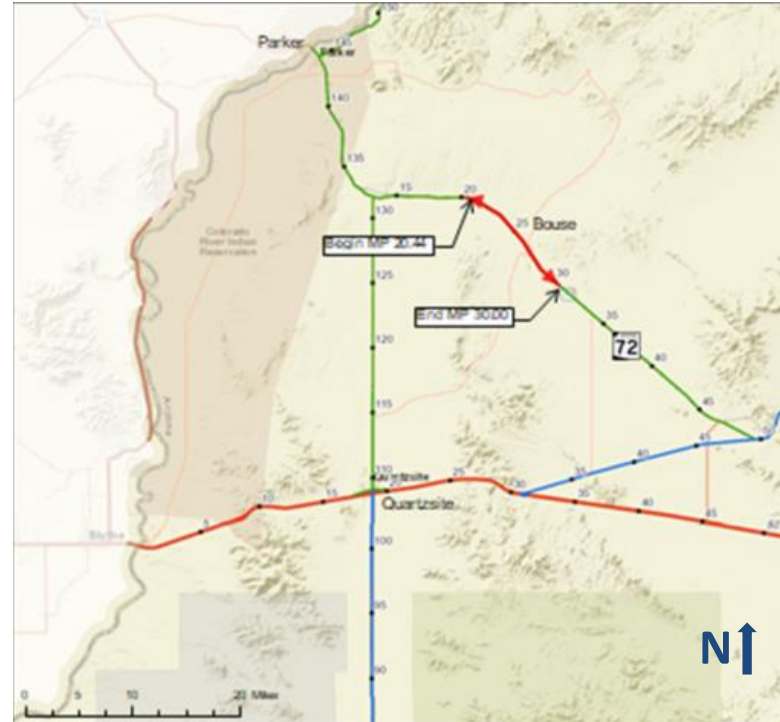





## District 1

## HPS TO LED LIGHTING SR 101L: SR 202L TO US 60 SR 202L (RED MTN): MCCLINTOCK DR TO THOMAS RD

## Item 3k

<b>Low Bid</b>	<b>\$1,372,920</b>
<b>State Estimate</b>	<b>\$1,500,100</b>
<b>Difference</b>	<b>-\$127,180</b>
<b>% Difference</b>	<b>-8.5%</b>

**Recommendation: Award**  
**Reasons for Difference:**

- Luminaires



## District 6

## TRAFFIC SIGNAL & TURN LANES YUMA COUNTY

## Item 31

<b>Low Bid</b>	<b>\$1,150,000</b>
<b>State Estimate</b>	<b>\$1,218,864</b>
<b>Difference</b>	<b>-\$68,864</b>
<b>% Difference</b>	<b>-5.6%</b>

### Recommendation: Award

#### Reasons for Difference:

- Roadway Grading
- Asphaltic Concrete

