

Arizona State Transportation Board Meeting

District Report - Southeast District

Todd Emery August 15, 2025





Current Construction Projects


Queen Creek Bridge US 60, MP 227.7 Contractor: Ames Construction 43% Complete, 51% Time Spent

Waterfall Canyon Bridge US 60, MP 229.5 Contractor: Ames Construction 23% Complete, 51% Time Spent

7th Street to MP 173 US 191, MP 163 to MP 173 Contractor: FNF Construction 96% Complete, 89% Time Spent

Table Top Road to 7th StUS 191, MP 160 to MP 163
Contractor: FNF Construction
74% Complete, 96% Time Spent

US 191 At SR 75 & SR 78 US 191, MP 154 Contractor: Granite Construction 83% Complete, 125% Time Spent

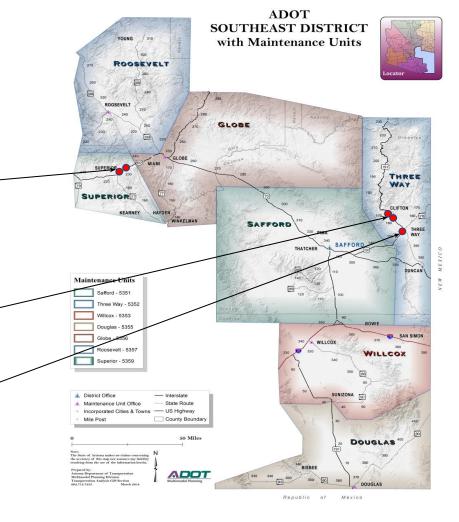









US 60, Waterfall Canyon Bridge US 191 At SR 75 & SR 78 Roundabout







Current Construction Projects

Schulze Ranch - Town of Miami

US 60, MP 241.4 to MP 242.2

Contractor: Meridian Engineering Company

68% Complete, 93% Time Spent

W Santee St to US 70

US 60, MP 250.1 to MP 252.1 Contractor: Granite Construction

0% Complete, 6% Time Spent

County Rd 220 - Yellowjacket Rd

US 70, MP 287.9 to MP 289

Contractor: Show Low Construction

8% Complete, 4% Time Spent

Reay Lane - 8th Street

US 70, MP 335 to MP 340


Contractor: Sunland Asphalt & Construction

0% Complete, 0% Time Spent

East Willcox TI UP Bridge

I-10, MP 344.5 to MP 345.5 Contractor: Granite Construction

99% Complete, 122% Time Spent

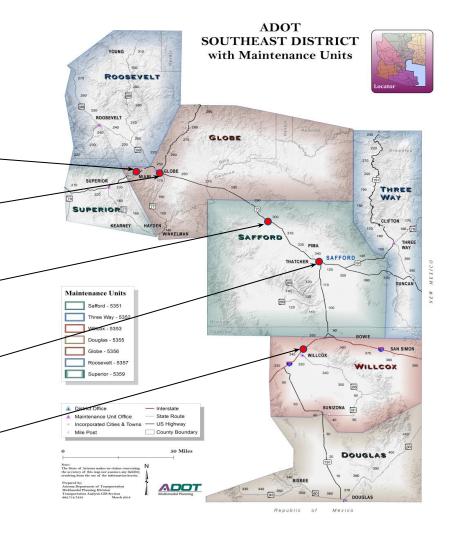



US 60, Schulze Ranch - Town of Miami



I-10, East Willcox TI UP









