


Item 8 – State Engineer's Report: November 21, 2025 Summary of Active and Finalized Projects

- **108 projects under construction** **\$2.3 B**
- **8 projects finalized in October** **\$47.9 M**
- **Fiscal Year to date:** **47 projects finalized**

Current Statewide District Updates



South Central District Current Projects

I-10 Widening Ina to Ruthrauff

MP 248.03-MP 251.85

Contractor: Granite Construction

90% Complete, 97% Time Spent

I-10 Kino to Country Club

MP 262-MP 264.5 (Design Build)

Contractor: Sundt/Jacobs

24% Complete, 13% Time Spent

I-19 Irvington TI (Design), MP 60.83

Final Design Firm: WSP

Construction: Spring of 2026

Amole RR OP EB/WB Deck Replacement

MP 292

Contractor: Granite Construction


2.5% Complete, 57% Time Spent

SR-83 Black Oak Drive to Lower Elgin Road

MP 31-MP 29

Contractor: Granite Construction

6% Complete, 30% Time Spent

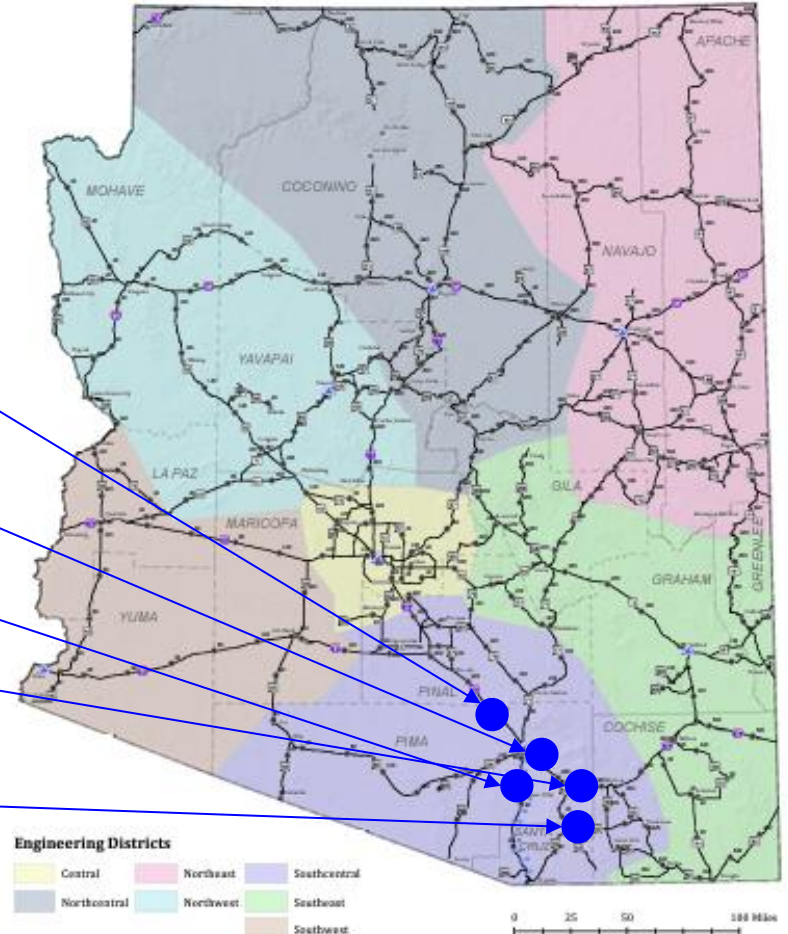

Northcentral District Current Projects

Townsend Winona to Sunset Crater Drainage Repairs

US 89 MP 423 - MP 432

Contractor: Granite Construction

105% Complete, 102% Time Spent

I-40 Broadband: CA State Line to I-17/I-40 T.I.

Contractor: EX² Technologies, LLC

67% Complete, 56% Time Spent

Willard Springs Wildlife Overpass

Contractor: SEMA Construction


64% Complete, 63% Time Spent

Two Guns to Dennison

I-40 MP 229 - 240

Contractor: Fann Contracting

33% Complete, 19% Time Spent

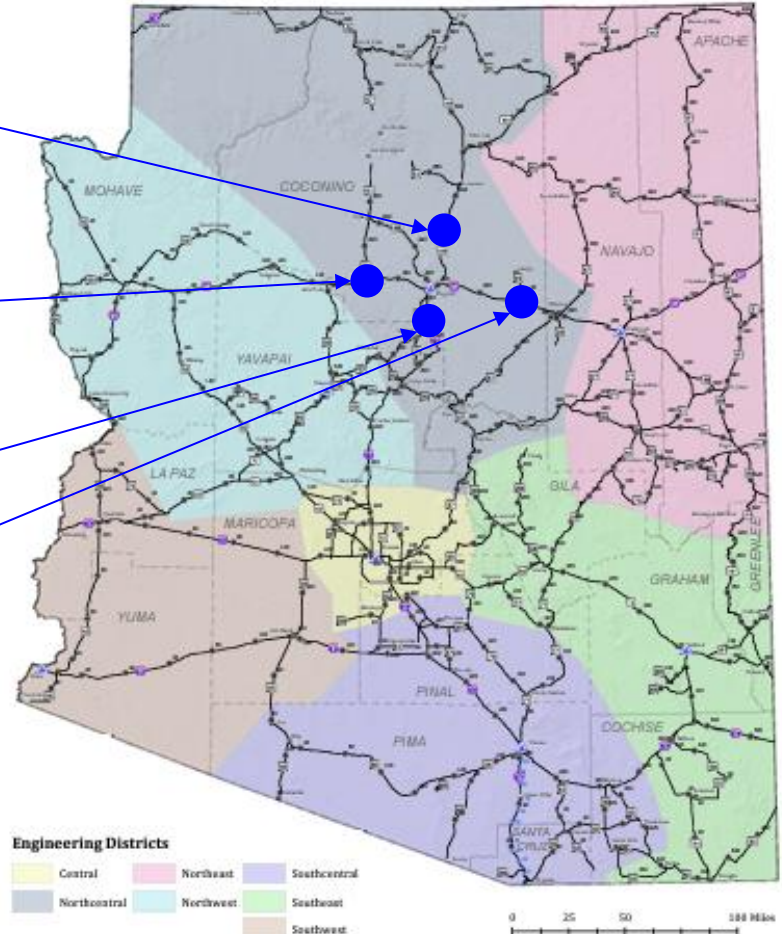

Southwest District Current Projects

Statewide Road Weather Info System Upgrade

Contractor: Roadway Electric, LLC.

3% Complete, 0% Time Spent

State Route 72, NW Bouse-SE Bouse

MP 20.44-30 Pav. Pres.

Contractor: FNF Construction, Inc.

39% Complete, 28% Time Spent

SR 95, Tyson St.-N. Of Quartzsite

MP 109 - 116 Pav. Pres.

Contractor: FNF Construction, Inc.

99% Complete, 95% Time Spent

Yuma County, Co. 14th St & Avenue 4E

Traffic Signal Installation

Contractor: DPE Construction, Inc.


1% Complete, 47% Time Spent

City of Yuma, Pedestrian Hybrid Beacons

Pedestrian Hybrid Beacon Installation

Contractor: DPE Construction, Inc.

0% Complete, 6% Time Spent

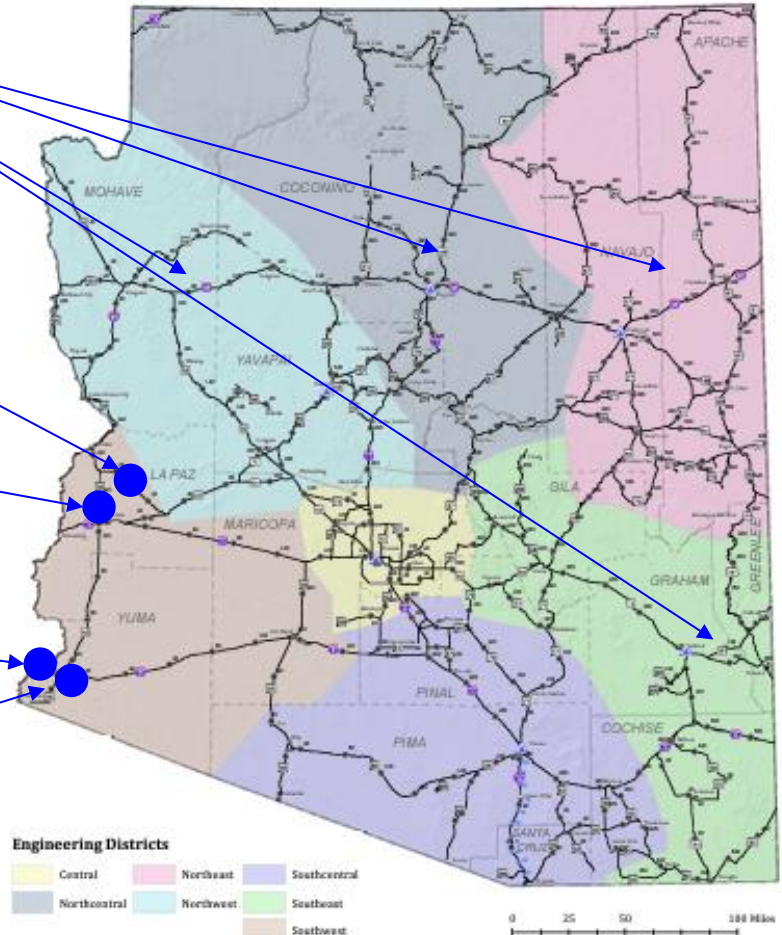

Southeast District Current Projects

W Santee St to US 70

US 60, MP 250.1 to MP 252.1

Contractor: Granite Construction

19% Complete, 54% Time Spent

County Rd 220 - Yellowjacket Rd

US 70, MP 287.9 to MP 289

Contractor: Show Low Construction


44% Complete, 41% Time Spent

Reay Lane - 8th Street

US 70, MP 335 to MP 340

Contractor: Sunland Asphalt & Construction

7% Complete, 23% Time Spent

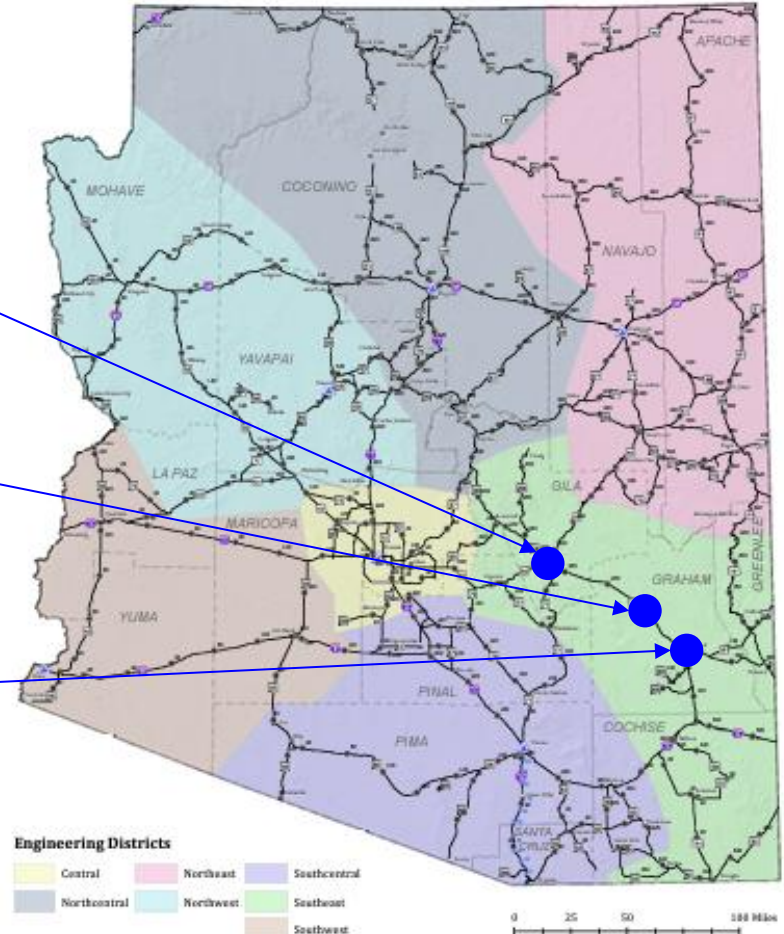

Northwest District Current Projects

West Tony Avenue-West Rocky Point Avenue

US93, MP 26 - MP 30

Contractor: McCormick Construction

56% Complete, 41% Time Spent

Holy Moses Wash to Rattlesnake Wash

I-40, MP 46 - MP 58

Contractor: Fisher Sand & Gravel

32% Complete, 59% Time Spent

Cane Springs

US 93, MP 106 - MP 110

Contractor: FNF Construction


58% Complete, 38% Time Spent

Morristown-Wickenburg

US 60, MP 110 - MP 122

Contractor: Sunland Asphalt

12% Complete, 22% Time Spent

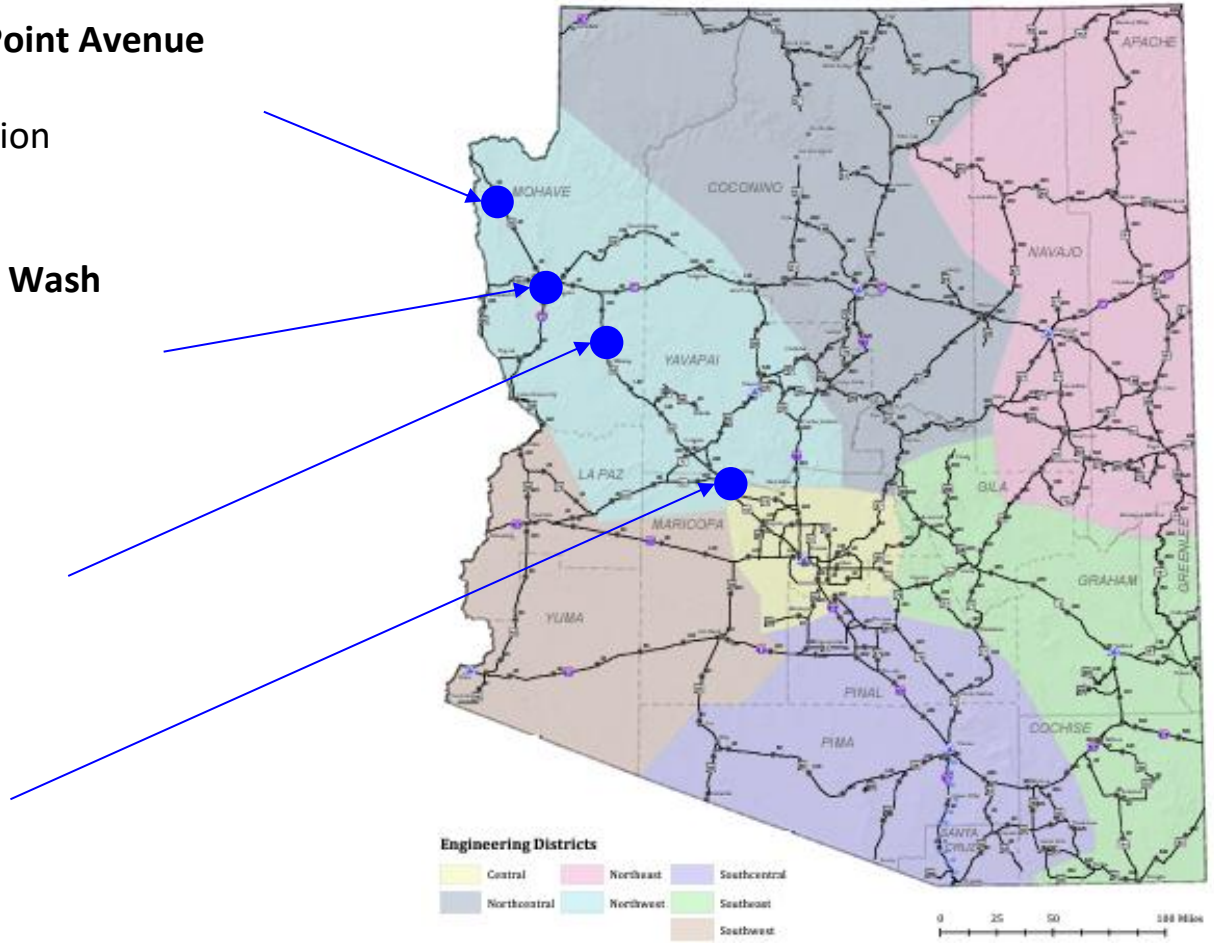

Northeast District Current Projects

Allentown TI

I 40 MP 351.35

Contractor: FNF

91% Complete, 101% Time Spent

Perkins Valley Bridge Widening

I-40 MP 283.4

Contractor: SEMA Construction

0% Complete, 5% Time Spent

Joseph City Sidewalk Improvements

Contractor: Hawk Contracting


98% Complete, 71% Time Spent

Pine Oaks to Fawnbrook

SR 260 MP 343.5 - 344.5

Contractor: Show Low Construction

21% Complete, 12% Time Spent

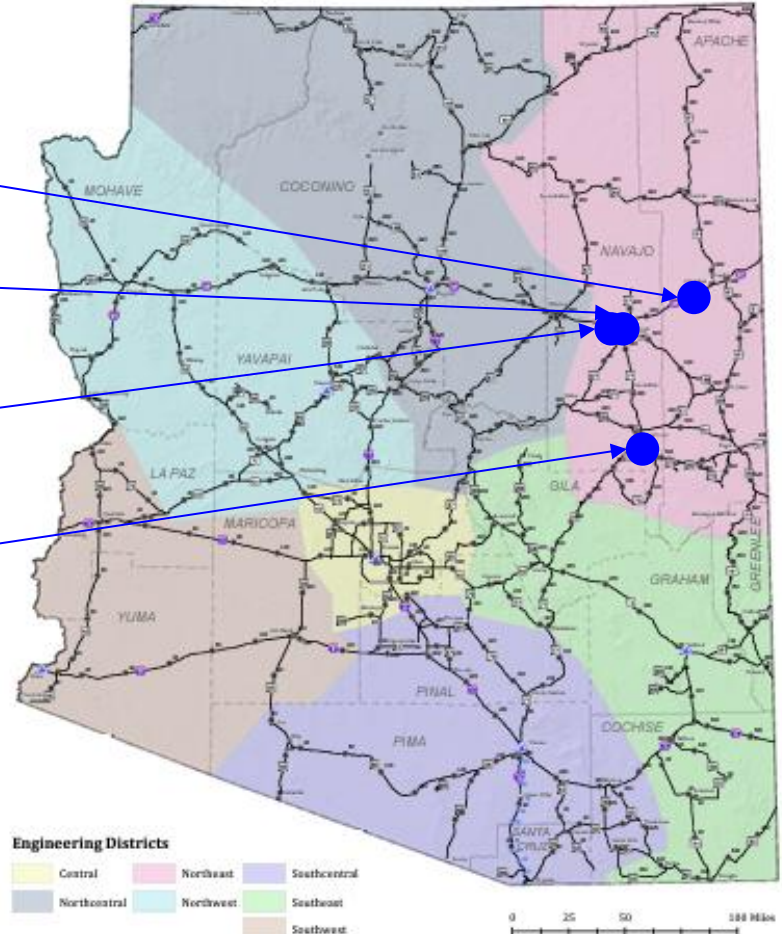

Central District Current Projects

I-17 SR74 to Anthem Way

I-17 Pavement Rehabilitation in Phoenix
48% Complete 62% Time Spent

SR101 Princess to Shea

Loop 101 Expansion in Scottsdale
93% Complete 93% Time Spent

SR101 I-17 to 75th Ave

Loop 101 Expansion in Phoenix/Glendale
52% Complete 45% Time Spent

US 60X Sossaman to Meridian


Old US60 Highway
82% Complete 85% Time Spent

SR202 Val Vista to SR101L

Loop 202 Expansion in Chandler/Gilbert
54% Complete 51% Time Spent

I-10 Gila River Bridge

Bridge Replacement
71% Complete 66% Time Spent

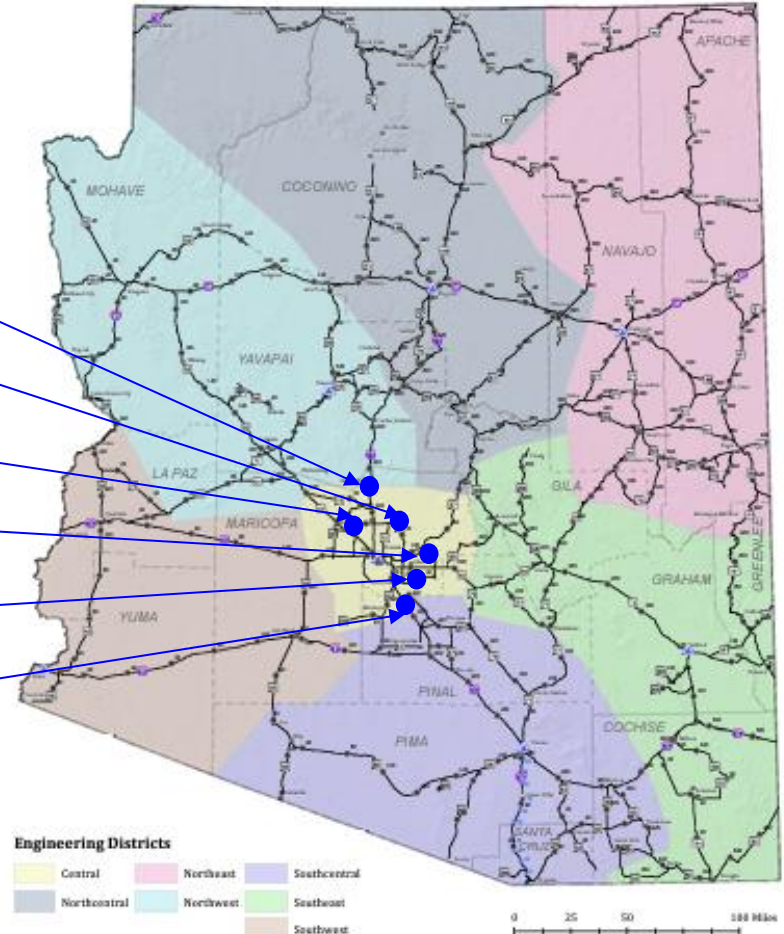

Item 9– New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3e	I10	\$3,090,844	\$2,934,591	\$156,253	5.3%
3f	LOCAL	\$1,194,211	\$1,238,716	(\$44,505)	-3.6%
9a	US95	\$24,676,798	\$19,555,109	\$5,121,689	26.2%
9b	SR 303L	\$129,253,115	\$174,154,965	(\$44,901,851)	-25.8%
9c	VARIOUS	\$1,072,320	\$653,000	\$419,320	64.2%
9d	LOCAL	\$2,818,888	\$4,363,049	(\$1,544,161)	-35.4%
9e	LOCAL	\$1,299,695	\$1,411,809	(\$112,114)	-7.9%
9f	LOCAL	\$4,211,713	\$5,740,038	(\$1,528,324)	-26.6%
TOTAL THIS MONTH		\$167,617,583	\$210,051,276	(\$42,433,693)	-20.2%
TOTAL FY TO DATE		\$518,705,796	\$594,550,667	(\$75,844,871)	-12.8%

Monthly Totals for Construction Contracts

Jul-25	12	12	\$62,784,082	\$68,010,729	(\$5,226,647)	-7.7%
Aug-25	10	9	\$38,937,658	\$46,892,438	(\$7,954,780)	-17.0%
Sep-25	11	11	\$169,185,208	\$170,035,931	(\$850,723)	-0.5%
Oct-25	9	7	\$80,181,265	\$99,560,293	(\$19,379,028)	-19.50%
Nov-25	8	6	\$167,617,583	\$210,051,276	(\$42,433,693)	-20.2%
Dec-25						
Jan-26						
Feb-26						
Mar-26						
Apr-26						
May-26						
Jun-26						
Fiscal YTD	50	45	\$518,705,796	\$594,550,667	(\$75,844,871)	-12.8%

District 6

ROADWAY IMPROVEMENTS US 95: IMPERIAL DAM & ABERDEEN RD


Item 9a

Low Bid	\$24,676,798
State Estimate	\$19,555,109
Difference	\$5,121,689
% Difference	26.2%

Recommendation: AWARD

Reasons for Difference:

- Production Rate/Shifts
- Construction of Roundabout
- Phased Construction
- Remote Location

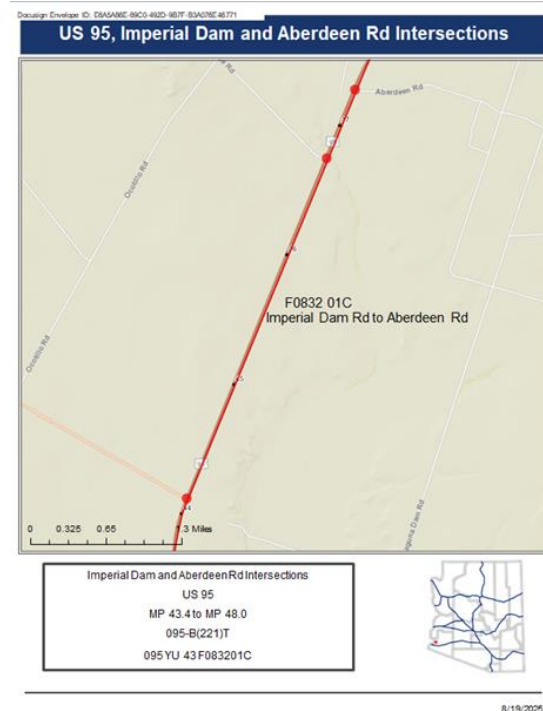

District 1

BRIDGE CONSTRUCTION SR 303L: BOB STUMP MEMORIAL PARKWAY

Item 9b

DocuSign Envelope ID: 5B25BABC-D2F2-406A-B34C-5CFDECA8AED9

Low Bid	\$129,253,115
State Estimate	\$174,154,965
Difference	-\$44,901,851
% Difference	-25.8%

Recommendation: AWARD

Reasons for Difference:


- Reduced Concrete Cost
- Self Perform Major Portions of Work, owns equipment and form work
- Additional work crews/reduce contract time and costs.

LOCATION MAP

LOCATION: SR 303L; 51st Avenue – I-17

PROJECT NO: 303 MA 136 F0562 01C

FEDERAL ID: 303-A(203)T

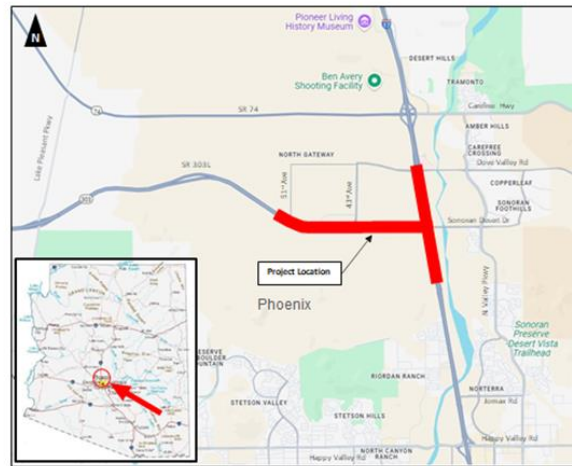

District 5

**LUMINARIES
FLAGSTAFF AREA: VARIOUS LOCATIONS**

Item 9c


Low Bid	\$1,072,320
State Estimate	\$653,000
Difference	\$419,320
% Difference	64.2%

Recommendation: AWARD

Reasons for Difference:

- Cost of Luminaries

DocuSign Envelope ID: 4C160D66-1F83-4987-A2E9-D1789C14D8B6

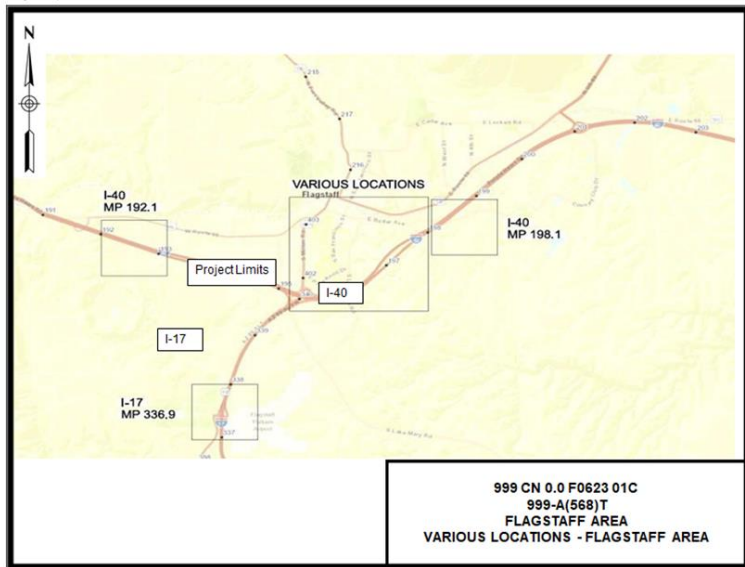

CITY OF APACHE JUNCTION OLD WEST HWY

Item 9d

Recommendation: REJECT BIDS

- Smaller Crew Sizes and Location of Material Source



DISTRICT 6

ROADWAY IMPROVEMENTS YUMA COUNTY

Item 9e

Low Bid	\$1,299,695
State Estimate	\$1,411,809
Difference	-\$112,114
% Difference	-7.9%

Recommendation: POSTPONE ACTION

Reasons for Difference:

- Removal Costs



District 6

**CONSTRUCT ROADWAY
YAVAPAI COUNTY**


Item 9f

Low Bid	\$4,211,713
State Estimate	\$5,740,038
Difference	-\$1,528,324
% Difference	-26.6%

Recommendation: AWARD

Reasons for Difference:

- Material Source Location
- Production Rate

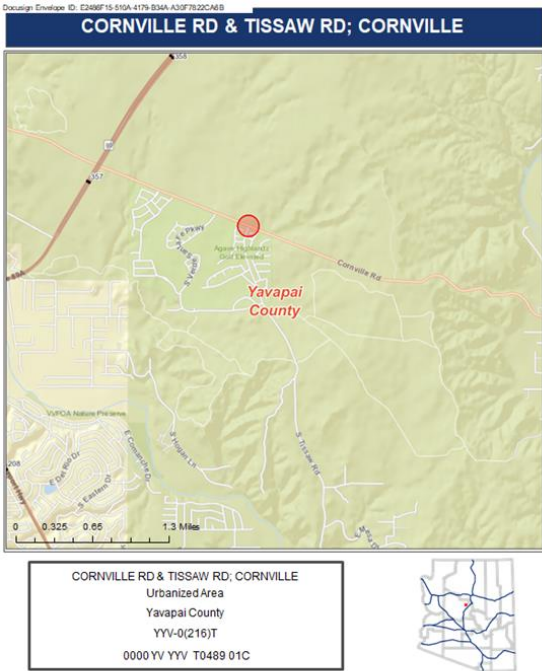

District 1

SYSTEM ENHANCEMENTS I10: 7TH STREET - CHANDLER BOULEVARD

Item 3e


Low Bid	\$3,090,844
State Estimate	\$2,934,591
Difference	\$156,253
% Difference	5.3%

Recommendation: AWARD

Reasons for Difference:

- Removal Costs

Drawings Envelope ID: 17C0F670-6CB9-42A0-8C12-E145745DC1F1

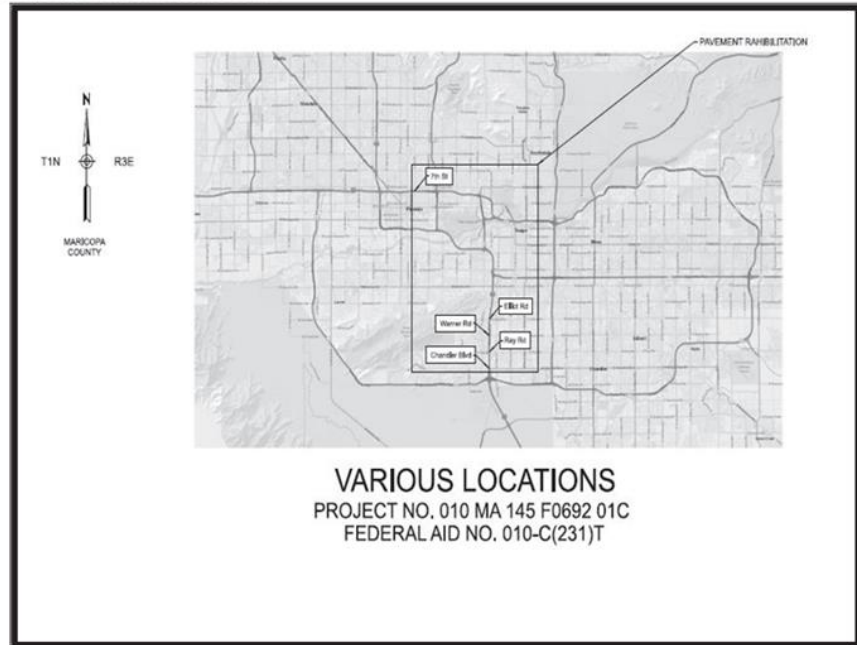

District 4

CONSTRUCT NEW TRAFFIC SIGNAL SR 384: CENTENNIAL BLVD & PINAL AVE.

Item 3f

Low Bid	\$1,194,211
State Estimate	\$1,238,716
Difference	-\$44,505
% Difference	-3.6%

Recommendation: AWARD

Reasons for Difference:

- Removal Costs

