

State Transportation Board District Administrator's Report December 19, 2025





Randy Everett - Senior District Administrator

Sara Howard - Assistant District Engineer

I-17 Mill & Fill - SR74 to Anthem

Construction Completion: 67%

Contract Time Completed: 74%

Contractor: Fann Construction

Estimated Completion: January 2026



SR101 - Princess to Shea

Construction Completion: 94%

Contract Time Completed: 97%

Contractor: FNF Construction

Estimated Completion: January 2026



SR101 - I-17 to 75th Ave

Construction Completion: 58%

Contract Time Completed: 48%

Contractor: Coffman Specialties

Estimated Completion: March 2027



SR202 Santan - SR101 to Val Vista

Construction Completion: 56%

Contract Time Completed: 54%

Contractor: Sundt/CS Construction JV

Estimated Completion: February 2027



US60X - Sossaman to Meridian

Construction Completion: 84%

Contract Time Completed: 88%

Contractor: Pulice Construction

Estimated Completion: May 2026



I-10 - Gila River Bridge

Construction Completion: 73%

Contract Time Completed: 69%

Contractor: Pulice Construction

Estimated Completion: August 2026



Upcoming District Projects



I-17/SR 303 System To System

Start Construction: January 2026

Contractor: Pulice Construction

Construction Cost: \$235M

Completion: Fall 2028



SR 303 - Van Buren to MC 85

Bid Opening: February 2026

Construction Cost: \$500M

Completion: Spring 2029




I-10/SR101 DHOV

Bid Opening: January 2026

Construction Cost: \$293M

Completion: Late 2028

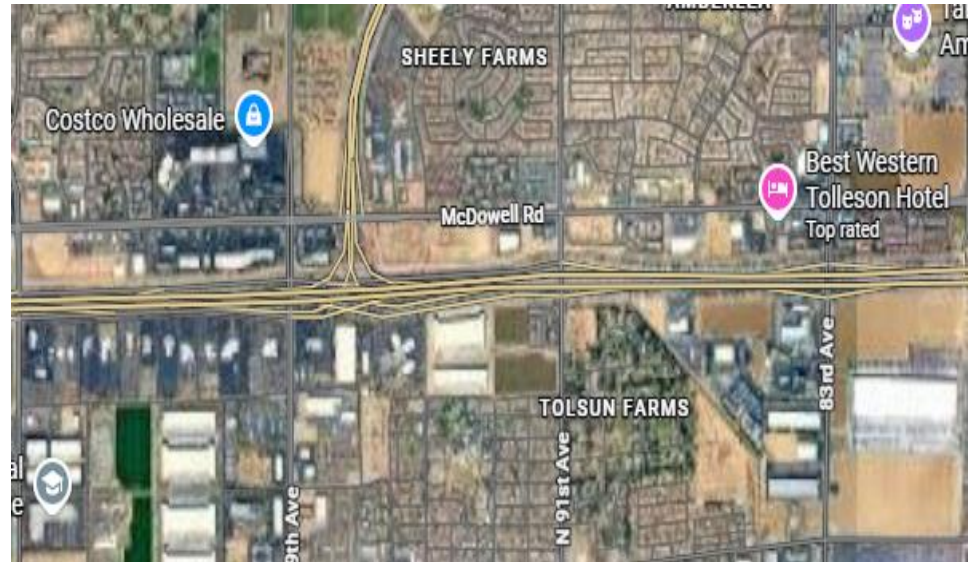

I-10 - Jackrabbit Trail TI

Anticipated Start:
Late Spring/Early Summer 2026

Construction Cost: \$58M

Completion: Fall/Winter 2027




SR 51 - I-10 to Shea Diamond Grind

Bid Opening: December 2025

Construction Cost: \$56M

Completion: Fall 2026

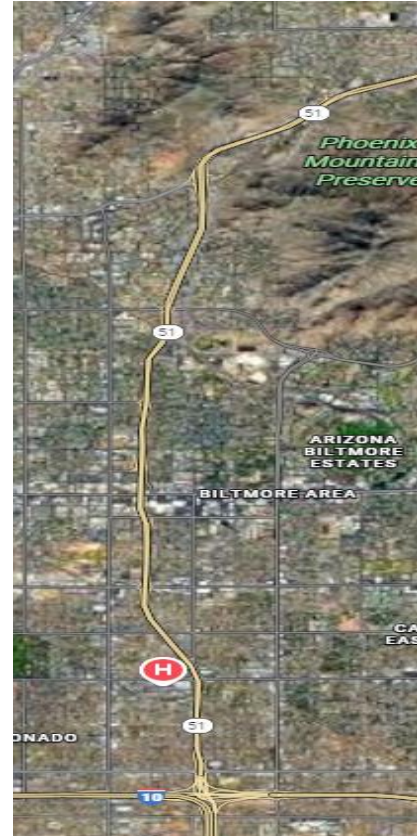

Thank You

