

State Transportation Board District Administrator's Report March 20, 2026





Randy Everett - Senior District Administrator

Sara Howard - Assistant District Engineer

Recently Completed District Projects



I-17 Mill & Fill - SR74 to Anthem

ARIZONA
DEPARTMENT OF
TRANSPORTATION

Construction Completion: 100%

Contract Time Completed: 100%

Contractor: Fann Construction

Completion: January 2026



SR101 - Princess to Shea

ARIZONA
— DEPARTMENT OF —
TRANSPORTATION

Construction Completion: 100%

Contract Time Completed: 100%

Contractor: FNF Construction

Completion: January 2026



Ongoing District Projects



SR101 - I-17 to 75th Ave



Construction Completion: 68%

Contract Time Completed: 58%

Contractor: Coffman Specialties

Estimated Completion: March 2027



SR202 Santan - SR101 to Val Vista



Construction Completion: 67%

Contract Time Completed: 63%

Contractor: Sundt/CS Construction JV

Estimated Completion: February 2027



I-10 - Gila River Bridge



Construction Completion: 88%

Contract Time Completed: 80%

Contractor: Pulice Construction

Estimated Completion: August 2026



US60X - Sossaman to Meridian



Construction Completion: 90%

Contract Time Completed: 99%

Contractor: Pulice Construction

Estimated Completion: May 2026



I-17/SR303 to 51st Ave



Construction Completion: 5%

Contract Time Completed: 4%

Contractor: Pulice Construction

Estimated Completion: July 2028




SR 51 - I-10 to Shea Diamond Grind

Construction Completion: 5%

Contract Time Completed: 5%

Contractor: Emery Sapp & Sons Construction

Estimated Completion: October 2026

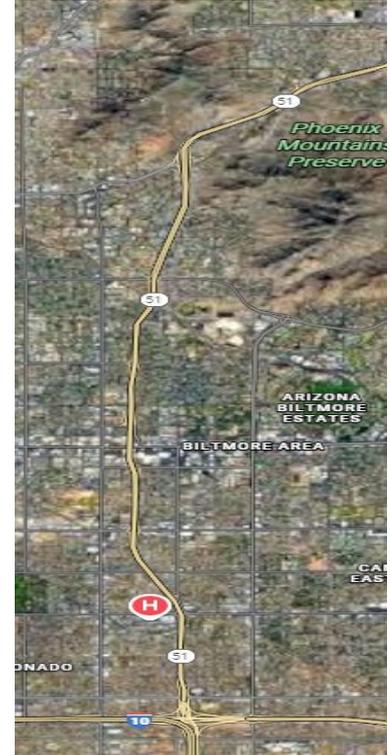

Upcoming District Projects



I-10/SR101 DHOV



Construction Completion: 0%

Contract Time Completed: 0%

Contractor: FNF Construction

Estimated Completion: Mid 2028



SR 303 - Van Buren to MC 85

Construction Completion: 0%

Contract Time Completed: 0%

Contractor: Pulice Construction

Estimated Completion: Early 2029



I-10 - Jackrabbit Trail TI




Construction Completion: 0%

Contract Time Completed: 0%

Contractor: Sundt Construction

Estimated Completion: Late 2027

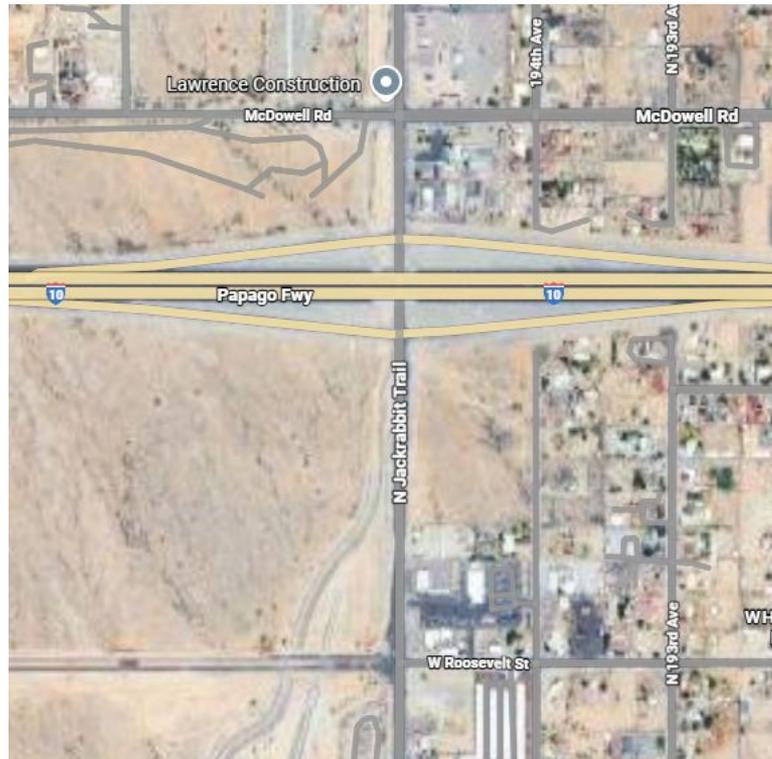

Thank You

