


Item 8 – State Engineer’s Report: March 20, 2026 Summary of Active and Finalized Projects

- **113 projects under construction** **\$2.6 B**
- **4 projects finalized in February** **\$18.7 M**
- **Fiscal Year to date:** **65 projects finalized**

Current Statewide District Updates



Northwest District Current Projects

West Kingman TI

I-40, MP 48.87 - MP 51.56

Contractor: Fisher Sand & Gravel Co.

63% Complete, 67% Time Spent

Cane Springs

US 93, MP 105.99 - MP 109.42

Contractor: FNF Construction, Inc.

71% Complete, 50% Time Spent

Placeritas Creek to Date Creek

US 93, MP 156.0 - MP 172.0

Contractor: FNF Construction, Inc.


34% Complete, 7% Time Spent

Morristown to Wickenburg

US 60, MP 110.59 - MP 121.5

Contractor: Sunland Asphalt & Construction, LLC

79% Complete, 52% Time Spent

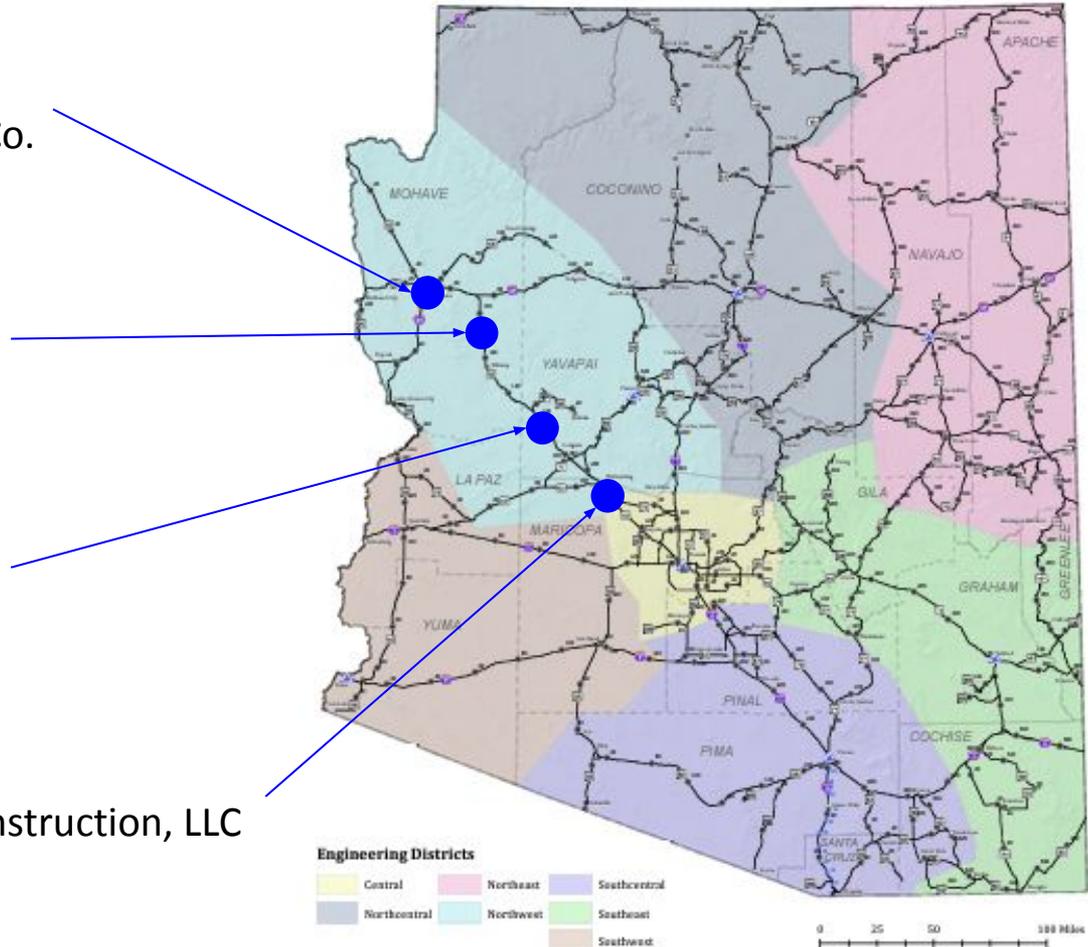

Northcentral District Current Projects



Tuba City - East
US 160 MP 322-335
Contractor: Sunland Asphalt
0% Complete, 0% Time Spent


I-40 to Pipeline Rd
SR 64 MP 186 - 205
Contractor: Fann Contracting
0% Complete, 0% Time Spent

I-40 Broadband: CA State Line to I-17/I-40 T.I.
Contractor: EX² Technologies, LLC
82% Complete, 75% Time Spent

Willard Springs Wildlife Overpass
I-17 MP 327
Contractor: SEMA Construction
70% Complete, 69% Time Spent

Two Guns to Dennison
I-40 MP 229 - 240
Contractor: Fann Contracting
44% Complete, 33% Time Spent

SR 87 Pavement/ADA Upgrades
SR 87 MP 250 - 255
Contractor: Paveco
28% Complete, 24% Time Spent

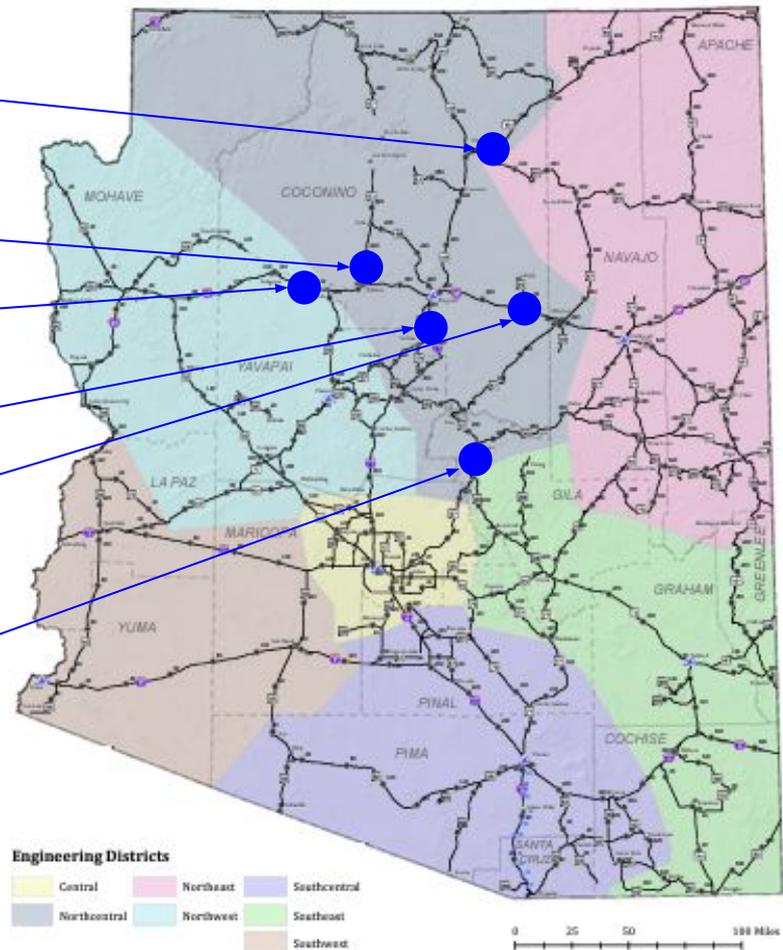

Northeast District Current Projects

Perkins Valley Bridge Widening

I-40 MP 283.4

Contractor: SEMA Construction
27% Complete, 24% Time Spent

Little Colorado River Bridge Rehab

SR77 MP 388.5

Contractor: FNF Construction
0% Complete, 0% Time Spent

MP8 - Phoenix Park Wash


SR 377 MP 8 - 13

Contractor: SEMA Construction
0% Complete, 0% Time Spent

24th West St to US 191

US180 MP 366.9 to 368.9

Contractor: WW Clyde
0% Complete, 0% Time Spent

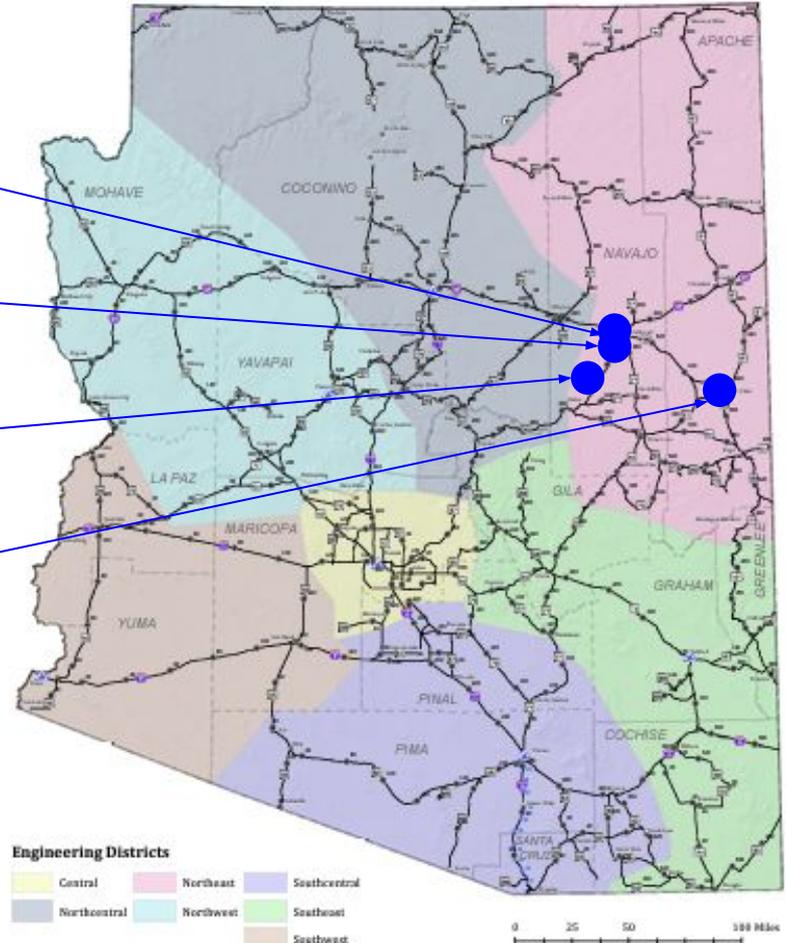

Southwest District Current Projects

Statewide Road Weather Info System Upgrade

Contractor: Roadway Electric, LLC.
30% Complete, 22% Time Spent

State Route 72, NW Bouse-SE Bouse

MP 20.44-30 Pav. Pres.
Contractor: FNF Construction, Inc.
97% Complete, 68% Time Spent

US 95, Imperial Dam Rd-Aberdeen Rd

New Roundabouts & Pav. Pres.
Contractor: Fisher Sand & Gravel, Co.
4% Complete, 12% Time Spent

City of Yuma, Pedestrian Hybrid Beacons

Pedestrian Hybrid Beacon Installation
Contractor: DPE Construction, Inc.
1% Complete, 41% Time Spent

City of Yuma, Pedestrian Hybrid Beacons


Pedestrian Hybrid Beacon Installation
Contractor: AJP Electric, Inc.
0% Complete, 31% Time Spent

Statewide Port of Entry Signing

Contractor: Hawk Contracting, LLC.
66% Complete, 55% Time Spent

Cesar Chavez Boulevard

Roadway Expansion
Contractor: DPE Construction, Inc.
2% Complete, 3% Time Spent

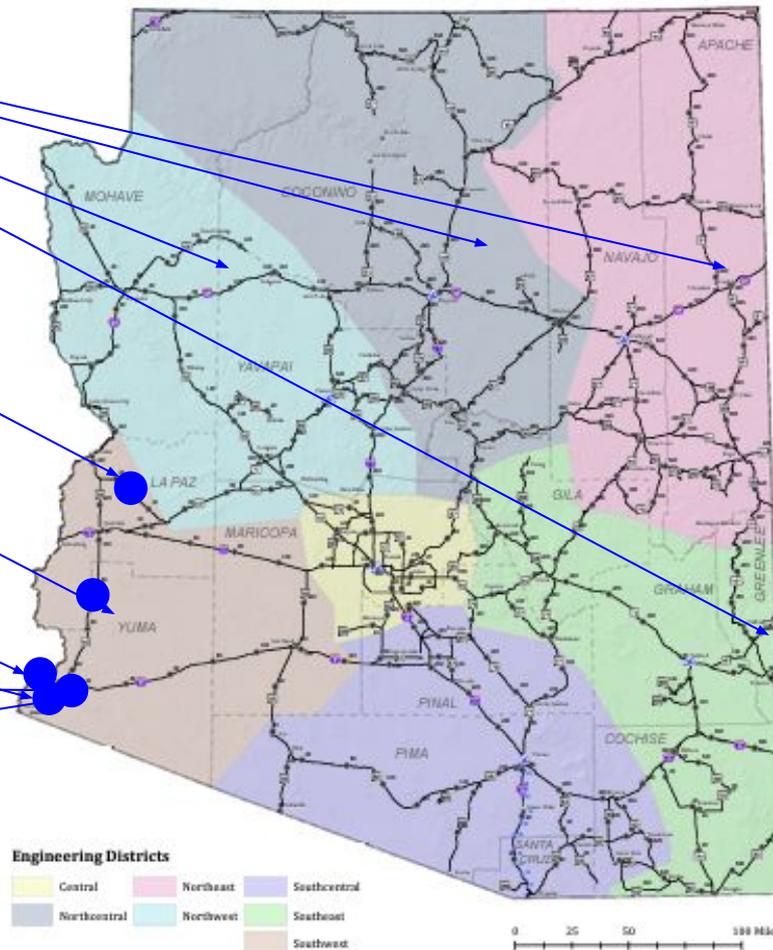

Southcentral District Current Projects

I-10 Widening Ina to Ruthrauff

MP 248.03-MP 251.85

Contractor: Granite Construction

93% Complete, 109% Time Spent

I-10 Kino to Country Club

MP 262-MP 264.5 (Design Build)

Contractor: Sundt/Jacobs

39% Complete, 24% Time Spent

I-19 Irvington TI (Design), MP 60.83

Final Design Firm: WSP

Advertised: January 2026

Construction: Summer of 2026

Amole RR OP EB/WB Deck Replacement

MP 292

Contractor: Granite Construction


35% Complete, 85% Time Spent

SR-83 Black Oak Drive to Lower Elgin Road

MP 31-MP 29

Contractor: Granite Construction

90% Complete, 90% Time Spent

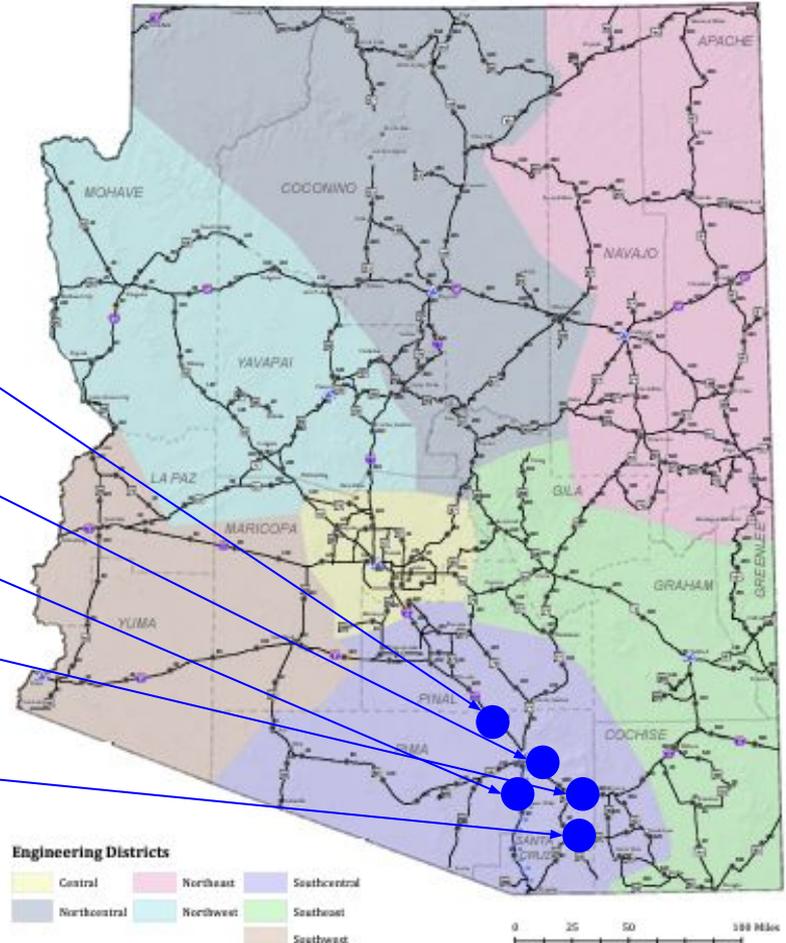

Southeast District Current Projects

Queen Creek Bridge

US 60, MP 227.7

Contractor: Ames Construction
49% Complete, 48% Time Spent

Waterfall Canyon Bridge


US 60, MP 229.5

Contractor: Ames Construction
55% Complete, 48% Time Spent

Medicine Way Rd to MP 275.7

US 70, MP 274.5 to MP 275.7

Contractor: SEMA Construction
43% Complete, 50% Time Spent

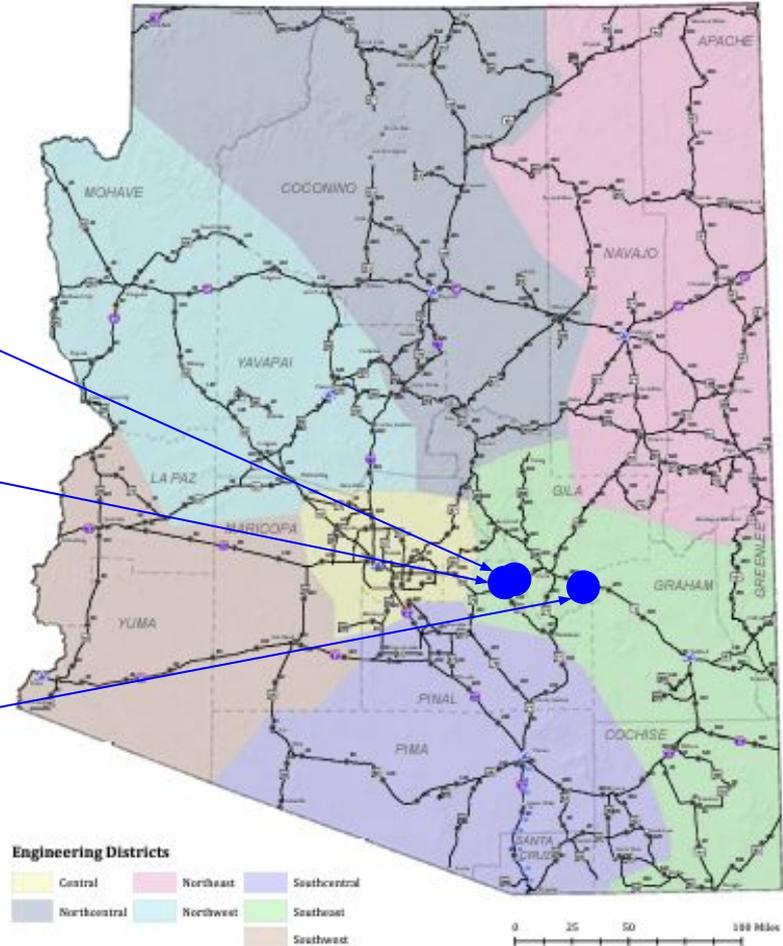

Central District Current Projects


I-17/SR303 to 51st Ave
New system ramps and widening in Phoenix
5% Complete 4% Time Spent

SR101 I-17 to 75th Ave
Loop 101 Expansion in Phoenix/Glendale
68% Complete 58% Time Spent

US 60X Sossaman to Meridian
Old US60 Highway
90% Complete 99% Time Spent

SR202 Val Vista to SR101L
Loop 202 Expansion in Chandler/Gilbert
67% Complete 63% Time Spent

I-10 Gila River Bridge
Bridge Replacement
88% Complete 80% Time Spent

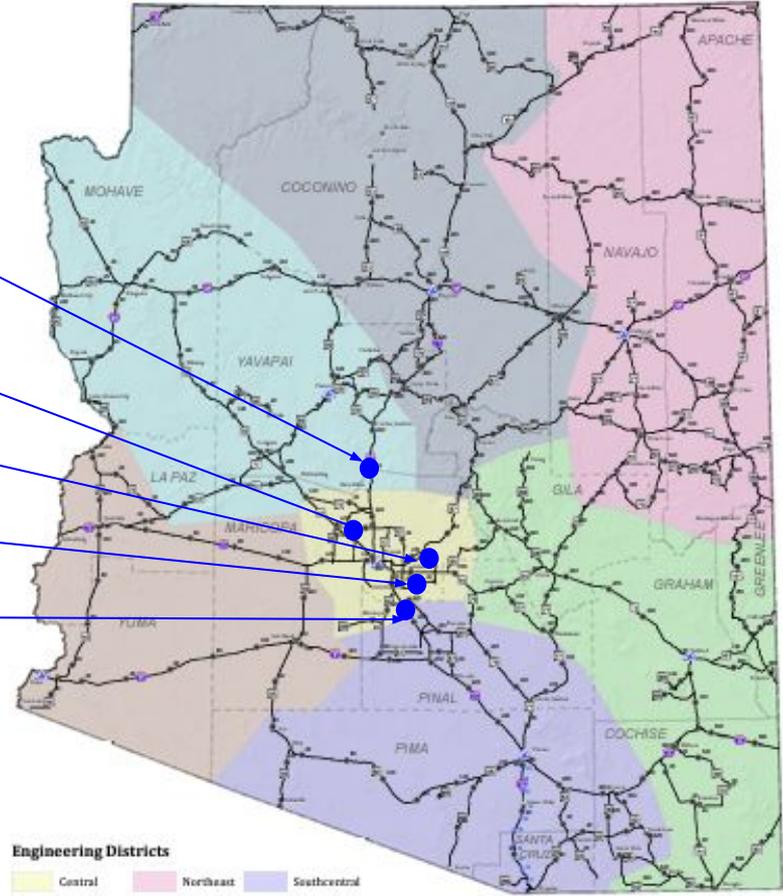

Item 9 - New Construction Contracts

Item	Highway	Low bid	Department Estimate	Difference	Percent
3d	US 60	\$22,471,538	\$25,182,415	(\$2,710,877)	-10.8%
3e	SR 85	\$11,347,477	\$11,824,017	(\$476,540)	-4.0%
3f	SR202L	\$1,053,741	\$1,092,830	(\$39,089)	-3.6%
3g	SR 260	\$76,247,869	\$81,652,728	(\$5,404,859)	-6.6%
3h	LOCAL	\$1,652,538	\$1,767,215	(\$114,677)	-6.5%
3i	LOCAL	\$620,000	\$605,637	\$14,363	2.4%

Continued on Next Slide-

Item 9 - New Construction Contracts Contd.



9a	I 17	\$2,480,223	\$1,794,577	\$685,646	38.2%
9b	I 40	\$8,125,969	\$9,717,949	(\$1,591,980)	-16.4%
9c	SR 101L	\$192,382,454	\$233,352,335	(\$40,969,881)	-17.6%
9d	SR 101L	\$3,972,000	\$7,139,524	(\$3,167,524)	-44.4%
9e	SR 303L	\$322,698,631	\$379,926,602	(\$57,227,971)	-15.1%
9f	SR 80	\$4,099,454	\$3,707,070	\$392,384	10.6%
9g	LOCAL	\$1,533,160	\$2,002,631	(\$469,471)	-23.4%
9h	LOCAL	\$2,171,287	\$1,784,947	\$386,341	21.6%
TOTAL THIS MONTH		\$615,983,585	\$723,451,215	(\$107,467,630)	-14.9%
TOTAL FY TO DATE		\$1,333,712,707	\$1,523,510,454	(\$189,797,747)	-12.5%

Monthly Totals for Construction Contracts

Month	No. of Bids	Awards	Low bid	Department Estimate	Difference	Percent
Jul-25	12	12	\$62,784,082	\$68,010,729	(\$5,226,647)	-7.7%
Aug-25	10	9	\$38,937,658	\$46,892,438	(\$7,954,780)	-17.0%
Sep-25	11	11	\$169,185,208	\$170,035,931	(\$850,723)	-0.5%
Oct-25	9	7	\$80,181,265	\$99,560,293	(\$19,379,028)	-19.5%
Nov-25	8	6	\$167,617,583	\$210,051,276	(\$42,433,693)	-20.2%
Dec-25	15	15	\$169,640,875	\$167,272,777	\$2,368,098	1.4%
Jan-26	1	1	\$6,174,827.07	\$6,971,897.85	(\$797,071)	-11.4%
Feb-26	7	8	\$23,207,624.00	\$31,263,897.00	(\$8,056,273)	-25.8%
Mar-26	14	13	\$615,983,585.00	\$723,451,215.00	(\$107,467,630)	-14.9%
Fiscal YTD	87	82	\$1,333,712,707	\$1,523,510,454	(\$189,797,747)	-12.5%

District 6



**SYSTEM PRESERVATION
I 17: SR 179 TI OP
F031401C**

Item 9a

Low Bid	\$2,480,223
Department Estimate	\$1,794,577
Difference	\$685,646
% Difference	38.2%

Recommendation: AWARD


Reasons for Difference:

- Phased Construction
- Nighttime Work
- Forest Service Requirements

DocuSign Envelope ID: 064602F7-05B7-46E6-940D-AA4A6337E39F

LOCATION MAP

LOCATION: SR 179 TI OP SB
PROJECT NO: 017 YV 298 F0314 01C
FEDERAL ID: 017-B-(236)T

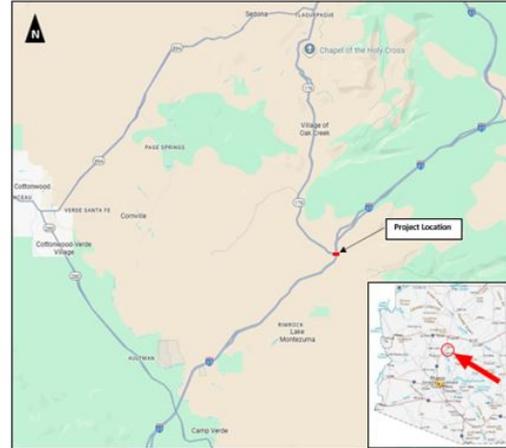

District 6

**PAVEMENT REHABILITATION
I 40: US 93 TO SILVER SPRINGS ROAD
F063701C**

Item 9b




Low Bid	\$8,125,969
Department Estimate	\$9,717,949
Difference	-\$1,591,980
% Difference	-16.4%

Recommendation: AWARD

Reasons for Difference:

- Shorter Hauling Distance
- Higher Production Rate
- Contractor Owned Equipment

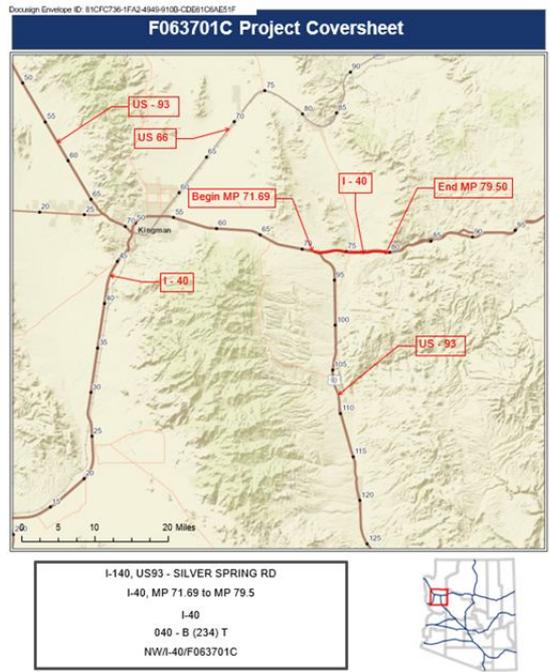

District 1

**SYSTEM ENHANCEMENT
SR 101: SR 101 & I 10 SYSTEM TI
F047501C**

Item 9c




Low Bid	\$192,382,454
Department Estimate	\$233,352,335
Difference	-\$40,969,881
% Difference	-17.6%

Recommendation: AWARD

Reasons for Difference:

- Higher Production Rates
- Shorter Hauling Distance
- Contractor Owned Falsework & Forms

Design Envelope ID: 154014DC-CD11-4262-9A85-C112200CABF

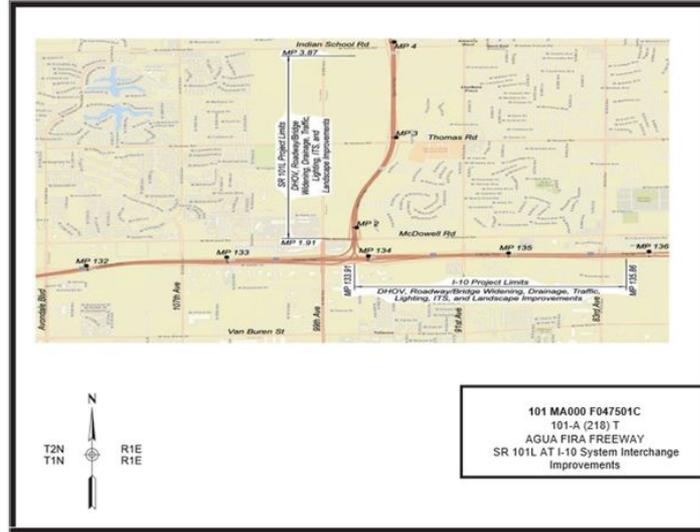

District 1

**SYSTEM ENHANCEMENT
SR 101L: PRINCESS DR - SHEA BLVD.
F077001C**

Item 9d



Low Bid	\$3,972,000
Department Estimate	\$7,139,524
Difference	-\$3,167,524
% Difference	-44.4%

Recommendation: AWARD

Reasons for Difference:

- Higher Production Rates
- Contractor Owned Equipment



District 1

NEW FACILITIES
SR 303L: MC 85 TO VAN BUREN STREET
H687001C

Item 9e



Low Bid	\$322,698,631
Department Estimate	\$379,926,602
Difference	-\$57,227,971
% Difference	-15.1%

Recommendation: AWARD

Reasons for Difference:

- Contractor owned Specialized Forms & Equipment
- Subcontracted Work
- Material Cost



District 3

**CAPACITY ADDITIONS
CITY OF DOUGLAS: SR 80 CHINO RD EXT. - PHASE 2
T058101C**

Item 9f




Low Bid	\$4,099,454
Department Estimate	\$3,707,070
Difference	\$392,384
% Difference	10.6%

Recommendation: AWARD
Reasons for Difference:

- Remote Location
- Higher Hauling Costs

CHINO ROAD EXTENSION PHASE II: 9TH ST - SR 80

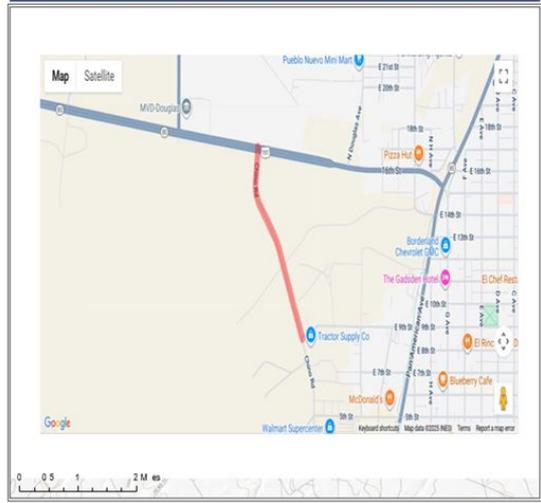

0000 CH DGS T0581 01 C
DGS-0(205) T
CITY OF DOUGLAS
CH/NO ROAD EXTEN S/ION PHASE //I
9TH ST - SR 80



**ROADWAY RECONSTRUCTION & MULTI USE
PATHWAY**

Item 9g

District 3

**TOWN OF HUACHUCA CITY
SKYLINE DR: SR90 TO LANDFILL ENTRANCE
SKYLINE DR: GILA AVE. TO EDGEWOOD ST.
T050301C & T050401C**





Low Bid	\$1,533,160
Department Estimate	\$2,002,631
Difference	-\$469,471
% Difference	-23.4%

Recommendation: AWARD

Reasons for Difference:

- Higher Production Rates
- Lower Material Costs
- Lower Disposal Costs

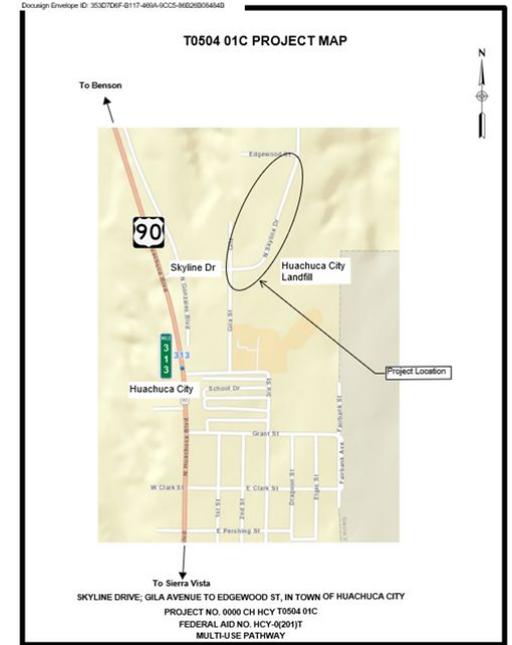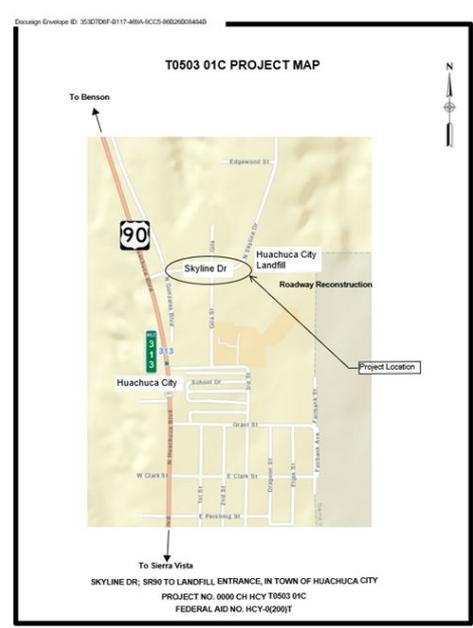

District 6


**BRIDGE REHABILITATION
YAVAPAI COUNTY: CROOKTON RD AT BNSF RR OP
T059201C**

Item 9h

Low Bid	\$2,171,287
Department Estimate	\$1,784,947
Difference	\$386,341
% Difference	21.6%

Recommendation: AWARD
Reasons for Difference:

- RR Track Protection Needed
- Work over RR
- Existing Site Conditions

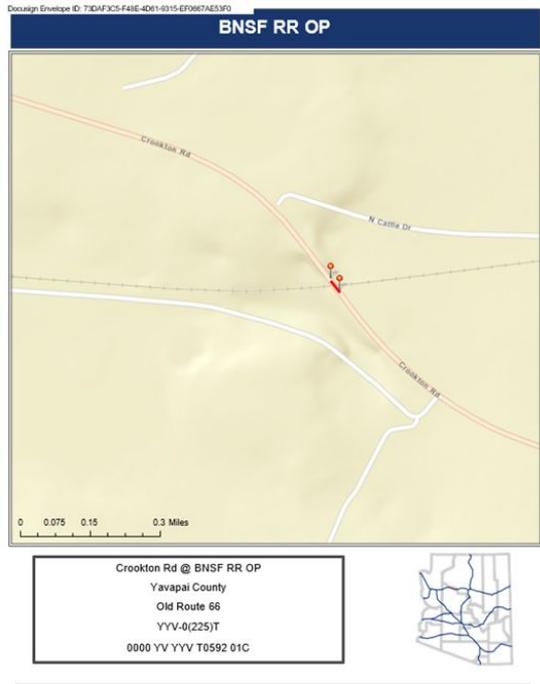

CONSENT ITEMS

District 1

**PAVEMENT REHABILITATION
US 60: 85 TH AVE. TO I 17
F067501C**

Item 3d



Low Bid	\$22,471,538
Department Estimate	\$25,182,415
Difference	-\$2,710,877
% Difference	-10.8%

Recommendation: AWARD
Reasons for Difference:

- Removal Work



District 2

**SYSTEM PRESERVATION
SR 85: ELOTA AVE. TO MP 60.0
F067201C**


Item 3e



Low Bid	\$11,347,477
Department Estimate	\$11,824,017
Difference	-\$476,540
% Difference	-4.0%

Recommendation: AWARD
Reasons for Difference:

- Removal Work

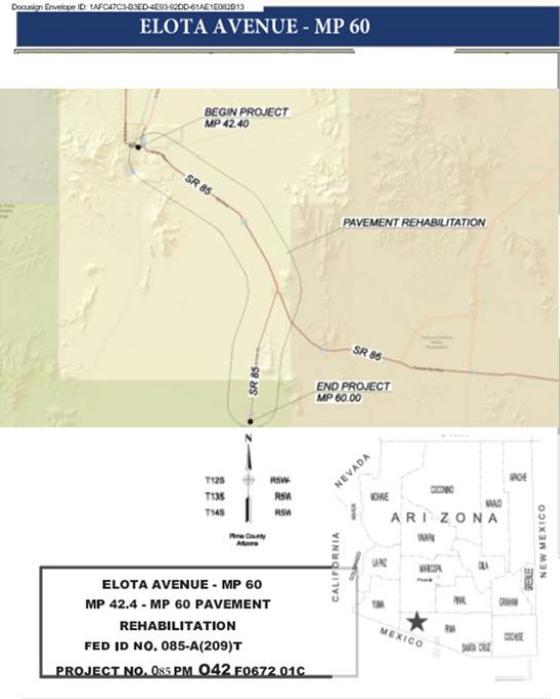

District 1

**LIGHTING FIXTURE REPLACEMENT
SR 202L: MCCLINTOCK DR TO 48TH ST
F074301C**

Item 3f




Low Bid	\$1,053,741
Department Estimate	\$1,092,830
Difference	-\$39,089
% Difference	-3.6%

Recommendation: AWARD
Reasons for Difference:

- Mobilization Costs

202 MA 050 F0743 01 C
202-C(212T)
SR 101(PRICE) to 48th ST

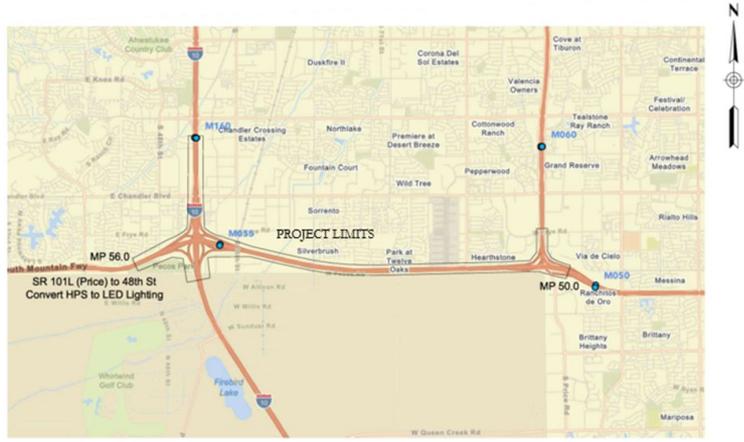

District 4




**CAPACITY ADDITIONS
SR 260: LION SPRINGS
F013901C**

Item 3g

Low Bid	\$76,247,869
Department Estimate	\$81,652,728
Difference	-\$5,404,859
% Difference	-6.6%

Recommendation: AWARD
Reasons for Difference:

- Removal Work
- Material Prices

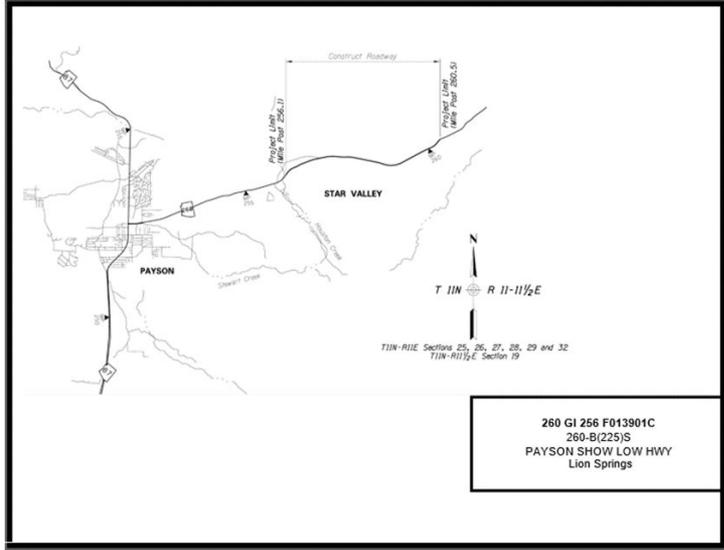

**INTERSECTION IMPROVEMENTS
YUMA COUNTY
COUNTY 14TH ST & AVE C
COUNTY 14TH ST & AVE G
T043601C & T044101C**

Item 3h

District 6




Low Bid	\$1,652,538
Department Estimate	\$1,767,215
Difference	-\$114,677
% Difference	-6.5%


Recommendation: AWARD
Reasons for Difference:

- Asphalt Placement
- Pole Installation
- Electrical Work

Design Envelope ID: 18D5964B-4D3A-4C3C-872A-896E442318E3

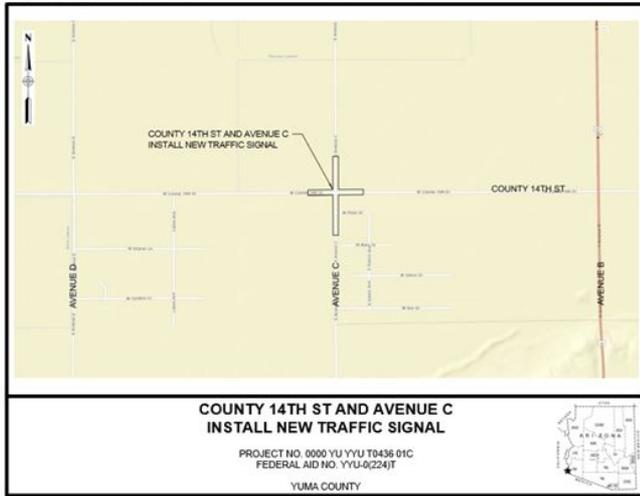

Design Envelope ID: 18D5964B-4D3A-4C3C-872A-896E442318E3

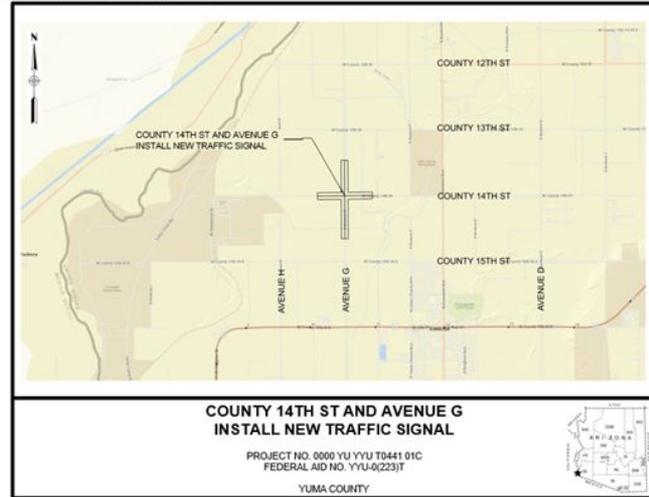

**SYSTEM ENHANCEMENT
YUMA COUNTY
PATHWAY - AVENUE B TO AVENUE C/W
T052201C**

Item 3i

District 6



Low Bid	\$620,000
Department Estimate	\$605,637
Difference	\$14,363
% Difference	2.4%

Recommendation: POSTPONE ACTION

Reasons for Difference:

- Removal Work

