


ITEM 9

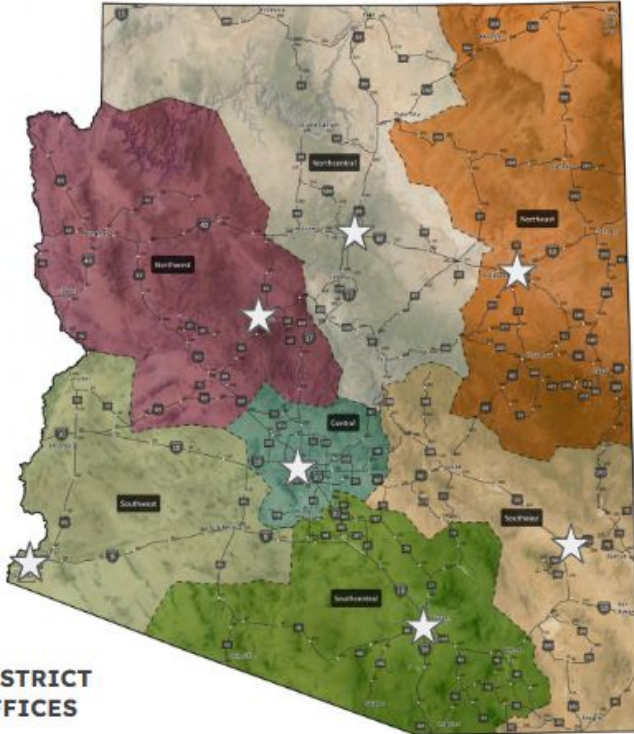

★ DISTRICT
OFFICES

State Engineer's Report June 2026

Summary of Active and Finalized Projects

117 Projects Under Construction

\$3.3 Billion

7 Projects Finalized in June


\$25.6 Million

Fiscal Year to Date

87 Projects Finalized



★ **DISTRICT OFFICE**

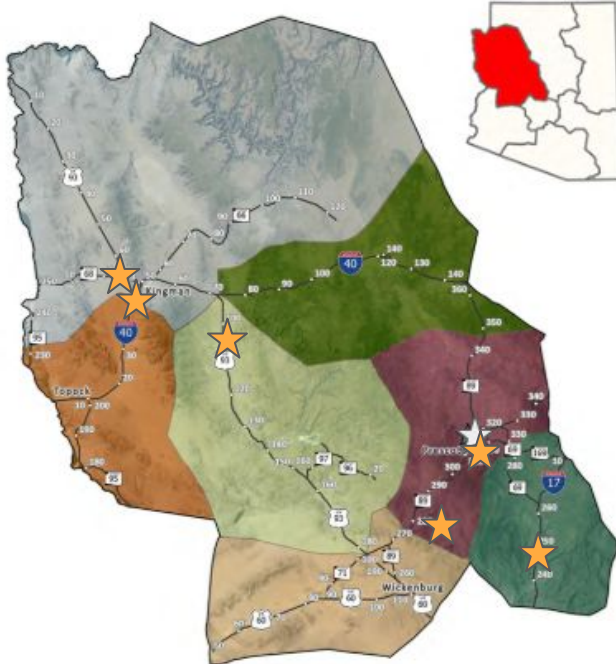

Rancho Santa Fe Parkway TI

I-40, MP 55.85 - MP 57.27

Contractor: Pulice Construction, Inc.

98% Complete, 78% Time Spent

I-40/US 93 West Kingman TI

I-40, MP 48.87 - MP 51.56

Contractor: Fisher Sand & Gravel Co.

78% Complete, 74% Time Spent

Cane Springs

US 93, MP 105.99 - MP 109.42

Contractor: FNF Construction, Inc.

81% Complete, 64% Time Spent

Wash Bridge at Walnut Grove Rd

Yavapai County Off-System Bridge Project

Contractor: C.S. Construction, Inc

58% Complete, 77% Time Spent

Lee Blvd to E of Walker Road

SR 69, MP 292.58 to MP 293.43

Contractor: Asphalt Paving & Supply, Inc.


67% Complete, 79% Time Spent

Sunset Point to SR 69

I-17, MP 252 to MP 262

Contractor: Asphalt Paving & Supply, Inc.

6% Complete, 18% Time Spent

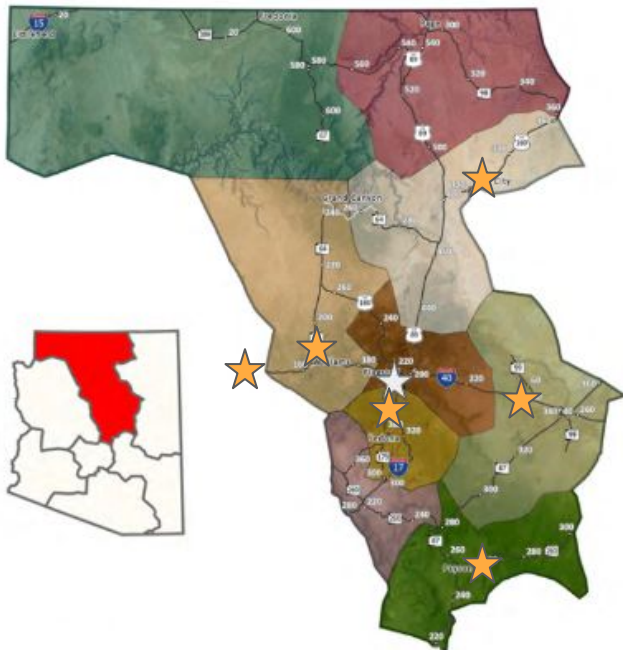

☆ **DISTRICT OFFICE**

Lions Springs Section

SR 260, MP 256.2 - MP 260.1

Contractor: AMES Construction, Inc.

7% Complete, 5% Time Spent

Tuba City - East

US 160 , MP 321.8 - MP 335

Contractor: Sunland Asphalt & Construction, LLC

43% Complete, 42% Time Spent

Willard Springs Wildlife Overpass

I-17, MP 327

Contractor: SEMA Construction, Inc.

80% Complete, 96% Time Spent

Two Guns to Dennison

I-40, MP 229 - MP 240

Contractor: Fann Contracting, Inc

77% Complete, 60% Time Spent

I-40 to Pipeline Rd

SR 64, MP 185.8 to MP 205

Contractor: Fann Contracting, Inc


52% Complete, 24% Time Spent

Broadband: CA State Line to I-17/I-40 T.I.

US 60, MP 110.59 to MP 121.50

Contractor: eX2 Technology, LLC

97% Complete, 93% Time Spent

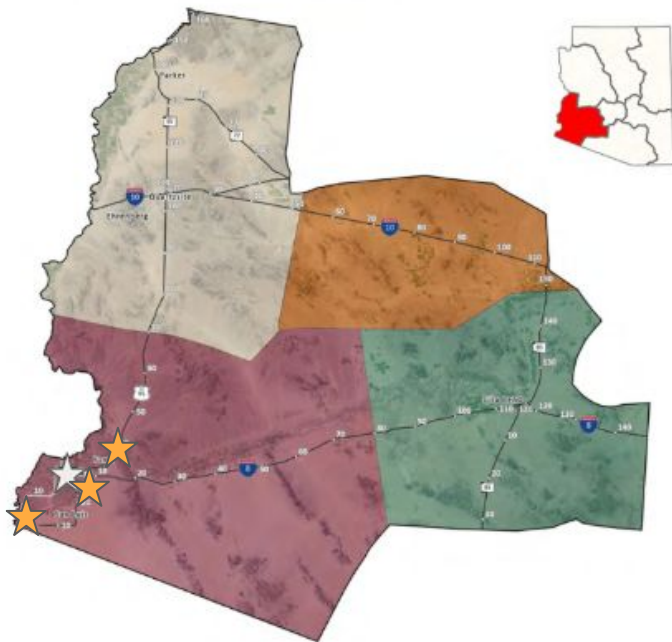

US 95, Imperial Dam Road-Aberdeen Road

US 95, MP 43.40-55

Contractor: Fisher Sand & Gravel, Co.

33% Complete, 34% Time Spent

Cesar Chavez Boulevard

City of San Luis

Contractor: DPE Construction, Inc.

12% Complete, 17% Time Spent


County 11th Street & Avenue G

Yuma County

Contractor: DPE Construction, Inc.

1% Complete, 34% Time Spent

★ **DISTRICT OFFICE**

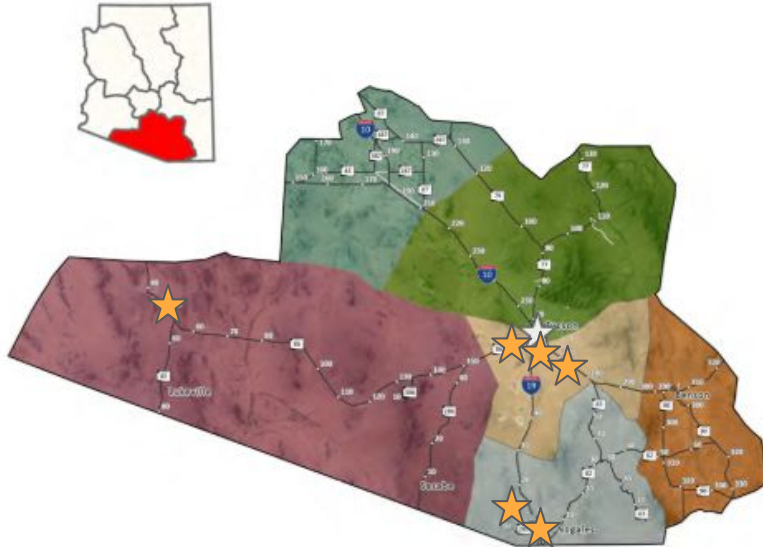

Elota Avenue

SR 85, MP 42.40 - MP 60

Contractor: Granite Construction

7% Complete, 22% Time Spent

Kino to Country Club (DB)

I-10, MP 262 - MP 264.5

Design Builder: Sundt/Jacobs

57% Complete, 34% Time Spent

Irvington Road TI

I-19, MP 60.83

Contractor: AMES Construction

0% Complete, 0% Time Spent

Amole Railroad Overpass

I-10, MP 292

Contractor: Granite Construction

79% Complete, 100% Time Spent

Western Avenue TI

I-19, MP 0.94 - MP 1.26

Contractor: Granite Construction


48% Complete, 104% Time Spent

Pena Blanca Lake

SR 289, MP 0 - MP 10.83

Contractor: Granite Construction

90% Complete, 92% Time Spent

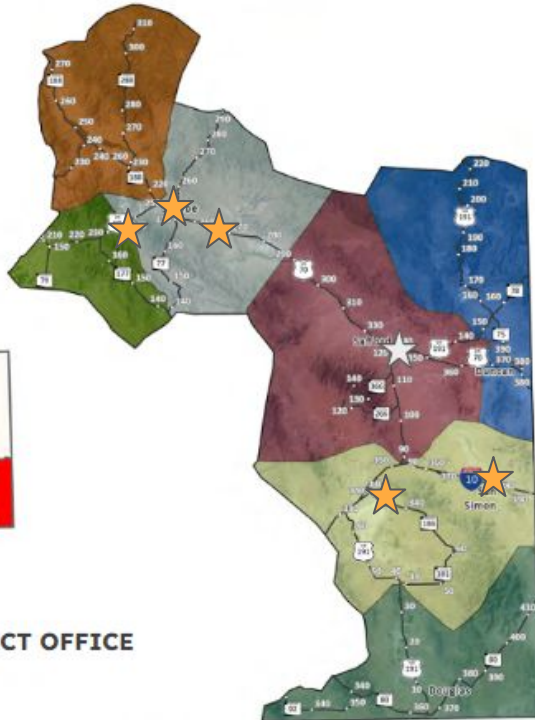

★ DISTRICT OFFICE

Cochise Railroad Overpass

US 191, MP 62.5 - MP 63.2

Contractor: SEMA Construction, Inc.

13% Complete, 24% Time Spent

Jct SB I-10 to MP 356.49

I-10 , MP 345.5 - MP 356.49

Contractor: FNF Construction, Inc.

72% Complete, 35% Time Spent

W Santee St to US 70

US 60 MP 250 - MP 252.05

Contractor: Granite Construction Company

92% Complete, 87% Time Spent

Queen Creek Bridge

US 60, MP 227 - MP 228

Contractor: Ames Construction, Inc


68% Complete, 55% Time Spent

Medicine Way Rd - MP 275.7

US 70, MP 274 to MP 275.7

Contractor: SEMA Construction, Inc

78% Complete, 99% Time Spent

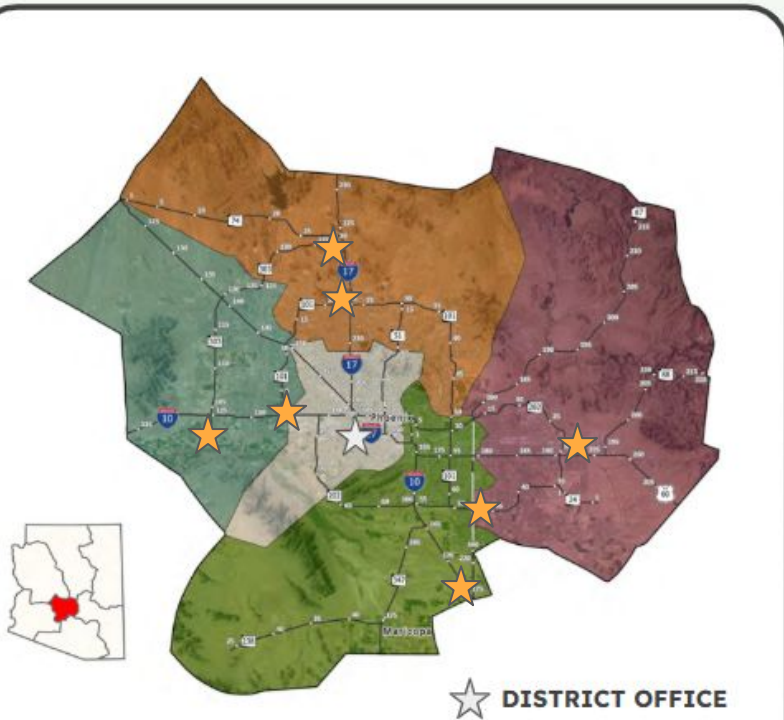

I-17/SR303 to 51st Ave

New system ramps and widening in Phoenix

MP 136.6 - MP 139

Contractor: Pulice Construction, Inc.

18% Complete, 23% Time Spent

SR101 I-17 to 75th Ave

Loop 101 Expansion in Phoenix/Glendale

MP 16.53 - MP 25.1

Contractor: Coffman Specialties, Inc

72% Complete, 85% Time Spent

I-10 Gila River Bridge

Bridge Replacement

MP 161.00 - MP 172.80

Contractor: Pulice Construction, Inc.

94% Complete, 99% Time Spent

I-10/SR101

New DHOV Ramp

MP 1.19 - MP 3.87

Contractor: FNF Construction, Inc

4% Complete, 9% Time Spent

SR 202 Val Vista to SR101L

Loop 202 Expansion in Chandler/Gilbert

MP 40.8 - MP 50.60

Contractor: Sundt Construction, Inc. (JV) C S Construction, Inc.

77% Complete, 83% Time Spent

SR303 MC85 to Van Buren

New Freeway

MP 99.14 - MP 103.23

Contractor: Pulice Construction, Inc.

3% Complete, 3% Time Spent

ITEM 10 - New Construction Contracts

Item	Highway	Low bid	Department Estimate	Difference	Percent
10a	SR 85	\$2,681,299	\$3,366,078	(\$684,779)	-20.3%
10b	I8 & I10	\$2,162,708	\$2,817,176	(\$654,468)	-23.2%
TOTAL THIS MONTH		\$4,844,007	\$6,183,254	(\$1,339,247)	-21.7%
TOTAL FY TO DATE		\$4,844,007	\$6,183,254	(\$1,339,247)	-21.7%

Monthly Totals for Construction Contracts

Month	No. of Bids	Awards	Low bid	Department Estimate	Difference	Percent
Jul-26	3	2	\$4,844,007	\$6,183,254	(\$1,339,247)	-21.7%
Fiscal YTD	3	2	\$4,844,007	\$6,183,254	(\$1,339,247)	-21.7%

District 1

DRAINAGE IMPROVEMENTS
SR 85: GILA BEND - LUKEVILLE HIGHWAY
F083301C

ITEM 10a

Low Bid	\$2,681,299
Department Estimate	\$3,366,078
Difference	-\$684,779
% Difference	-20.3%

Recommendation: AWARD
Reasons for Difference:


- Production Rate
- Material Costs

Recommendation: AWARD
Reasons for Difference:

- Production Rate
- Material Costs

- Recommendation: AWARD**
Reasons for Difference:

 - Production Rate
 - Material Costs

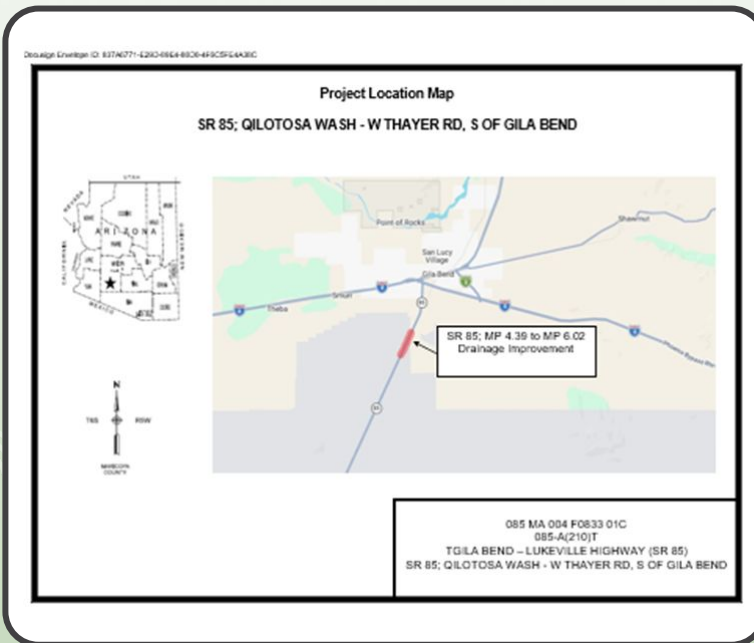

STATEWIDE

**INSTALL DMS & QUEUE WARNING SYSTEM
I-8 & I-10: GILA BEND QUARTZSITE EHRENBERG
F072501C**


ITEM 10b

Low Bid	\$2,162,708
Department Estimate	\$2,817,176
Difference	-\$654,468
% Difference	-23.2%

Recommendation: AWARD

Reasons for Difference:

- Production Rate
- Material Costs
- Subcontractor Quotes

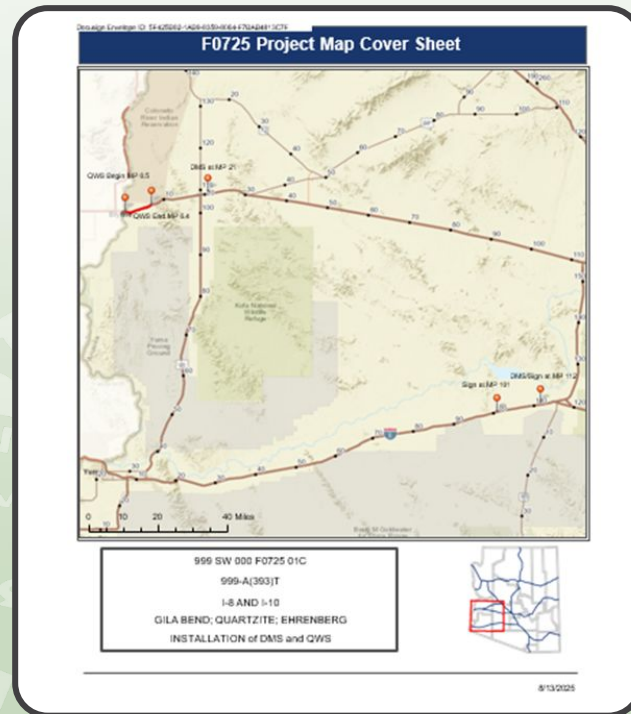

District 6

ADA IMPROVEMENT
SR 89: PRESCOTT - ASH FORK HWY
F076801C

ITEM 10c

Low Bid	\$795,500
Department Estimate	\$890,516
Difference	-\$95,016
% Difference	-10.7%

Recommendation: POSTPONE

