


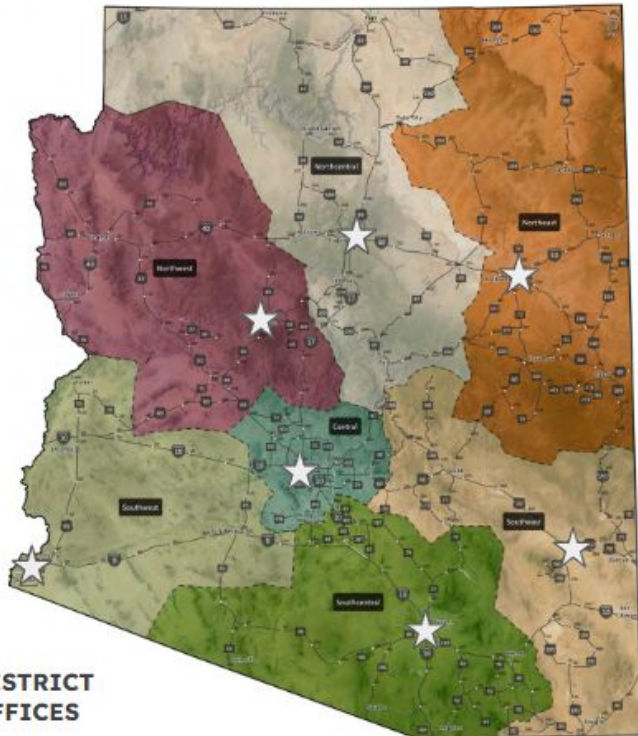

★ **DISTRICT
OFFICES**

State Engineer's Report July 2026

Summary of Active and Finalized Projects

117 Projects Under Construction

\$3.3 Billion

4 Projects Finalized in July


\$44.7 Million

Fiscal Year to Date

4 Projects Finalized



★ **DISTRICT OFFICE**

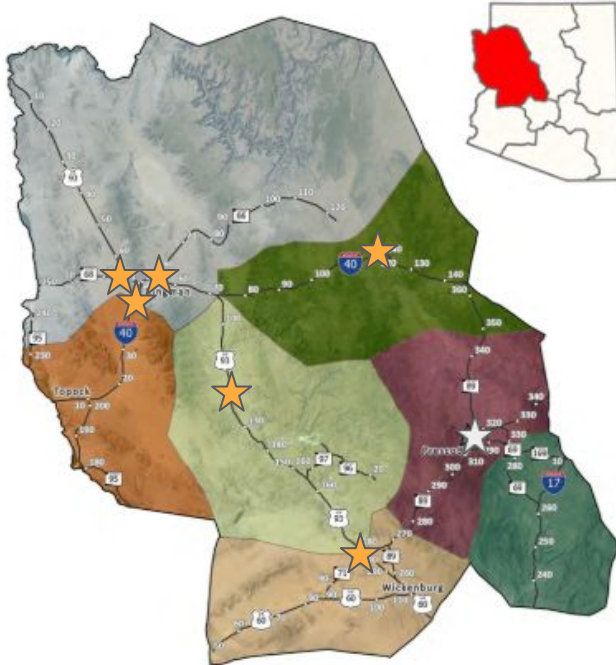

Rancho Santa Fe Parkway TI

I-40, MP 55.85 - MP 57.27

Contractor: Pulice Construction, Inc.

94% Complete, 97% Time Spent

I-40/US 93 West Kingman TI

I-40, MP 48.87 - MP 51.56

Contractor: Fisher Sand & Gravel Co.

79% Complete, 83% Time Spent

Cane Springs

US 93, MP 105.99 - MP 109.42

Contractor: FNF Construction, Inc.

83% Complete, 71% Time Spent

Cholla Canyon to E Old Wikieup Hillside

US 93, MP 127.7 - MP 131.0

Contractor: FNF Construction, Inc.

3% Complete, 2% Time Spent

MP 175.5-177, S of Date Creek

US 93, MP 175.5 to MP 177.0

Contractor: Fann Contracting, Inc.


3% Complete, 2% Time Spent

Markham to Seligman TI EB

I-40, MP 107.7 to MP 122.7

Contractor: Fann Contracting, Inc.

19% Complete, 13% Time Spent

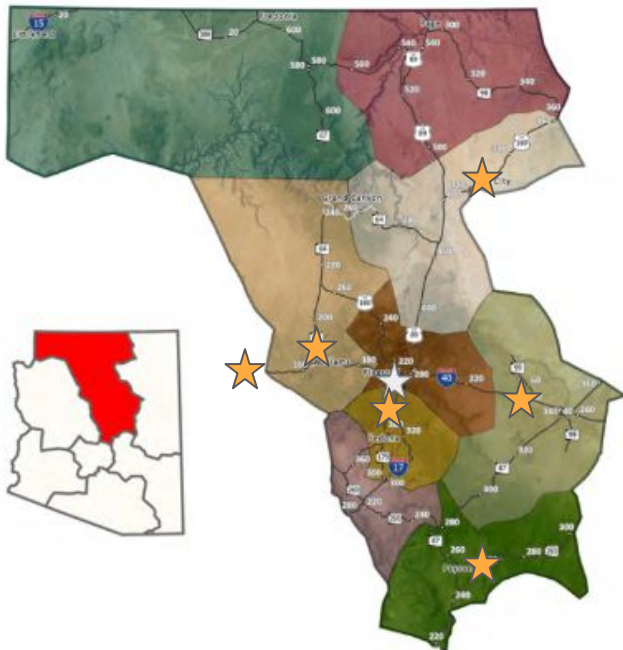

☆ DISTRICT OFFICE

Lions Springs Section

SR 260, MP 256.2 - MP 260.1

Contractor: AMES Construction, Inc.

11% Complete, 9% Time Spent

Tuba City - East

US 160 , MP 321.8 - MP 335

Contractor: Sunland Asphalt & Construction, LLC

77% Complete, 65% Time Spent

Willard Springs Wildlife Overpass

I-17, MP 327

Contractor: SEMA Construction, Inc.

85% Complete, 91% Time Spent

Two Guns to Dennison

I-40, MP 229 - MP 240

Contractor: Fann Contracting, Inc

96% Complete, 73% Time Spent

I-40 to Pipeline Rd

SR 64, MP 185.8 to MP 205

Contractor: Fann Contracting, Inc


73% Complete, 30% Time Spent

Broadband: CA State Line to I-17/I-40 T.I.

I-40, MP 110.59 to MP 121.50

Contractor: eX2 Technology, LLC

99% Complete, 99% Time Spent

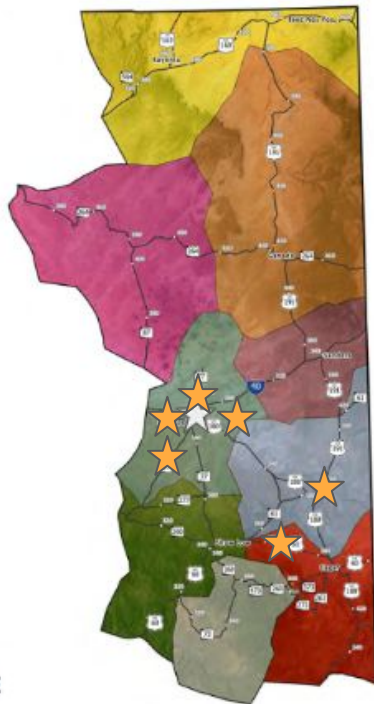

SR 61 to Wildcat Creek

US 60 MP 352.8 - MP 369.3

Contractor: WW Clyde & Co

97% Complete, 98% Time Spent

Perkins Valley TI

I-40 , MP 283.0

Contractor: SEMA Construction, Inc.

62% Complete, 54% Time Spent

Little Colorado River Bridge

SR 77, MP 388.0 - MP 389.0

Contractor: FNF Construction, Inc.

96% Complete, 97% Time Spent

MP 8 to Phoenix Park Wash

SR 377, MP 8 - MP 13

Contractor: SEMA Construction, Inc.

32% Complete, 64% Time Spent

24th West to US 191

US 180, MP 366.92 to MP 368.93

Contractor: WW Clyde & Co


39% Complete, 68% Time Spent

**Little Colorado River & Five Mile Wash
Bridges**

US 180, MP 309.05 to MP 310.6

Contractor: Vastco, Inc

0% Complete, 0% Time Spent

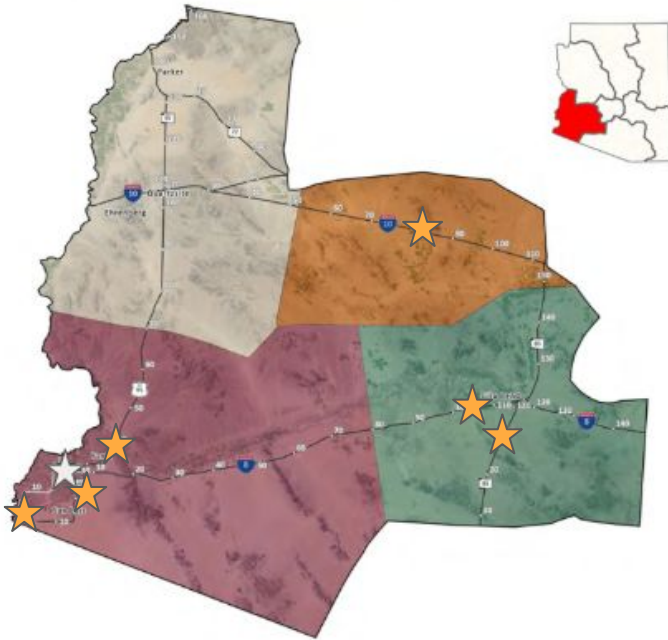

US 95, Imperial Dam Road-Aberdeen Road

US 95, MP 43.40-55

Contractor: Fisher Sand & Gravel, Co.

38% Complete, 41% Time Spent

SR 85 South, Qilotosa Wash-Thayer Road

SR 85S, MP 4.39-6.02

Contractor: J. Banicki Construction, Inc.

0% Complete, 0% Time Spent

I-10, Burnt Well Rest Area Truck Parking

I-10, MP 86

Contractor: Rummel Construction, Inc.

0% Complete, 0% Time Spent

I-8 & I-10 DMS & Queue Warning System

I-8, MP 100.7-112.7 & I-10, MP 0.5-6.4 & 20.9

Contractor: C S Construction, Inc.

0% Complete, 0% Time Spent

Cesar Chavez Boulevard

City of San Luis

Contractor: DPE Construction, Inc.

13% Complete, 20% Time Spent


County 11th Street & Avenue G

Yuma County

Contractor: DPE Construction, Inc.

11% Complete, 37% Time Spent

★ **DISTRICT OFFICE**

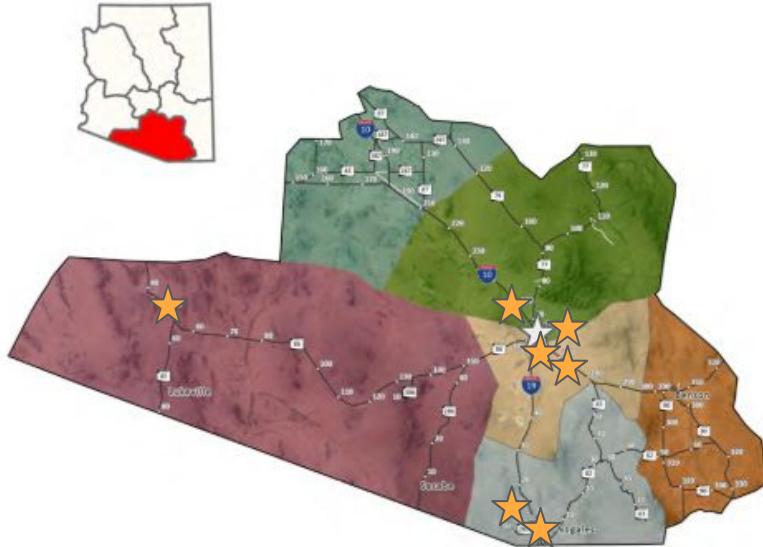

Elota Avenue

SR 85, MP 42.40 - MP 60

Contractor: Granite Construction

15% Complete, 33% Time Spent

Kino to Country Club (DB)

I-10, MP 262 - MP 264.5

Design Builder: Sundt/Jacobs

61% Complete, 38% Time Spent

Irvington Road TI

I-19, MP 60.83

Contractor: AMES Construction

3% Complete, 4% Time Spent

Amole Railroad Overpass

I-10, MP 292

Contractor: Granite Construction

96% Complete, 107% Time Spent

Western Avenue TI

I-19, MP 0.94 - MP 1.26

Contractor: Granite Construction


58% Complete, 127% Time Spent

Pena Blanca Lake

SR 289, MP 0 - MP 10.83

Contractor: Granite Construction

92% Complete, 92% Time Spent

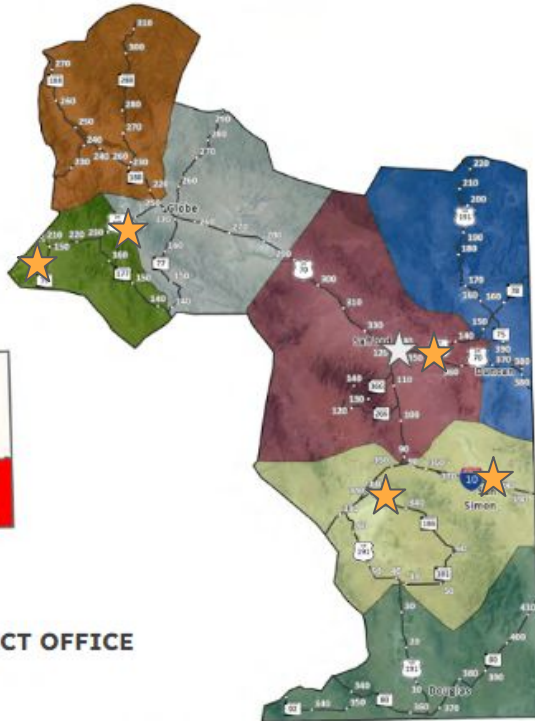

★ **DISTRICT OFFICE**

Cochise Railroad Overpass

US 191, MP 62.5 - MP 63.2

Contractor: SEMA Construction, Inc.

13% Complete, 29% Time Spent

Jct SB I-10 to MP 356.49

I-10, MP 345.5 - MP 356.49

Contractor: FNF Construction, Inc.

90% Complete, 46% Time Spent

North of Florence to Queen Valley

SR 79, MP 140 - MP 148

Contractor: SEMA Construction, Inc.

11% Complete, 12% Time Spent

Queen Creek Bridge

US 60, MP 227 - MP 228

Contractor: Ames Construction, Inc.


72% Complete, 57% Time Spent

US 70 to MP 134

US 191, MP 132.04 - MP 133.57

Contractor: Show Low Construction, Inc.

13% Complete, 7% Time Spent

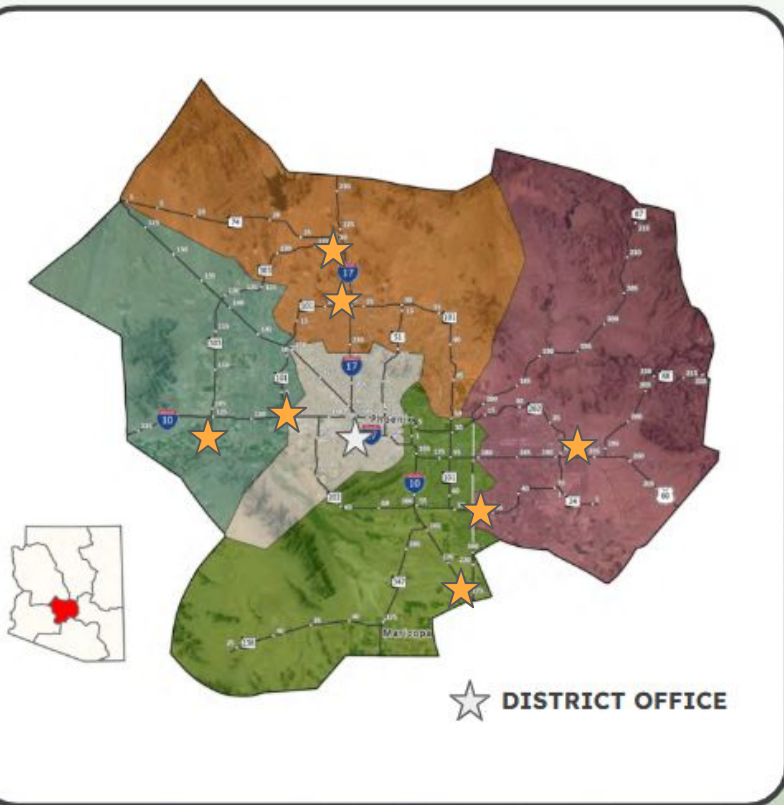

I-17/SR303 to 51st Ave

New system ramps and widening in Phoenix
MP 136.6 - MP 139
Contractor: Pulice Construction, Inc.
29% Complete, 22% Time Spent

SR101 I-17 to 75th Ave

Loop 101 Expansion in Phoenix/Glendale
MP 16.53 - MP 25.1
Contractor: Coffman Specialties, Inc.
88% Complete, 75% Time Spent

I-10 Gila River Bridge

Bridge Replacement
MP 161.00 - MP 172.80
Contractor: Pulice Construction, Inc.
103% Complete, 98% Time Spent

I-10/SR101

New DHOV Ramp
MP 1.19 - MP 3.87
Contractor: FNF Construction, Inc.
15% Complete, 8% Time Spent

SR202 Val Vista to SR101L

Loop 202 Expansion in Chandler/Gilbert
MP 40.8 - MP 50.60
Contractor: Sundt Construction, Inc. (JV) C S Construction, Inc.
88% Complete, 81% Time Spent

SR303 MC85 to Van Buren

New Freeway
MP 99.14 - MP 103.23
Contractor: Pulice Construction, Inc.
6% Complete, 6% Time Spent

ITEM 9 - New Construction Contracts

ITEM	HIGHWAY	LOW BID	DEPARTMENT ESTIMATE	DIFFERENCE	PERCENT
3e	I 40	\$33,840,994	\$36,534,075	(\$2,693,081)	-7.4%
3f	LOCAL	\$612,910	\$620,518	(\$7,608)	-1.2%
3g	LOCAL	\$3,981,070	\$4,130,696	(\$149,627)	-3.6%
3h	LOCAL	\$291,488	\$285,569	\$5,919	2.1%
3i	LOCAL	\$1,478,023	\$1,481,762	(\$3,739)	-0.3%
3j	US 70	\$8,917,160	\$10,187,569	(\$1,270,409)	-12.5%

ITEM 9 - New Construction Contracts, Cont'd.

ITEM	HIGHWAY	LOW BID	DEPARTMENT ESTIMATE	DIFFERENCE	PERCENT
9a	I 10	\$29,165,818	\$35,513,285	(\$6,347,467)	-17.9%
9b	I 40	\$1,007,234	\$1,413,141	(\$405,907)	-28.7%
9c	LOCAL	\$652,682	\$565,218	\$87,464	15.5%
9d	SR 89	\$795,500	\$890,516	(\$95,016)	-10.7%
TOTAL THIS MONTH		\$80,742,878	\$91,622,349	(\$10,879,470)	-11.9%
TOTAL FY TO DATE		\$85,586,885	\$97,805,603	(\$12,218,718)	-12.5%

Monthly Totals for Construction Contracts

MONTH	NO. OF BIDS	AWARDS	LOW BID	DEPARTMENT ESTIMATE	DIFFERENCE	PERCENT
Jul-26	3	2	\$4,844,007	\$6,183,254	(\$1,339,247)	-21.7%
Aug-26	10	10	\$80,742,878	\$91,622,349	(\$10,879,471)	-11.9%
Fiscal YTD	13	12	\$85,586,885	\$97,805,603	(\$12,218,718)	-12.5%

District 6

SYSTEM PRESERVATION
I-10: CA BORDER - DOME ROCK ROAD
F076201C


ITEM 9a

Low Bid	\$29,165,818
Department Estimate	\$35,513,285
Difference	-\$6,347,467
% Difference	-17.9%

Recommendation: AWARD

Reasons for Difference:

- Contractor Owned Aggregate
- Company Owned Equipment
- Proximity of Material Source

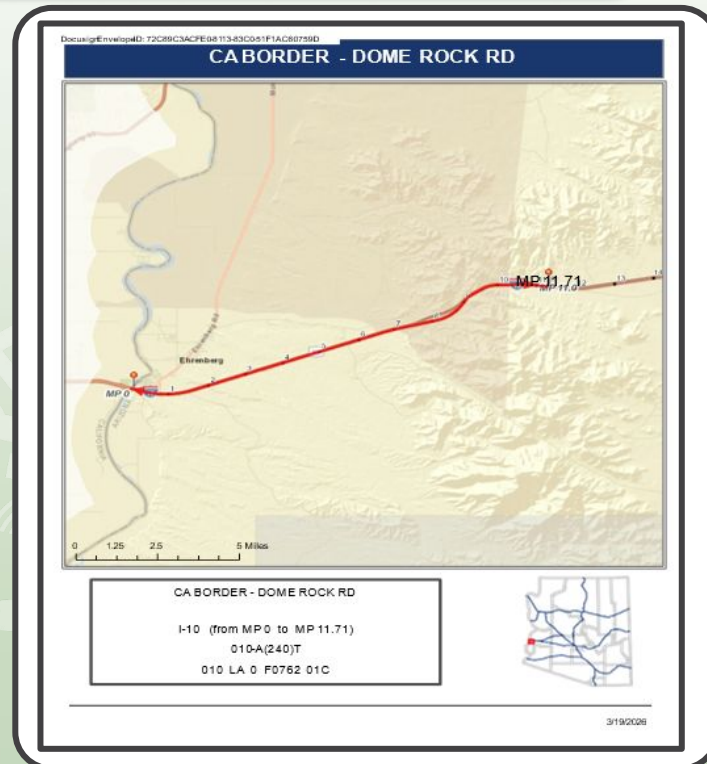

District 5

**FENCE REPLACEMENT
I-40: PARKS - BELLEMONT
F078901C**


ITEM 9b

Low Bid	\$1,007,234
Department Estimate	\$1,413,141
Difference	-\$405,907
% Difference	-28.7%

Recommendation: AWARD

Reasons for Difference:

- Higher Production Rate

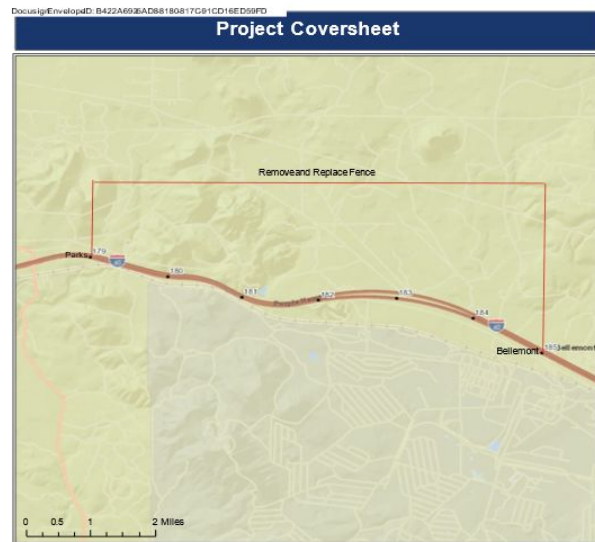

F078901C
State Highway Ash Fork - Flagstaff Hwy
Parks - Bellemont
040-C(233)




District 2

**BRIDGE REHABILITATION
TOWN OF ORO VALLEY: HONEYBEE WASH AT
RANCHO VISTOSO
T068601C**

ITEM 9c

Low Bid	\$652,682
Department Estimate	\$565,218
Difference	\$87,464
% Difference	15.5%

Recommendation: POSTPONE

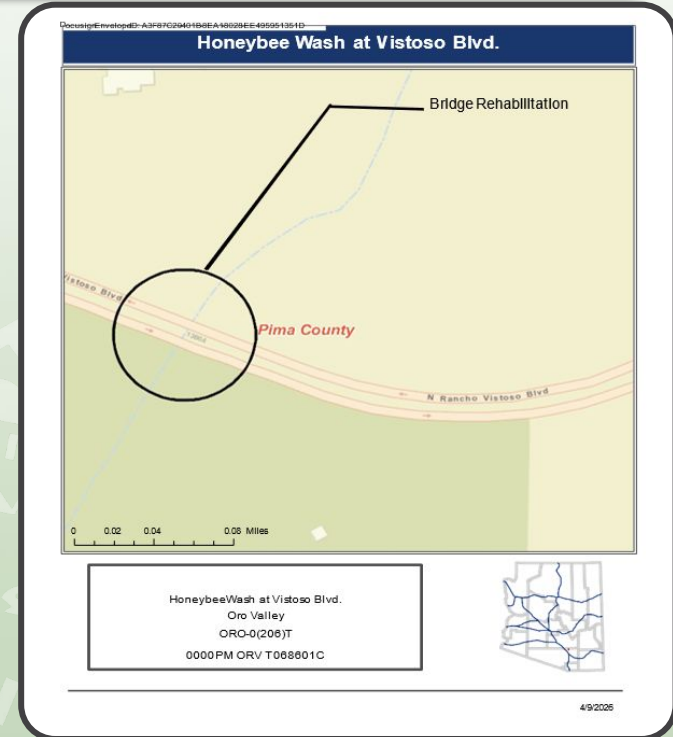

District 6


ADA IMPROVEMENT
SR 89: PRESCOTT - ASH FORK HWY
F076801C

Low Bid	\$795,500
Department Estimate	\$890,516
Difference	-\$95,016
% Difference	-10.7%

Recommendation: AWARD

Reasons for Difference:

- Removal Work
- Lower Material Cost

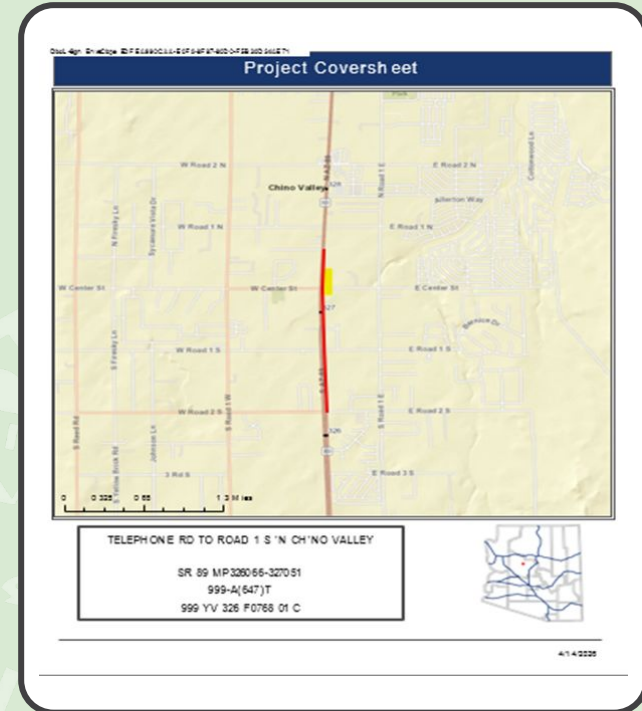

ITEMS
3e-3j

CONSENT AGENDA ITEMS

District 5

SYSTEM PRESERVATION I-40: MCCARRELL - QUERINO F075401C

ITEM 3e

Low Bid	\$33,840,994
Department Estimate	\$36,534,075
Difference	-\$2,693,081
% Difference	-7.4%

Recommendation: AWARD

Reasons for Difference:

- Removal Work
- Lower Material Price



District 1

CONDUIT, PULL BOXES & FIBER OPTIC CABLE
CITY OF SURPRISE: WADDELL RD.
LITCHFIELD RD. - BULLARD AVE.
T058801C

ITEM 3f

Low Bid	\$612,910
Department Estimate	\$620,518
Difference	-\$7,608
% Difference	-1.2%

Recommendation: AWARD

Reasons for Difference:

- Electrical Conduit/Directional Drill



District 7

ROAD WIDENING
CITY OF CASA GRANDE: THORNTON ROAD
SR 84 PETERS RD
T053001C

ITEM 3g

Low Bid	\$3,981,070
Department Estimate	\$4,130,696
Difference	-\$149,627
% Difference	-3.6%

Recommendation: AWARD

Reasons for Difference:

- Removal Work



THORNTONROAD; SR 84 - PETERSRD
SR 84 - PETERSRD
THORNTONROAD
CDS -CSG-0(214)T
000 PN T0530 01C



District 6

**BUS PULL OUTS INSTALLATION
CITY OF YUMA: AVENUE A AT 16TH STREET
T054201C**


ITEM 3h

Low Bid	\$291,488
Department Estimate	\$285,569
Difference	\$5,919
% Difference	2.1%

Recommendation: AWARD

Reasons for Difference:

- Construction Survey/Layout
- Location

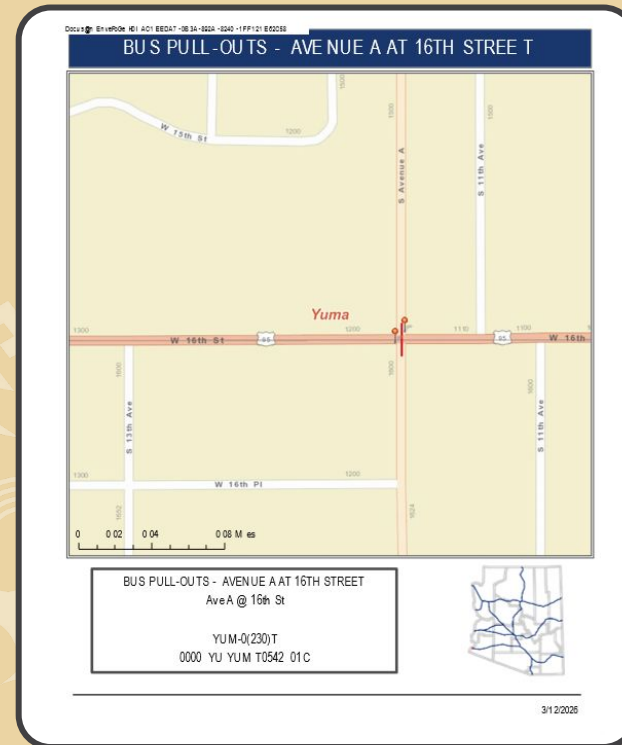

Low Bid	\$1,478,023
Department Estimate	\$1,481,762
Difference	-\$3,739
% Difference	-0.3%

Reasons for Difference:

- Removal Work



District 4

SYSTEM PRESERVATION
US 70: COTTONWOOD WASH - REAY LN
F075901C

ITEM 3j

Low Bid	\$8,917,160
Department Estimate	\$10,187,569
Difference	-\$1,270,409
% Difference	-12.5%

Recommendation: AWARD

Reasons for Difference:

- Removal Work
- Lower Material Cost

