

Transportation Board Meeting

Maricopa

Central Construction District

December 2015

Projects Under Construction

26 Projects Under Construction

- 25 Federally Funded Projects
 - 13 LPA Projects (Local Public Agency)
- 1 State Funded Project


Overall Construction Cost - \$ 313 Million

- Total Earned - \$255 Million

Major Projects - East Valley

US 60, Meridian Rd. TI


- Contract Amount - \$8.0M
- Completed Contract Amount - \$8.2M
- Substantially Complete

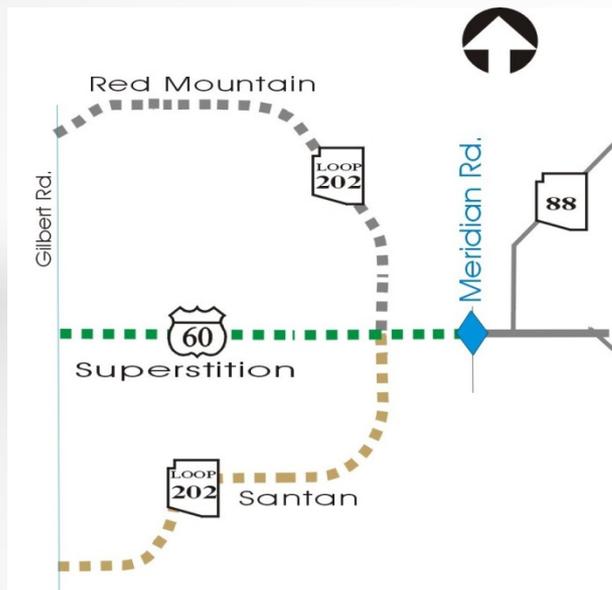

Major Projects - East Valley

L202, L101 – Broadway Rd.


- Contract Amount - \$109.2M
- Completed Contract Amount - \$113.6M
- 99% Complete

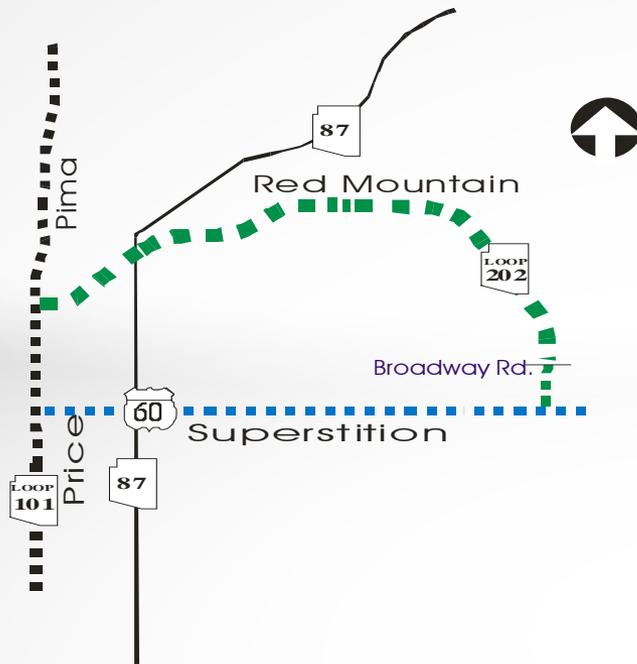

Major Projects - East Valley

L101, L202 – Shea Blvd.



- Contract Amount - \$72.7M
- Completed Contract Amount - \$50.9M
- 70% Complete

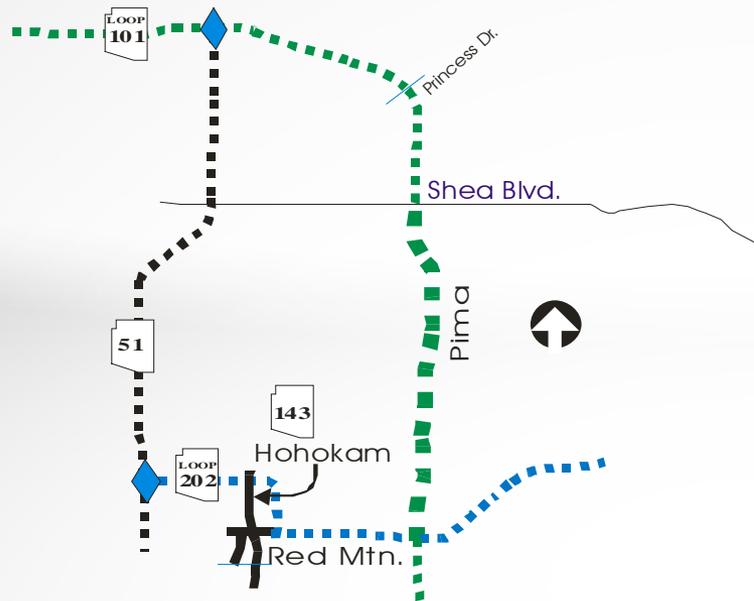

Major Projects – Northeast Valley

SR 51 / L101, Black Mountain Blvd.


- Contract Amount - \$17.8M
- Completed Contract Amount - \$16.5M
- 92% Complete

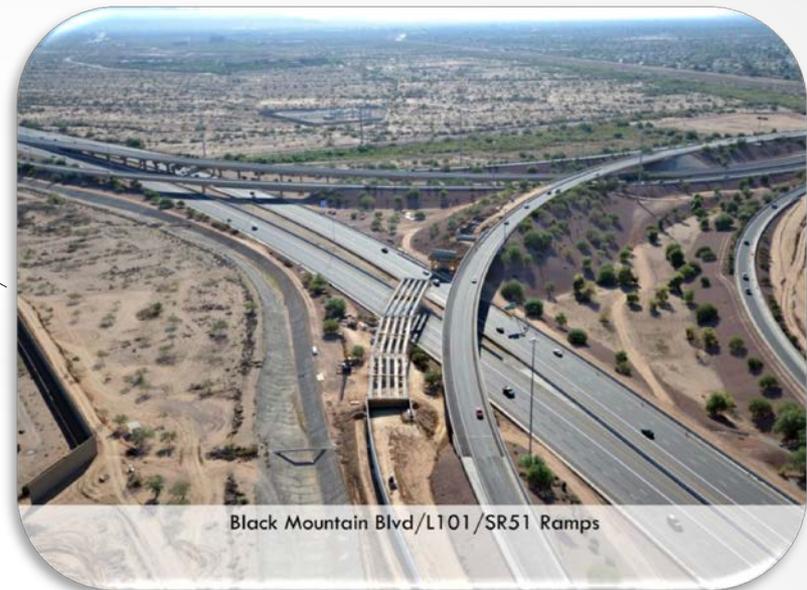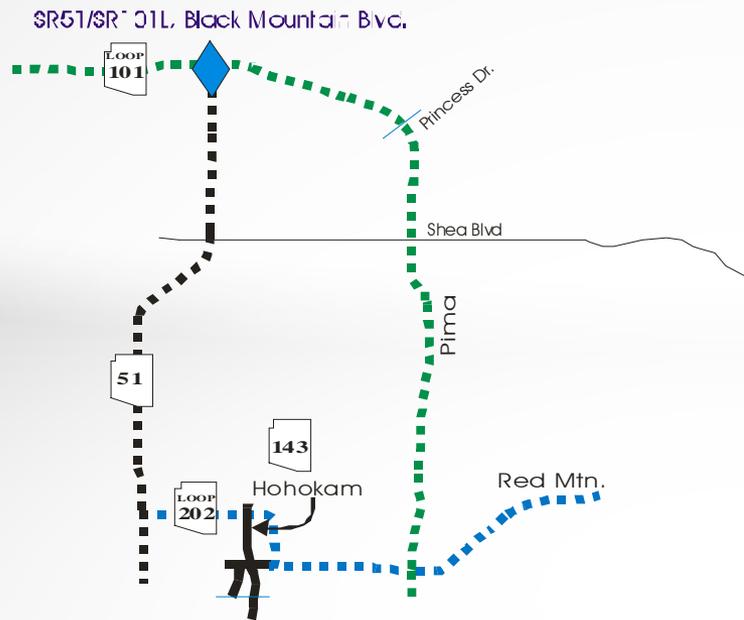

Major Projects - West Valley

L303 / US 60 TI


- Contract Amount - \$46.1M
- Completed Contract Amount - \$32.4M
- 70% Complete

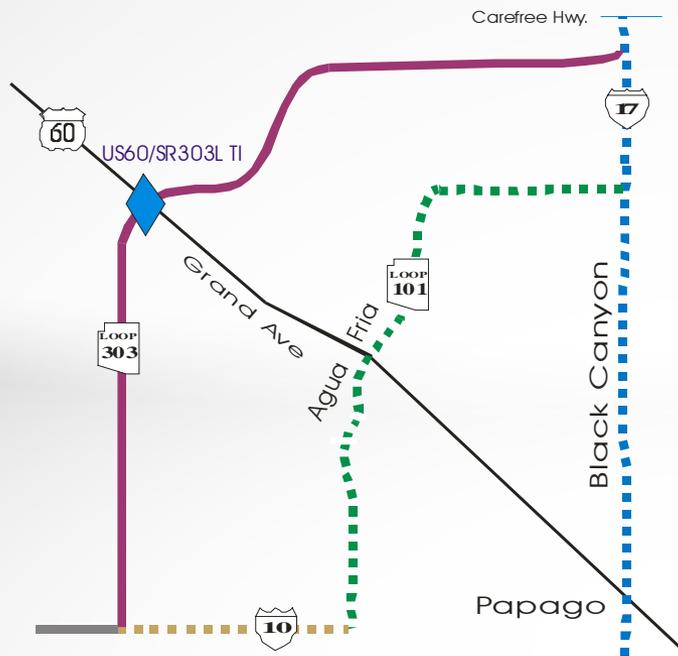


Major Projects - West Valley

L303, El Mirage Rd. TI

- Contract Amount - \$19.9M
- Completed Contract Amount - \$11.1M
- 56% Complete

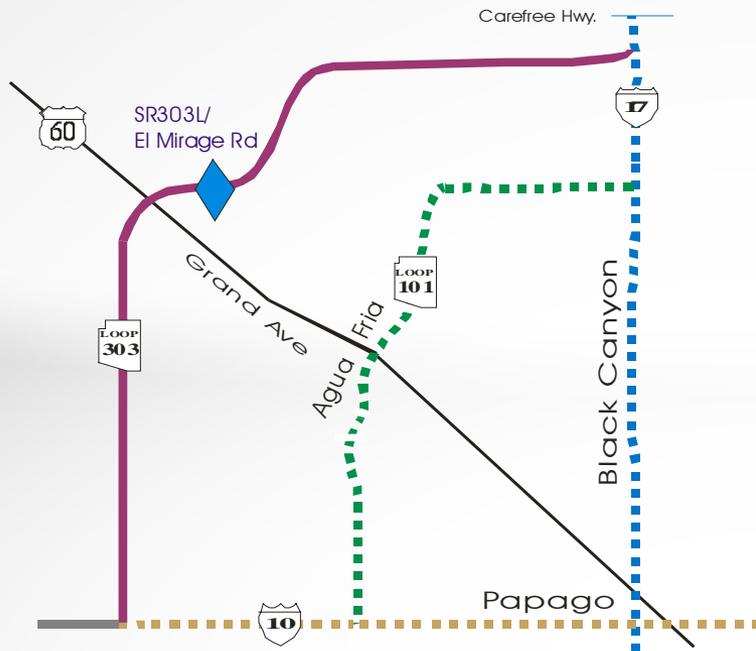

SR202L, South Mountain Freeway

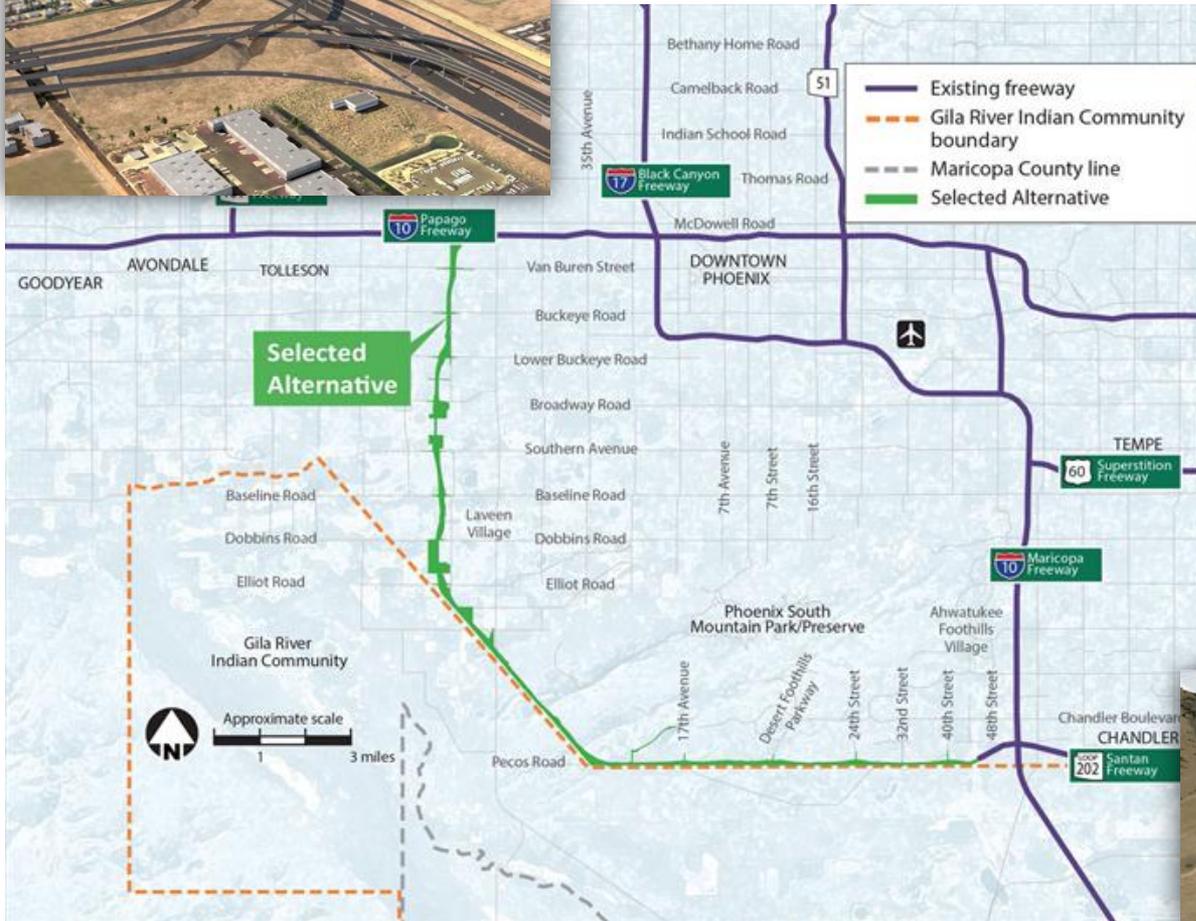

Notice to Proceed:
February 2016

Estimated Construction Budget:
\$1.9B

Shortlisted Teams:

- Connect 202 Partners (Fluor Granite Ames)
- South Mountain Development Group (Kiewit Sundt)
- South Mountain Mobility Group (Dragados Flatiron Pulice)



Madhu H. Reddy, P.E.
District Engineer
Central Construction District
Ph: 602-712-8965
