

State Transportation Board *"District"* Engineers Report

Presentation By: Randy Everett

Date: May 15, 2020

DISTRICT INFORMATION

KEY CONSTRUCTION STAFF:

RANDY EVERETT – SENIOR ADMINISTRATOR

JAMES HARTMAN – ASSISTANT DISTRICT ENGINEER

DYLAN CARDIE – ASSISTANT DISTRICT ENGINEER




Current Construction Projects

Preservation Projects (Pavement and Bridge)

Modernize Projects (Minor Projects, Safety)

Expansion Projects



Pavement Preservation - Flush



- SR87
- US60
- I-17
- Loop202 San Tan
- Loop202 Red Mountain
- Loop 101 Agua Fria

Modernization Projects



High T Interchange at Maricopa Road & SR347

Advertise: June 2020

Construction Cost: \$1.23M



Loop 101 Pima Freeway Widening

Construction Completion: 55%

Contract Time Completion: 61%





I-17 Drainage Upgrade

Construction Completion: 6%

Contract Time Completion: 25%



I-17 & Central Ave Bridge Replacement

Construction Completion: 0%

Contract Time Completion: 5%





I-10 and Fairway TI

Construction Completion: 81%

Contract Time Completion: 92%



Loop 101 Price Freeway

Construction Completion: 82%

Contract Time Completion: 65%



I-17 Pinnacle Peak & Happy Valley TI

Construction Completion: 64%


Contract Time Completion: 82%



SR24 – Gateway Freeway

Advertise: June 2020

Construction Cost: \$131M

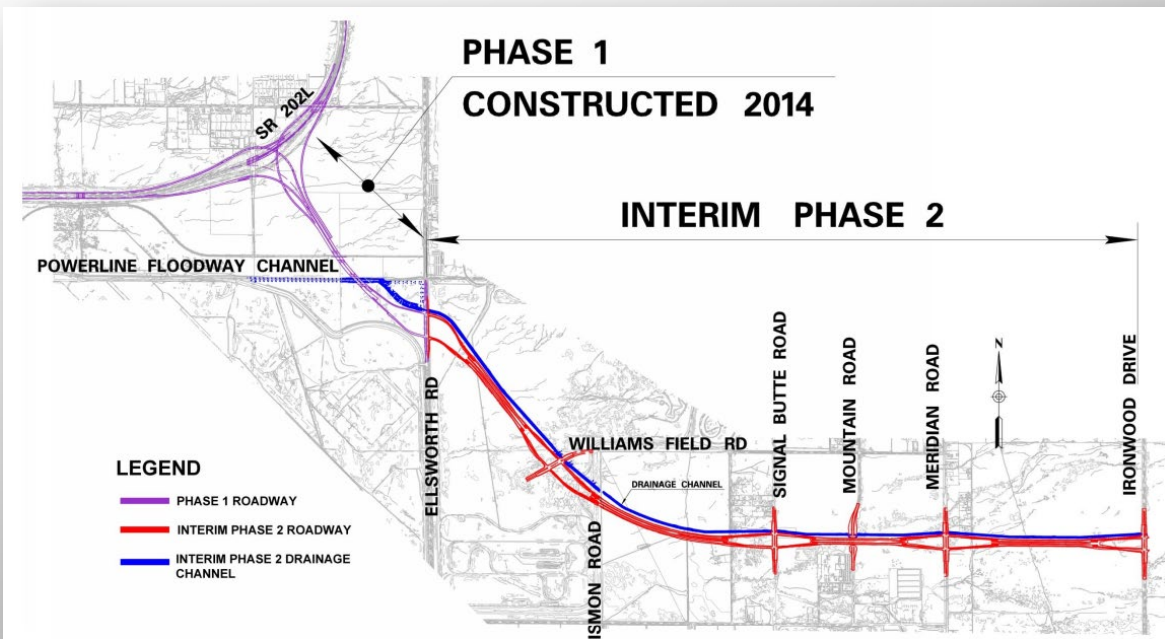




Lindsay Road TI

Advertise: July 2020

Construction Cost: \$26.9 Million

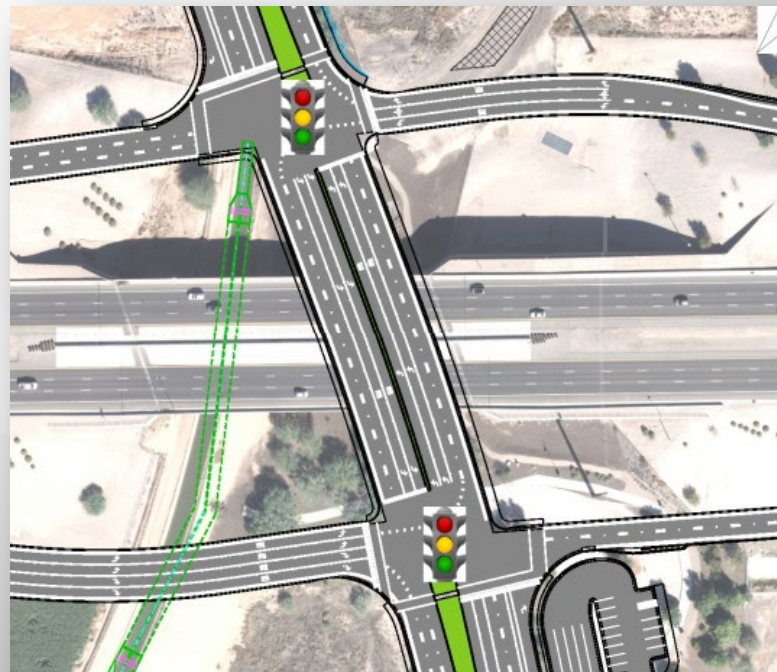



I-10 Gila River Bridge Replacement

Advertise: March 2021

Construction Cost: \$78 Million





Future Considerations





Remove Asphalt Carefully



Diamond Grinding





Final Diamond Ground Product



Questions?

