



# Phoenix Construction District District Engineer's Report

Madhu H. Reddy, P.E.



March 14, 2014




# Projects Under Construction

- 25 Projects Under Construction
  - 5 State Funded Projects
  - 20 Federally Funded Projects
    - 11 LPA Projects (Local Public Agency)
- Overall Construction Cost - \$ 374 Million


January 2014 Certification

# Regional Transportation Plan Freeway Program Phases I - IV, 2006 - 2025

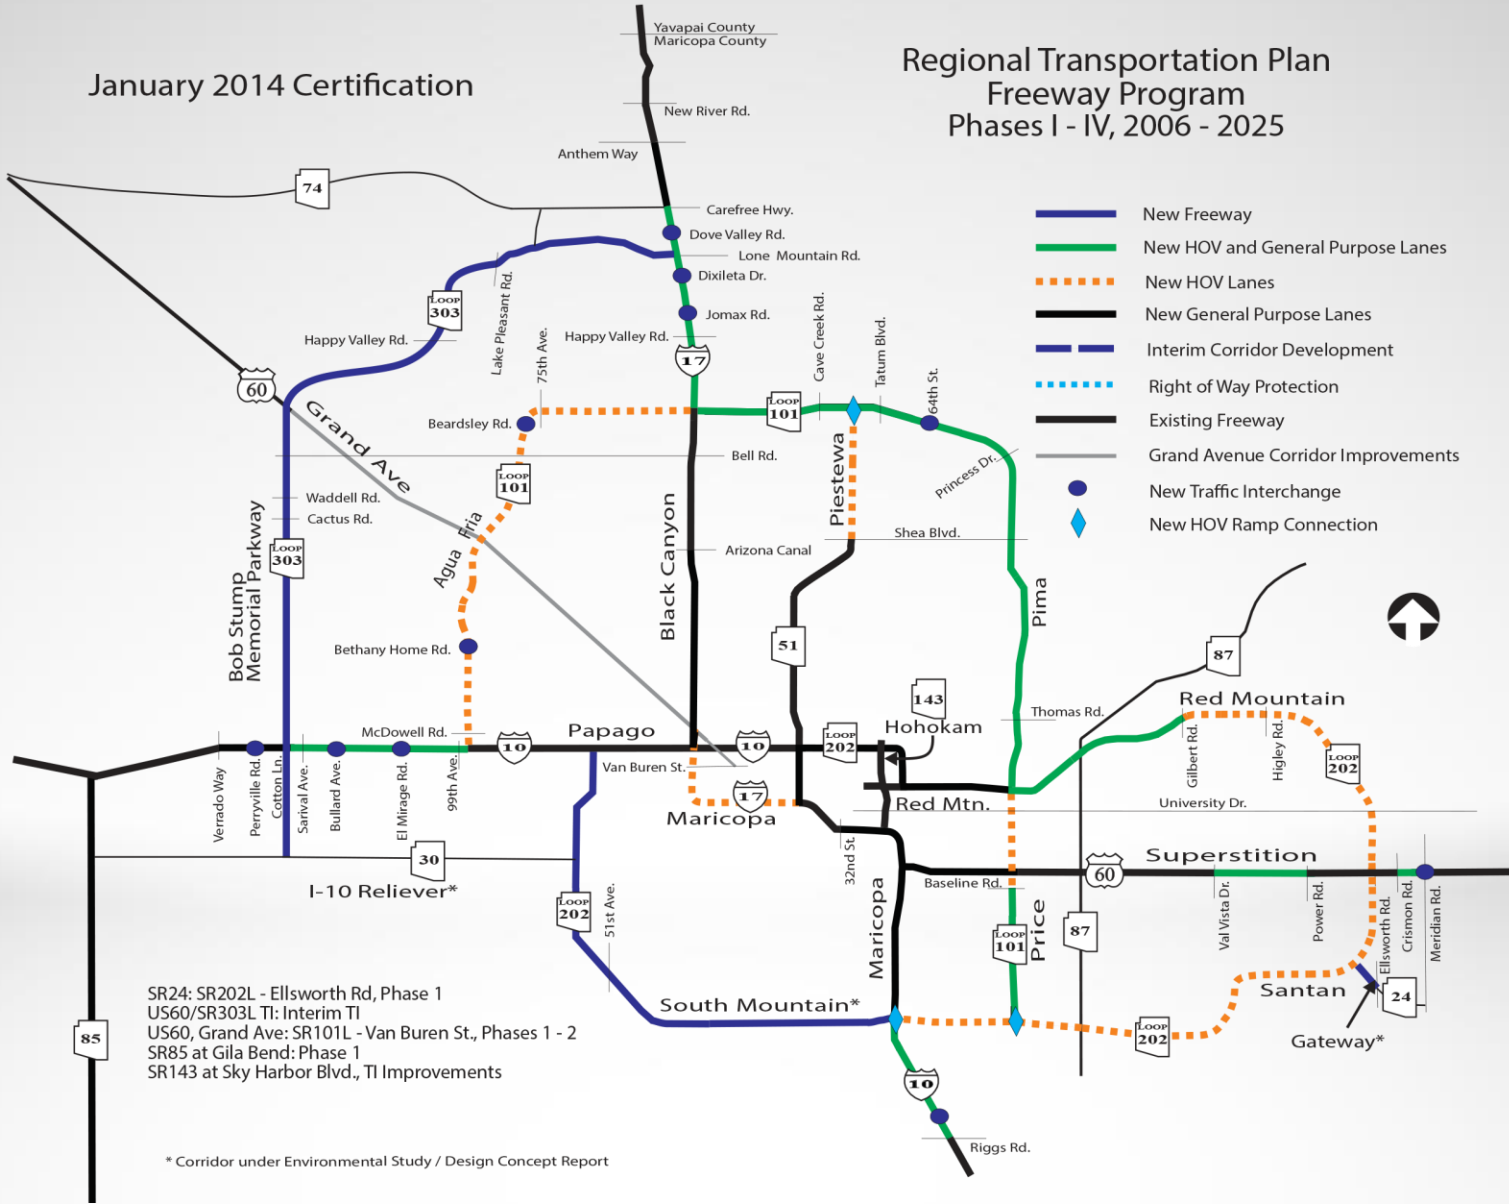

# L303 Projects

L303 Segments	Projects	Length	Construction Cost
Segment 1	I-10 / L303 TI	1.3 Miles	\$ 158,147,019.00
Segment 2	L303, Thomas Rd. - Camelback Rd.	2 Miles	\$ 37,729,965.00
Segment 3	L303, Camelback Rd. - Glendale Ave.	2 Miles	\$ 40,394,974.00
Segment 4	L303, Glendale Ave. - Peoria Ave.	3 Miles	\$ 78,984,874.00
Segment 5 - CMAR Project	L303, Peoria Ave. - Mountain View Rd.	6 Miles	\$ 148,065,807.18
			<b>\$ 463,322,639.18</b>

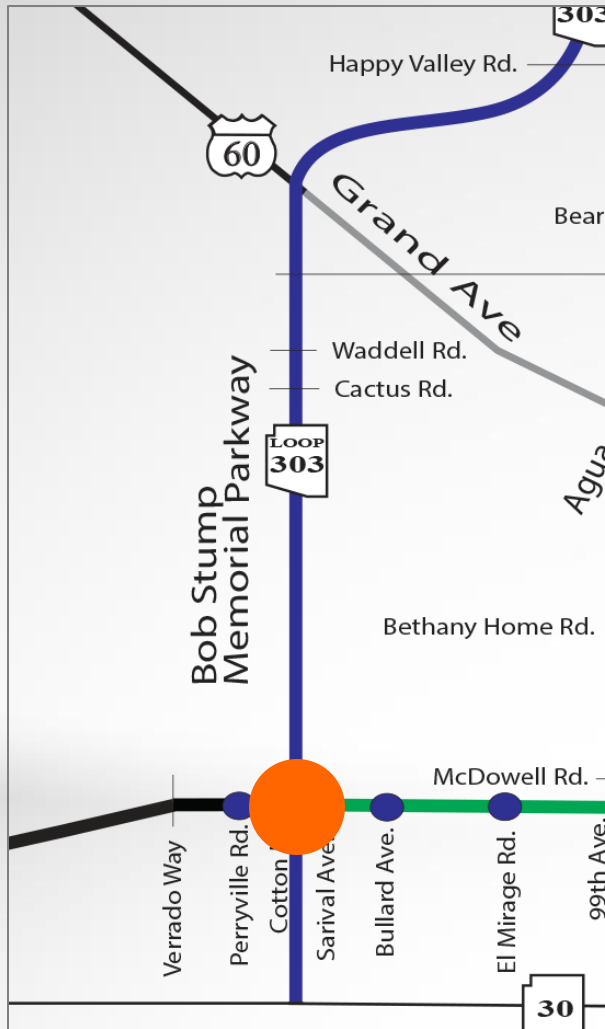

## **Project: I-10 / SR 303 TI**

Contractor: Pulice Construction, Inc.


Construction Cost: \$158 Million



Construction Start Date: November 2011

The Project is 98% complete.

Estimated Completion – Early Fall-2014

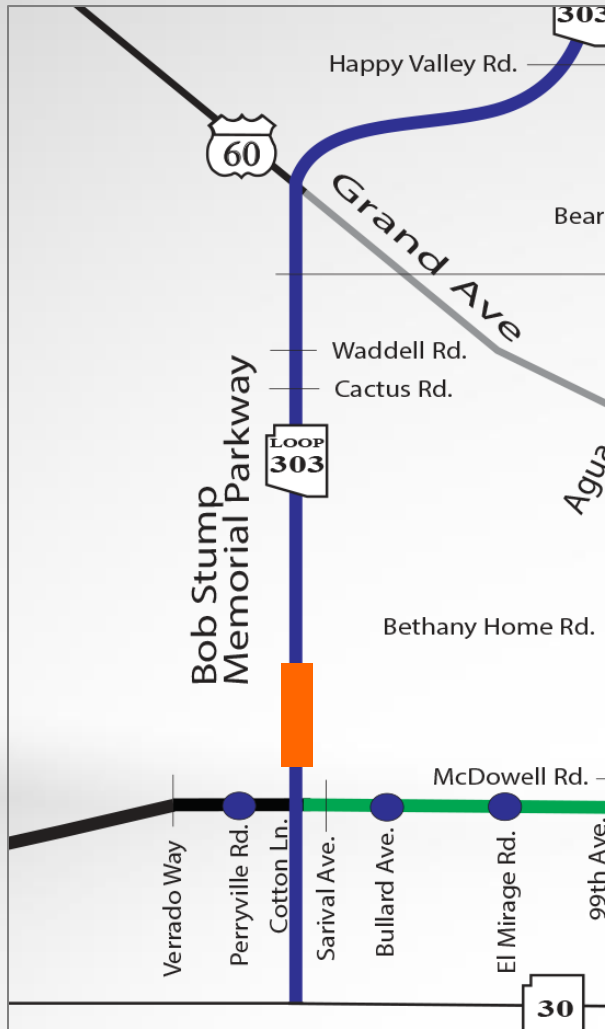

**Project: L303, Thomas Rd. to Camelback Rd.**


Contractor: Ames Construction, Inc.

Construction Cost: \$38 Million



Construction Start Date: July, 2012

Project is Substantially Complete as of November-2013

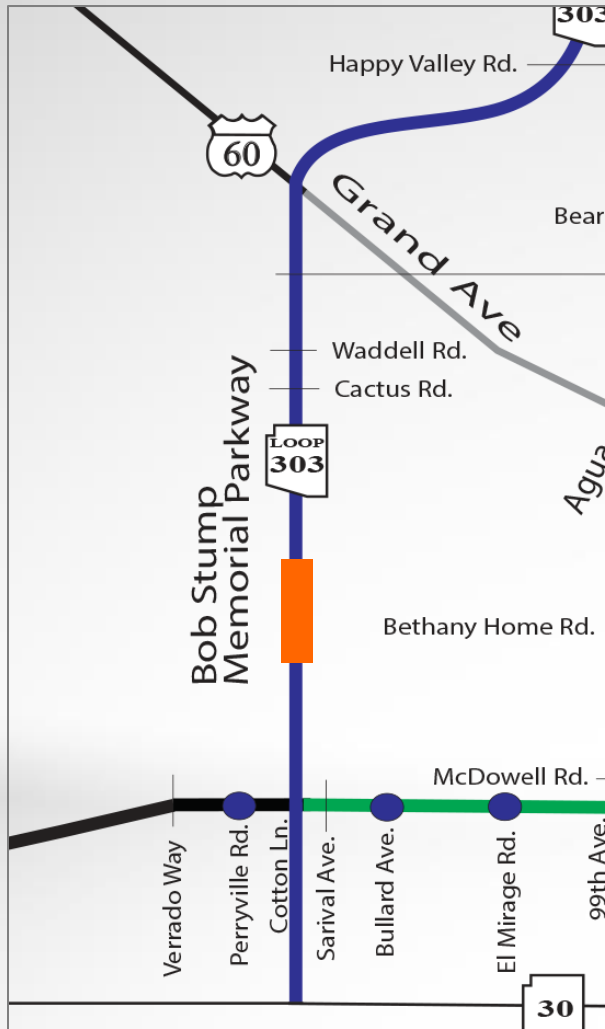

**Project: L303, Camelback Rd. to Glendale Ave.**

Contractor: Pulice Construction, Inc.


Construction Cost: \$40 Million



Construction Start Date: March, 2013

The Project is 76% complete.

Estimated Completion – Late Summer-2014

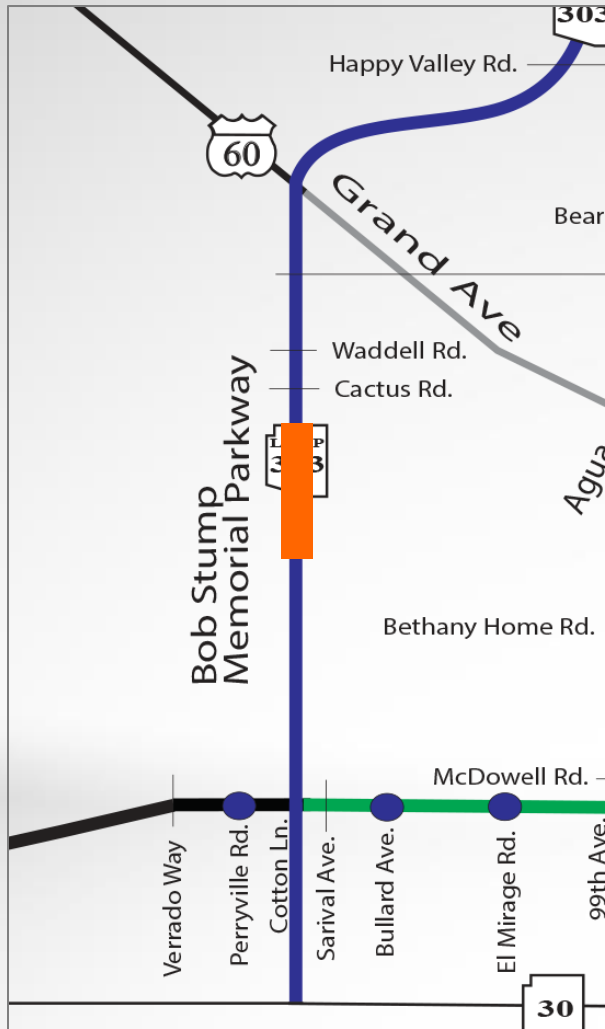

**Project: L303, Glendale Ave. to Peoria Ave.**

Contractor: Pulice Construction, Inc.


Construction Cost: \$79 Million



Construction Start Date: May, 2012

Project is Substantially Complete as of February-2014



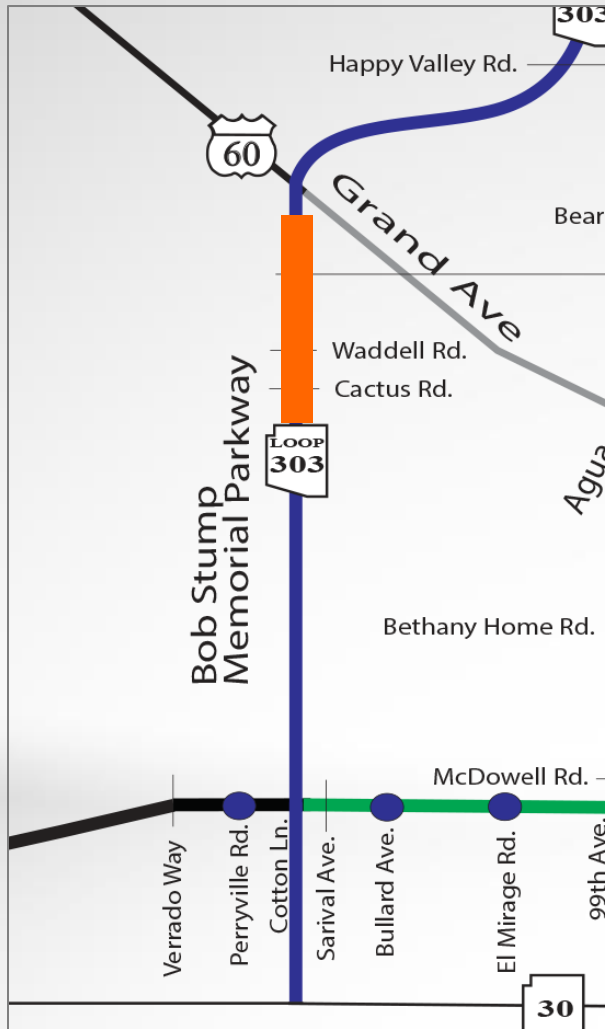


**CMAR Project:**  
**L303, Peoria Ave. to Mountain View Blvd.**  
 Contractor: Pulice Construction, Inc.  
 Construction Cost: \$148 Million



Construction Start Date: August, 2011  
 Project is Substantially Complete as of  
 November-2013

# L303 Landscaping Projects

- ✓ Waddell Rd. to Mountain View Blvd. (Under Construction)
- ✓ Peoria Ave. to Waddell Rd. (Under Construction)
- ✓ Glendale Ave. to Peoria Ave. (Advertisement – June 2014)
- ✓ Camelback Rd. - Glendale Ave. (Advertisement – July 2014)
- ✓ Thomas Rd. - Camelback Rd. (Advertisement – July 2014)
- ✓ L303 / I-10 TI (Advertisement – FY 2015)

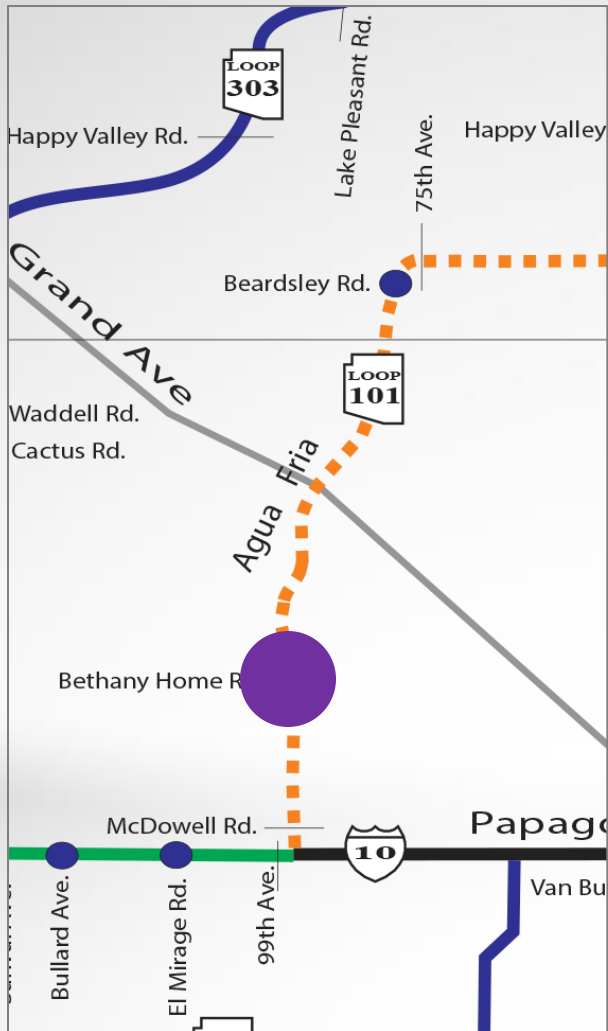

## L101, Maryland Ave. DHOV Ramps Design Build Project

Design Builder: Coffman Specialties, Inc. –  
TY-Lin Construction Cost: \$13 Million



Construction Start Date: September, 2013  
The Project is 91% complete.  
Estimated Completion – April-2014




## **SR 24 (Gateway Freeway)**

Contractor: Ralph L. Wadsworth  
 Construction Company  
 Construction Cost: \$82 Million



Construction Start Date: March, 2012  
 The Project is 97% complete.  
 Estimated Completion – Late Spring-2014

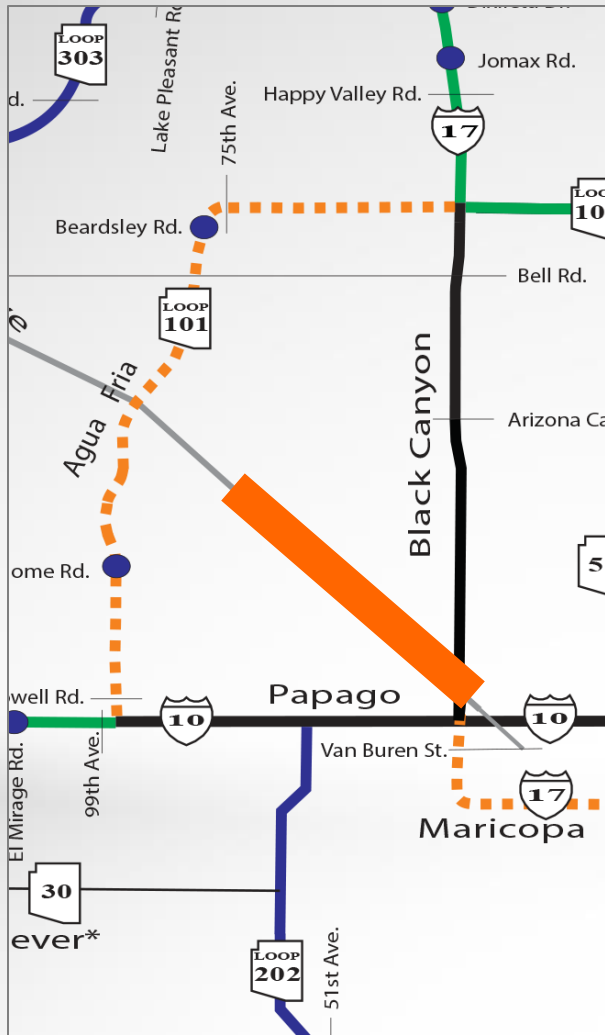

**US 60 (Grand Avenue) – 19<sup>th</sup> Ave. to 71<sup>st</sup> Ave.**

Contractor: Nesbitt Contracting Co., Inc.

Construction Cost: \$18 Million



Construction Start Date: January, 2013

The Project is 85% complete.

Estimated Completion – Late Spring-2014

# Upcoming 2014 Projects

January 2014 Certification

Regional Transportation Plan  
Freeway Program  
Phases I - IV, 2006 - 2025

**L303, El Mirage Rd. TI**


**SR 51, Black Mtn. Blvd.**

**L101, L202 – Shea Blvd.**

**L303 / US 60 TI CMAR**

**L202 DB, L101 –  
Broadway Rd.**

**Meridian Rd. TI**

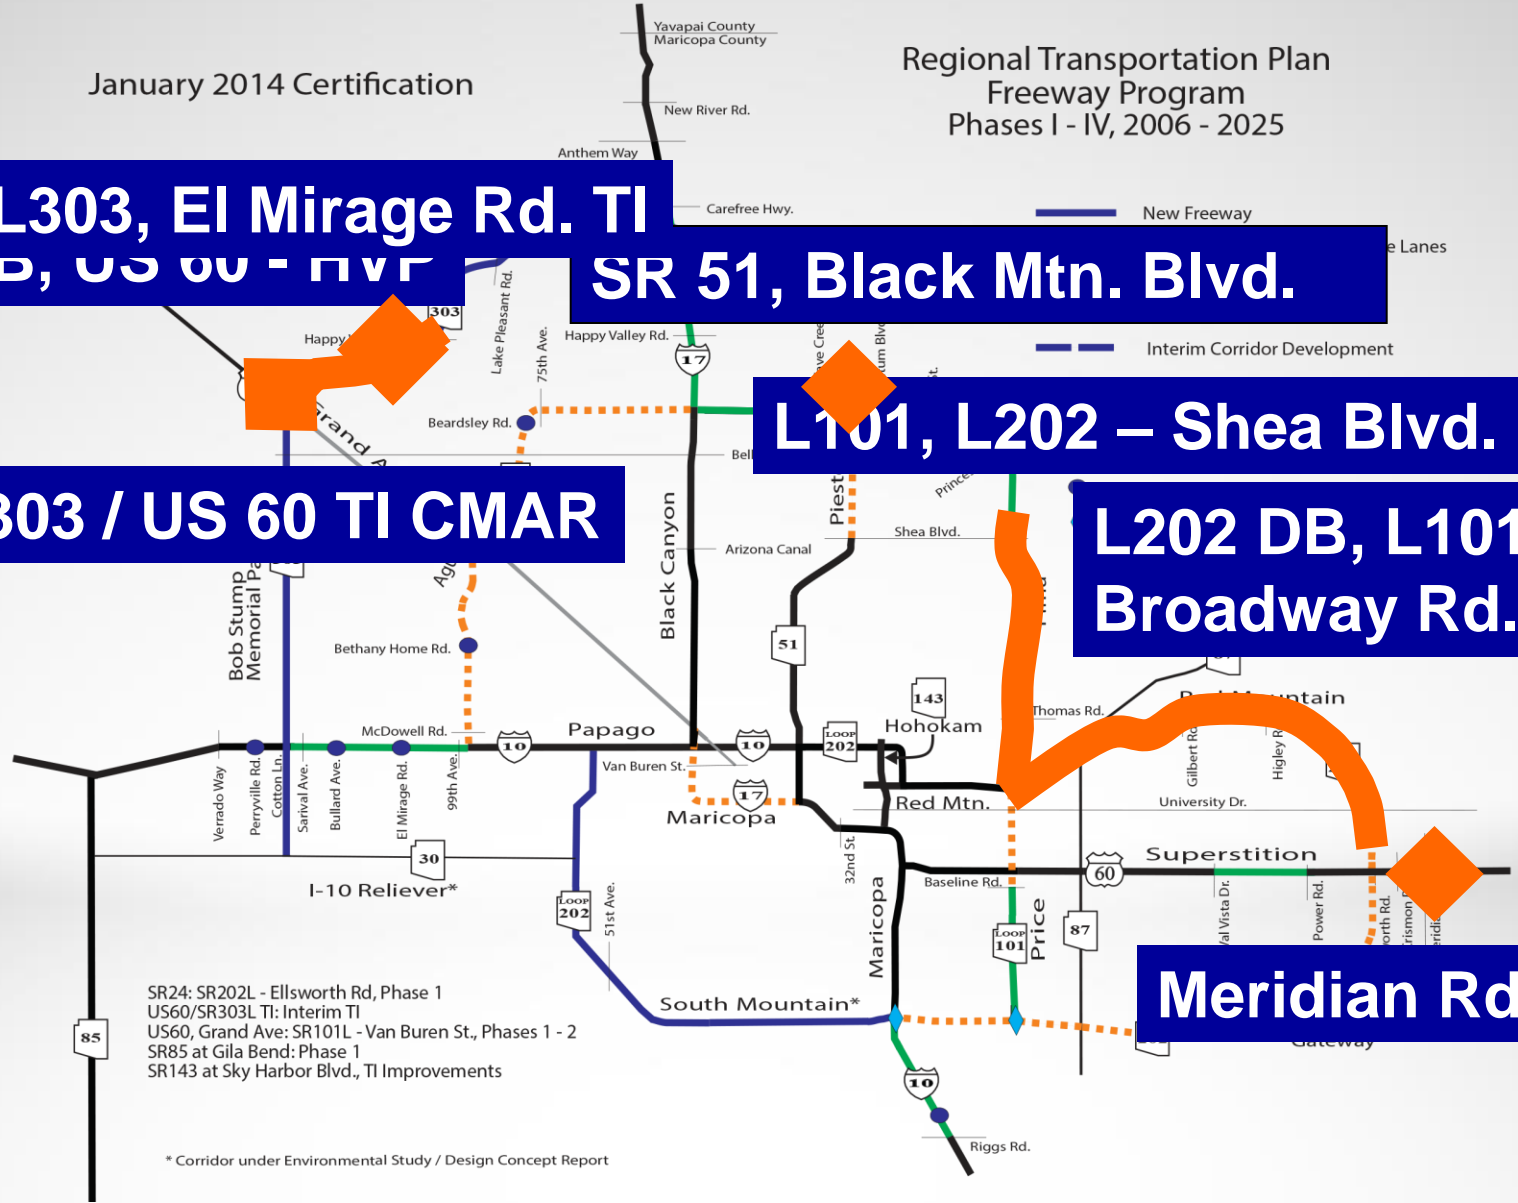

SR24: SR202L - Ellsworth Rd, Phase 1  
 US60/SR303L TI: Interim TI  
 US60, Grand Ave: SR101L - Van Buren St., Phases 1 - 2  
 SR85 at Gila Bend: Phase 1  
 SR143 at Sky Harbor Blvd., TI Improvements

\* Corridor under Environmental Study / Design Concept Report

# Phoenix Construction District District Engineer's Report



Madhu H. Reddy, P.E.  
District Engineer, Phoenix Construction District  
MReddy@azdot.gov  
602-712-8965
