

Transportation Board Meeting

Phoenix, Az



Central District

May 2019


Projects Under Construction

34 Projects Under Construction

- 20 Federally Funded Projects
 - 12 LPA Projects (Local Public Agency)
 - 2 Maintenance Projects

Overall District Contract Amount - \$ 1.336 Billion

- Total Earned - \$862 Million

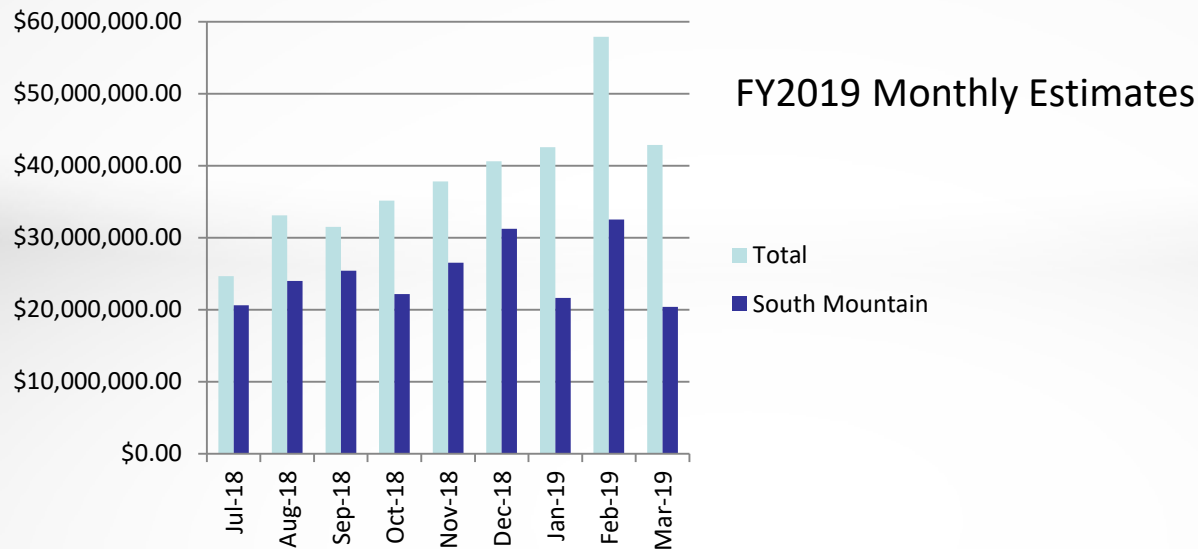

2018 Completed Projects



SR 88 –
Apache Jct
to Tortilla
Flats



SR 202
FMS – Ray
Rd to
Broadway
Rd



SR 88
Apache
Trail



US 60 – 48th
St Pump
Station
Rehab

Ongoing Projects

South Mountain Freeway

- Contract Amount - \$916M
- Completed Contract Amount - \$732M
- 71% Complete / 83% Time Used



Corridor wide construction

Completed 21 of 41 Bridges

Placed 261,815 tons of Asphalt

Began AR-ACFC paving in Salt River and I-10 Segments

Completed Blasting

SR347@UPRR

- Contract Amount - \$23.1M
- Completed Contract Amount - \$14.6M
- 61% Complete / 71% Time Used



UPRR deck pour complete

Borrow for bridge approaches complete

Honeycutt Rd construction has started

Traffic switch onto new SR347 scheduled for mid-late summer

I-17, Pinnacle Peak/Happy Valley TIs

- Contract Amount - \$50.1M
- Completed Contract Amount - \$11.6M
- 23% Complete / 22% Time Used



WB Pinnacle Peak Abutment and Pier Footings Poured

Drainage Work ongoing

Earthwork for ramps ongoing

Retaining Wall R-5 Complete

SR 101, I-17 to Pima Rd

- Contract Amount - \$184.5M
- Completed Contract Amount - \$27.1M
- 15% Complete / 11% Time Used



Preparing drilling pads for
19th Ave & 7th St Bridges

Preparation and Grading for
Miller Road Bridge Detour

Barrier Removal

Clearing, Grubbing and Plant
Salvage ongoing

I-10, Fairway Drive TI

- Contract Amount - \$20.8M
- Completed Contract Amount - \$1.4M
- 7% Complete / 13% Time Used



Clearing, Grubbing and
Plant Salvage

Earthwork including Over-
excavation

FMS re-route in progress

Utility Work at Garfield Rd
Connection

Upcoming Projects

SR101, Baseline to 202 Santan Design Build

I-17, ACDC to Greenway Drainage

I-10, Replace Fire Detection in Tunnel

FMS Projects

Local Agency Projects

Thank you

Julie Gadsby
Assistant District Engineer
Central District
Ph: 602-712-8965
