

Arizona State Transportation Board Meeting

District Engineer's Report

Todd Emery February 16, 2024



Current Construction Projects

Tonto Creek Bridge (Gila County)

New Bridge & Road Improvements

Contract \$21,094,933.18 - 90% Complete

US60, Queen Creek Bridge
Bridge Replacement
Contract \$40,766,879.28 - 0% Complete

US60, Waterfall Canyon Bridge Bridge Replacement Contract \$3,932,694.10 - 0% Complete

SR186 & Business Route 10 - (Arizona Ave - Rex Allen Dr)
Pavement Rehabilitation

Contract \$3,892,698 - 33% Complete

US191 S at I-10 Bridge Rehabilitation Contract \$5,331,936.25 - 19% Complete

Mule Pass Tunnel
Lighting and Restriping
Contract \$4,999,229.78 - 71% Complete

ADOT SOUTHEAST DISTRICT with Maintenance Units Maintenance Units



US191 S at I-10



Currently anticipate being able to reopen the US 191 S Overpass on May 30, 2024.

Overall Project Completion should be mid June 2024






Tonto Creek Bridge





Queen Creek Bridge

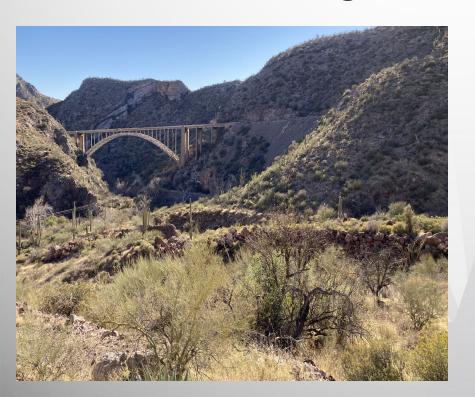

Waterfall Canyon Bridge






Upcoming Construction Projects

US191 at SR75 & SR78 (Construct Roundabout) Programmed Amount - \$6.3M Bids Opened January 26, 2024

US191, US70 to Black Hills Country Byway (Pavement Preservation) Programmed Amount - \$3.5M Bids Opened February 9, 2024)

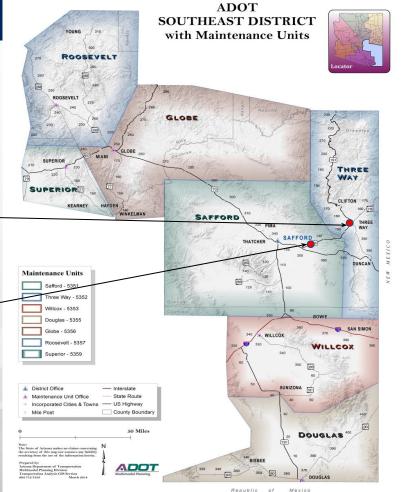



Development Projects

SR88, Fish Creek Hill - Apache Lake Marina
Roadway Repair
Programmed Amount - \$4M
CMAR Work - Anticipate Start of Construction - July 2024

US191, 7th St - MP 173
Pavement Rehabilitation
LEG Appropriation Amount - \$26,430,500
Scheduled Advertisement - February 28, 2024

US191, Armory Road to US70 (East Safford)
Pavement Rehabilitation
LEG Appropriation Amount - \$16,330,000
Scheduled Advertisement - February 28, 2024

East Willcox TI UP,
Bridge Rehabilitation
Programmed Amount - \$2M
Scheduled Advertisement - Oct 2024

US191 Cochise Railroad Overpass
Bridge Replacement with Widening
Programmed Amount - \$41M
Current Anticipated Advertisement - FY25

ADOT SOUTHEAST DISTRICT with Maintenance Units SAFFORE Maintenance Units County Boundary



Planning Projects

Douglas POE Connector Road
Design Concept Report / Environmental Assessment
Currently Anticipated to be Completed - End of year 2024

