

Item 9 – State Engineer’s Report

February 16, 2024

Summary of Active and Finalized Projects

- **86 projects under construction** **\$2.1 B**
- **6 projects finalized in December** **\$34.4 M**
- **Fiscal Year to date:** **36 projects finalized**

Item 10 – New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3-	I-40	\$29,985,000.00	\$35,088,680.00	(\$5,103,680.00)	-14.5%
3-	SR 89	\$524,444.00	\$528,151.49	(\$3,707.49)	-0.7%
10a	I-40	\$1,045,127.50	\$1,475,831.00	(\$430,703.50)	-29.2%
10b	US 191	\$6,519,519.00	\$5,060,075.70	\$1,459,443.30	28.8%
10c*	Local	\$2,197,112.00	\$1,282,920.00	\$914,192.00	71.3%
10d	Local	\$964,749.00	\$1,226,600.00	(\$261,851.00)	-21.3%
TOTAL THIS MONTH		\$39,038,839.50	\$43,379,338.19	(\$4,340,498.69)	-10.0%
TOTAL FY TO DATE		\$425,485,534.21	\$471,917,287.41	(\$46,431,753.20)	-9.8%


*Item 10c is "Postponed" and is not included in the totals

Monthly Totals for Construction Contracts



Month	No. of Projects Bid	Recommended for Award	Low bid	State Estimate	Difference	Percent
Jul-23	7	5	\$19,011,444.40	\$18,393,750.32	\$617,694.08	3.4%
Aug-23	10	8	\$15,076,259.00	\$16,327,669.15	(\$1,251,410.15)	-7.7%
Sep-23	6	5	\$21,729,234.61	\$27,909,439.00	(\$6,180,204.39)	-22.1%
Oct-23	8	6	\$182,623,916.73	\$200,304,332.20	(\$17,680,415.47)	-8.8%
Nov-23	4	4	\$76,384,614.80	\$79,739,806.55	(\$3,355,191.75)	-4.2%
Dec-23	7	7	\$71,621,225.17	\$85,862,952.00	(\$14,241,726.83)	-16.6%
Jan-24	6	5	\$39,038,839.50	\$43,379,338.19	(\$4,340,498.69)	-10.0%
Feb-24					\$0.00	
Mar-24					\$0.00	
Apr-24					\$0.00	
May-24						
Jun-24						
Fiscal YTD Total	48	40	\$425,485,534.21	\$471,917,287.41	(\$46,431,753.20)	-9.8%

Current Statewide District Updates



South Central District Current


ADOT

I-10 Widening:
Ina to Ruthrauff,
MP 248.03-MP 251.85

Country Club to Kino
(Design Build Procurement),
I-10, MP 262-MP 264.5

Irvington TI (Design),
I-19, MP 60.83

Border Patrol Station to
Moson Rd., SR 90, MP
304.4-MP 325.9

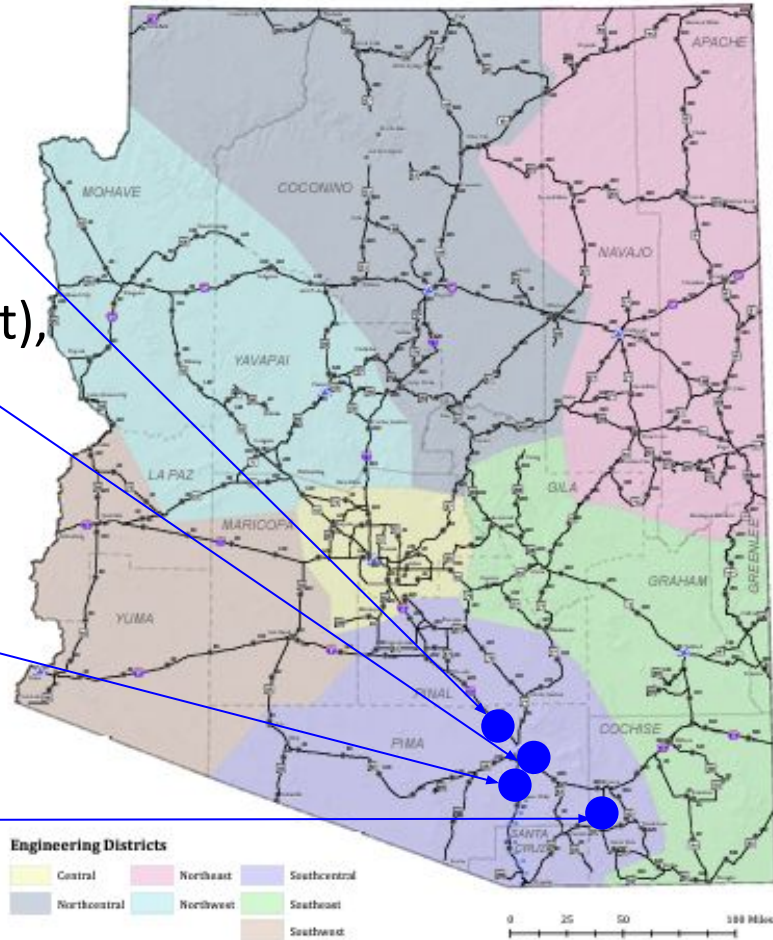

North Central District Current Projects


ADOT

North Lake Powell
Blvd Roundabout,
US89, MP 548.8

US160 Flashing Stop
Ahead Signs: SR98 &
IR15 Intersections

Pavement
Preservation, US 89,
MP 425 - MP 434

JW Powell Bridge
Replacement, I-17,
MP 337

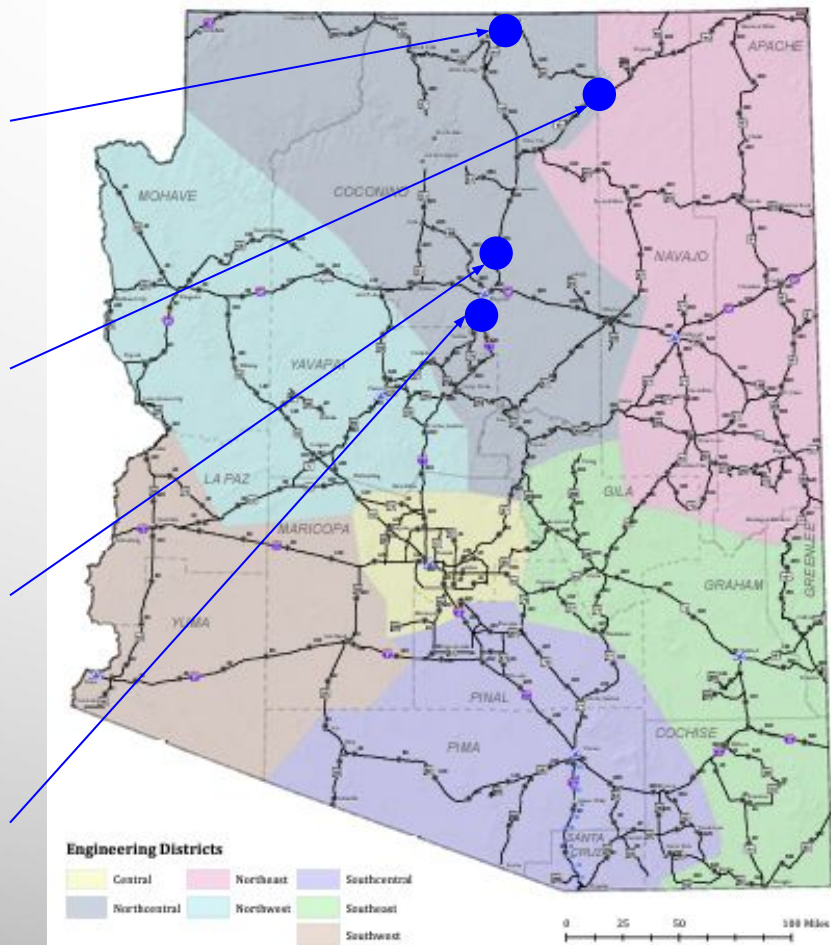


Southwest District's Current Projects

ADOT

**I-10 Truck Parking
Availability, 4 Locations
Signs for # Open Stalls**

**B-8 Gila Bend ADA Ramps
MP 119-MP121
Sidewalk/Ramp Upgrade**

**SR 85 Gila Bend to
County Line,
MP 0 - MP 16
Spot Repair/Safety
Upgrade**

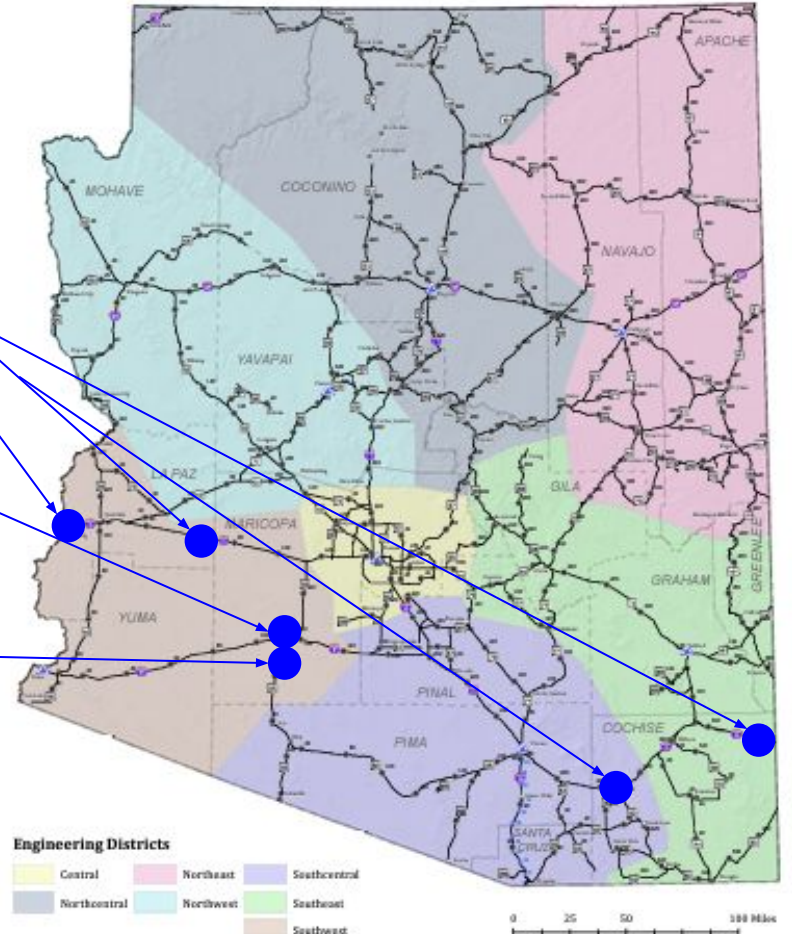

Northwest District Current Projects


ADOT

**Fort Rock TI -
Markham Wash,
I-40, MP 92-MP 107**

**E. Kingman TI WB
Bridge,
I-40, MP 83-MP 84**

**Gunsite Canyon
Road-Gray Wash,
US-93, MP 119-MP 130**

**Wash Bridges,
US-60, MP 57-MP 58**

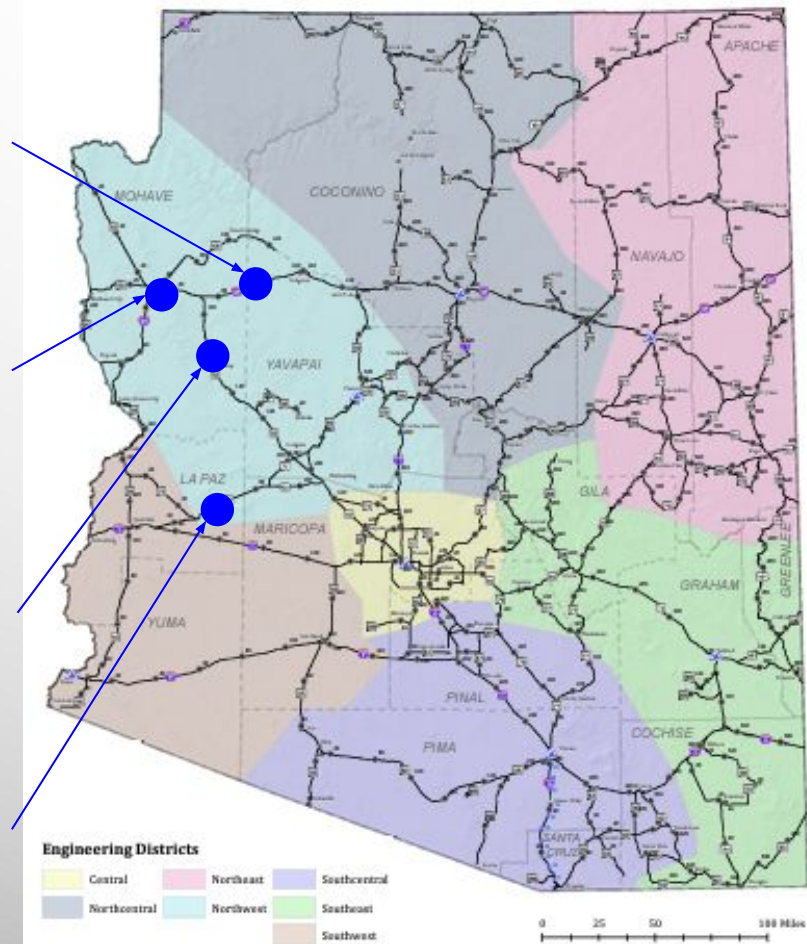

Northeast District Current Projects



Coyote Wash Bridge (Replace Superstructure)

SR 87, MP 375

Work Begins April 24

Pinta-McCarrel, (Pavement Pres.)

I 40, MP 318 - MP 330

Bid Opened 1/26/24

Crestview - Joy Nevine, (Paving)


B40 Holbrook, MP 286-MP 287

Bid Opening April 2024

SR 277-Forest Bdry, (Life Ext)

SR 377, MP 0-MP 6

Work Begins June 24

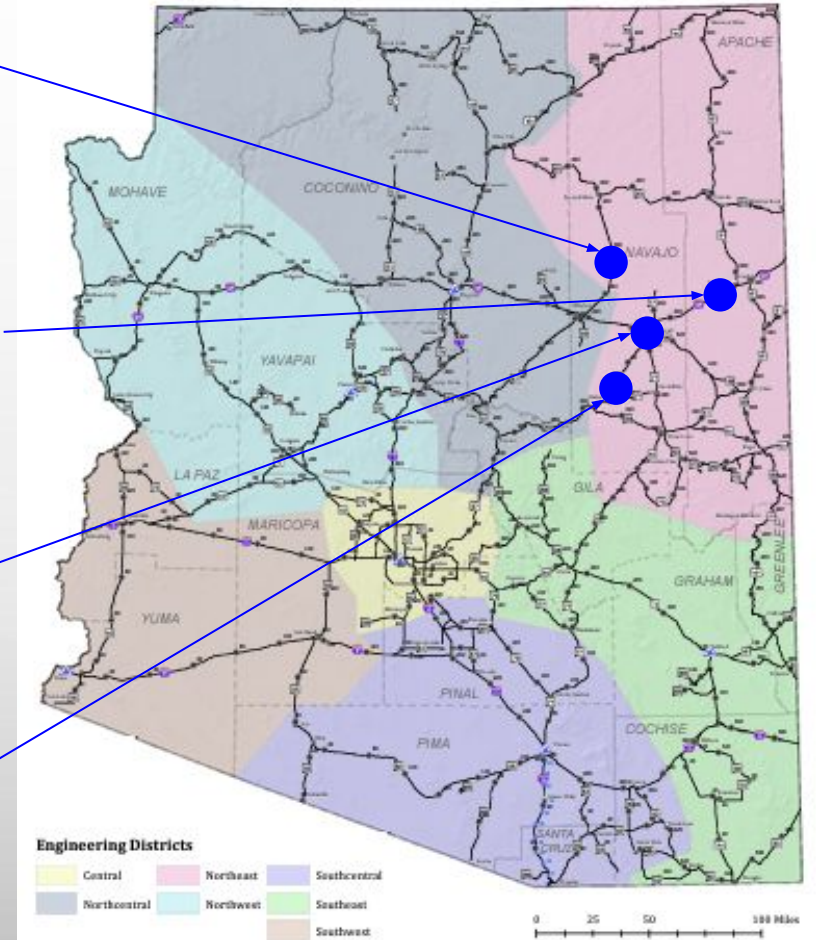

Central District Current Projects




SR101 Princess to Shea
Loop 101 Expansion in Scottsdale
3% Complete

16th Street Screenwall
SR101 Pima Freeway
70% Complete

SR347 at Lakeview Blvd.
In City of Maricopa
60% Complete

60X
Old US60 Highway
0% Complete

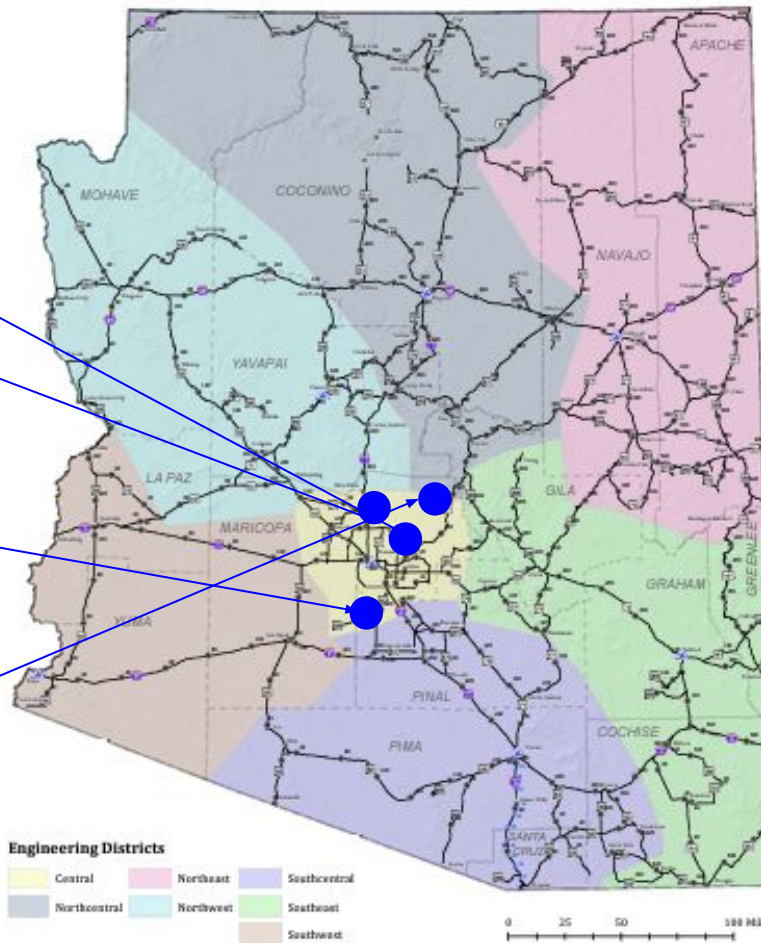


Low Bid	\$1,045,128
State estimate	\$1,475,831
Difference	-\$430,704
% Difference	-29.2%

Recommendation: Award

Reasons for Difference:

- Structural Excavation
- Structural Concrete
- Reinforcing Steel

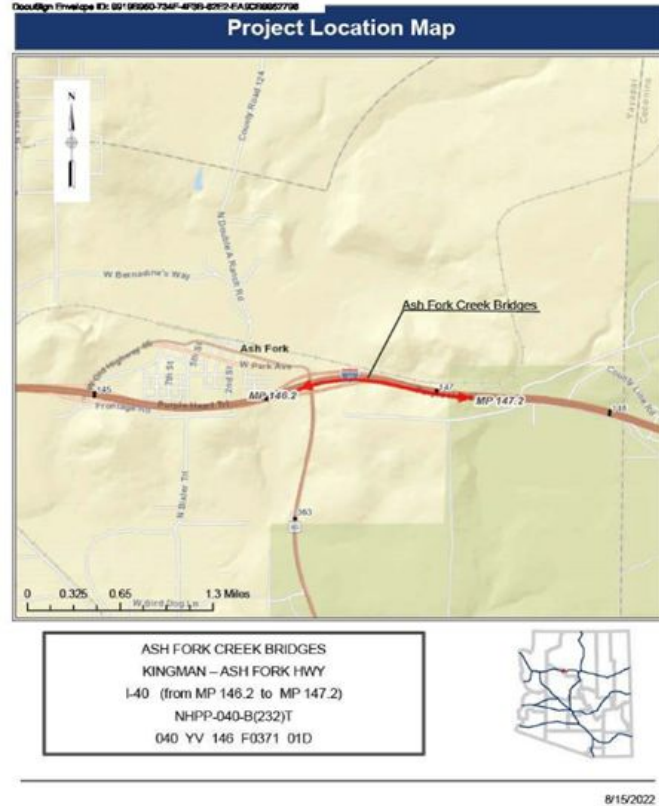




Low Bid	\$6,519,519
State estimate	\$5,060,076
Difference	\$1,459,443
% Difference	28.8%

Recommendation: Award

Reasons for Difference:

- PCCP
- Asphaltic Concrete

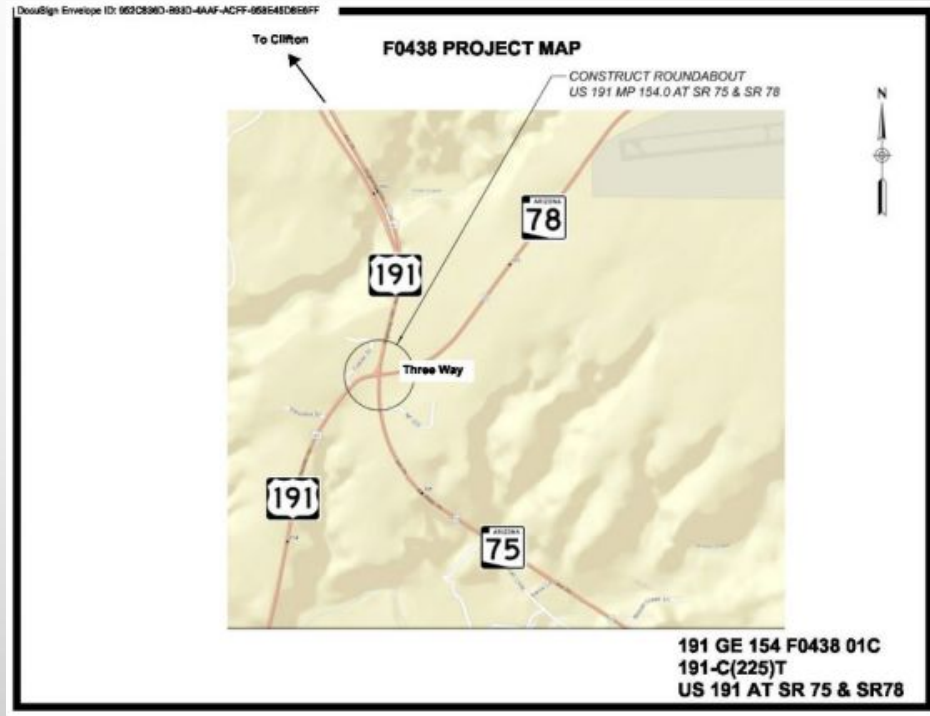




Low Bid	\$2,197,112
State estimate	\$1,282,920
Difference	\$914,192
% Difference	71.3%

Recommendation: Postponed

Reasons for Difference:

- Structural Concrete
- Voided Slab
- Mobilization

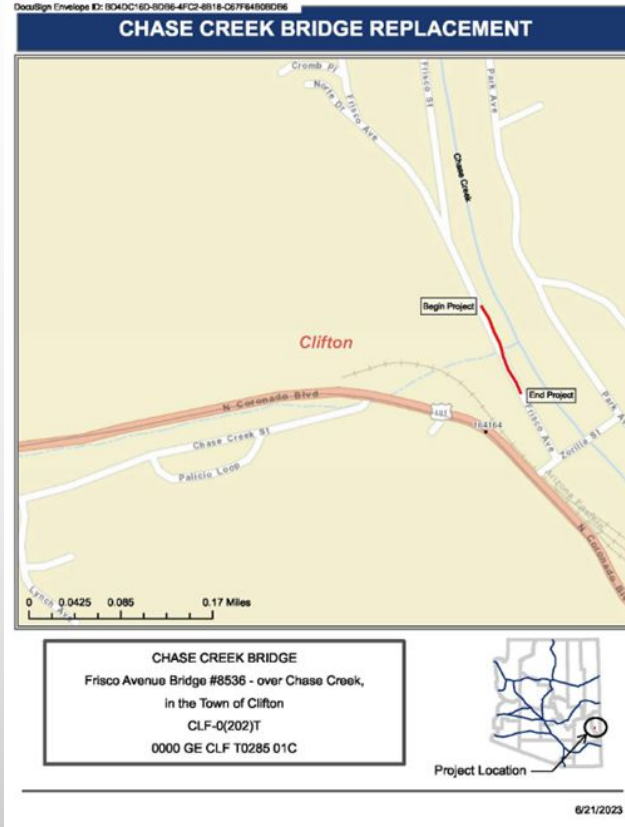




Low Bid	\$964,749
State estimate	\$1,226,600
Difference	-\$261,851
% Difference	-21.3%

Recommendation: Award

Reasons for Difference:

- Remove Poles & Bases
- Pole Foundation
- LED Luminaire

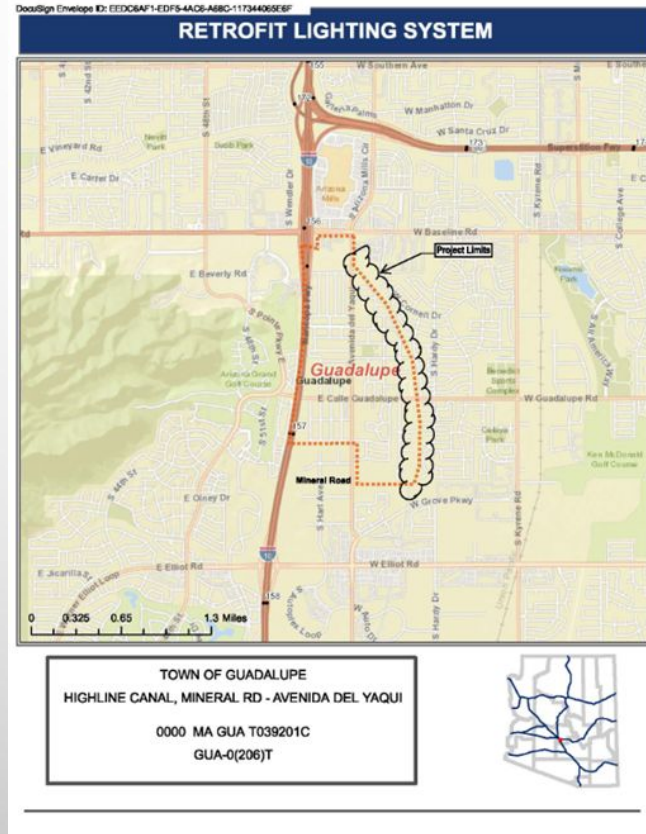




Low Bid	\$29,985,000
State estimate	\$35,088,680
Difference	-\$5,103,680
% Difference	-14.5%

Recommendation: Award

Reasons for Difference:

- Milling
- Asphaltic Concrete
- Mobilization

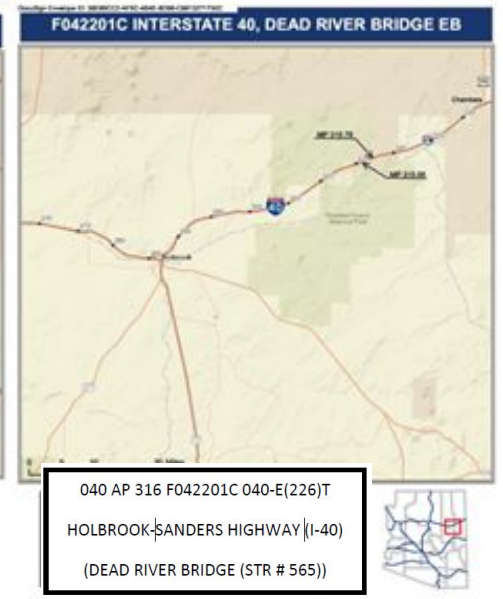




Low Bid	\$524,444
State estimate	\$528,151
Difference	-\$3,707
% Difference	-0.7%

Recommendation: Award

Reasons for Difference:

- Fog Coat

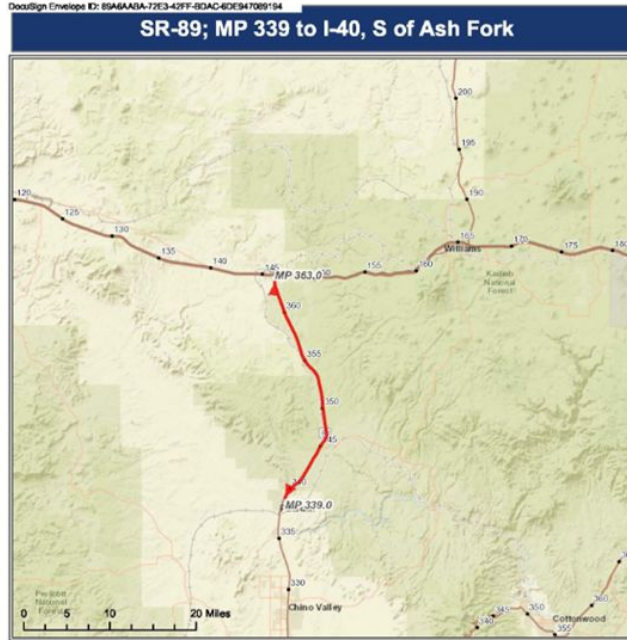

MP339 - I-40
SR-89; MP 339 - 363
SR-89 (from MP 339.0 to MP 363.0)
HSIP-089-B(220)T
089 YV 339 F0519 01C



5/15/2023
