

Item 8 – State Engineer's Report June 21, 2024 Summary of Active and Finalized Projects


95 projects under construction \$2.15 B

11 projects finalized in May \$76.9 M

Fiscal Year to date:

63 projects finalized

ARIZONA DEPARTMENT OF TRANSPORTATION

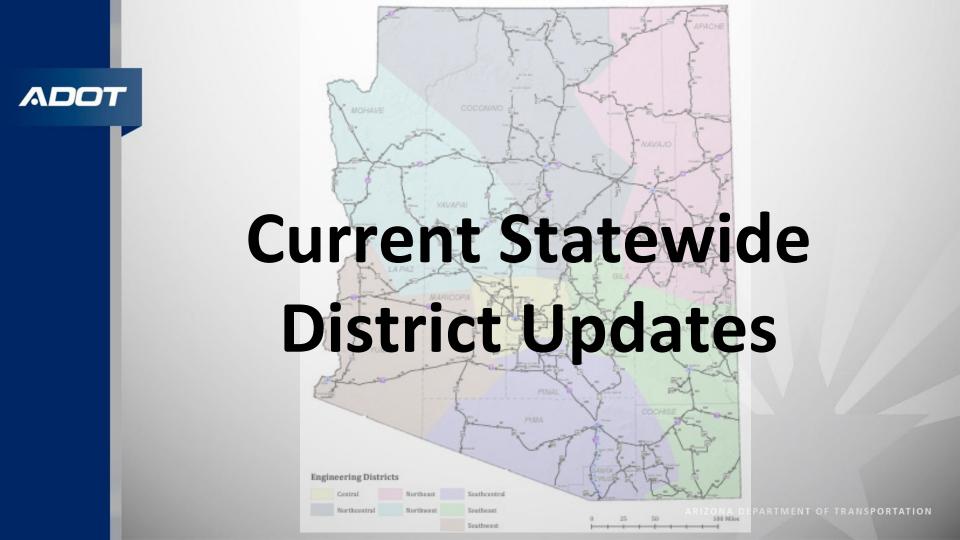

South Central District Current

SR87 and Skousen Traffic Signal


ADOT

I-10 Widening: Ina to Ruthrauff, MP 248.03-MP 251.85

Country Club to Kino (Design Build Procurement), I-10, MP 262-MP 264.5

Irvington TI (Design), I-19, MP 60.83

Border Patrol Station to Moson Rd., SR 90, MP 304.4-MP 325.9

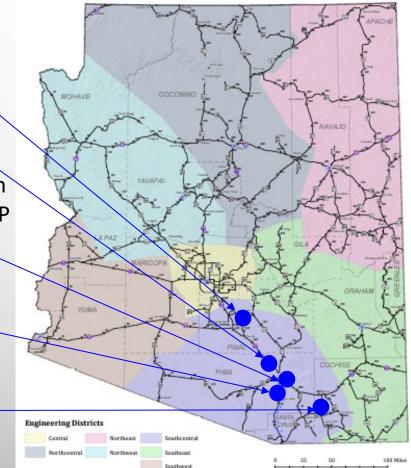

TRANSPORTATION


Southwest District's Current Projects

US 60, Vicksburg-Junct. SR 72 Pavement Preservation

ADOT

I-10, Scaddan Wash -Plomosa (MP 24-30) Pavement Preservation

B8, Weidner St.-Old Hwy 80 ADA Improvement Project

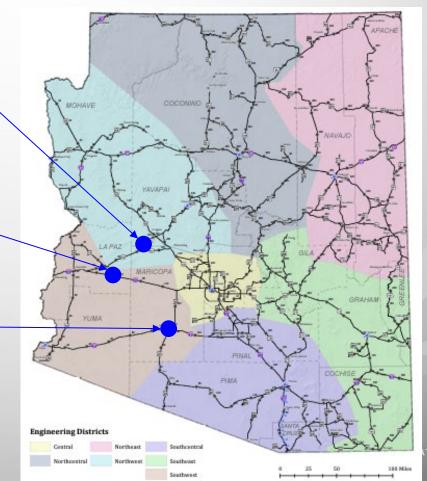

TION


Southeast District Current Projects

ADOT

Waterfall Canyon Bridge (Bridge Replacement) US60 MP 229.5 1% Complete

US191 at SR75 & SR78 (Construct New Roundabout) US191, MP 154 2% Complete

US191 TI Permanent Bridge Repair (Bridge Rehabilitation - ER) I-10 MP 331 to 332 80% Complete

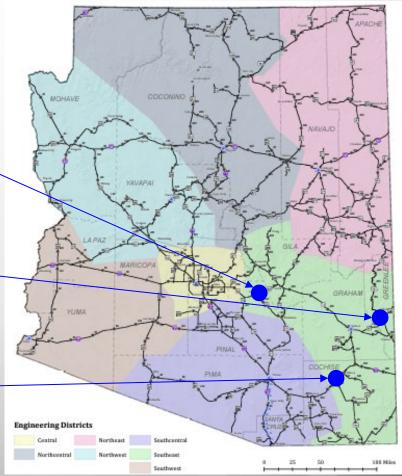


Initial Review Completed - 04/03/2024 Issues pending resolution Northwest District Current Projects

Ash Fork Creek Bridges I-40, MP 146 50% Complete, 57% Time Spent


ADOT

Needle Mountain TI - Lake Havasu TI I-40, MP 2-MP 8 Partnering Held 06/05/24

Mountain View Rd Mohave County 47% Complete, 62% Time Spent

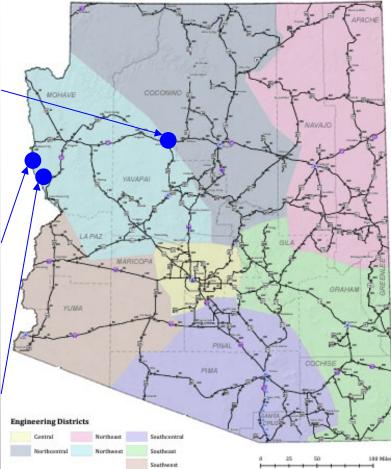


Northeast District Current Projects



Pinta to McCarrel I 40 MP 318 - MP 330 Dead River Bridge Eastbound I40 MP 316

Jct. SR 277 to Forest Boundary SR 377 MP 0 - MP 6

Overgaard to Camperland SR 260 MP 310 - MP 317

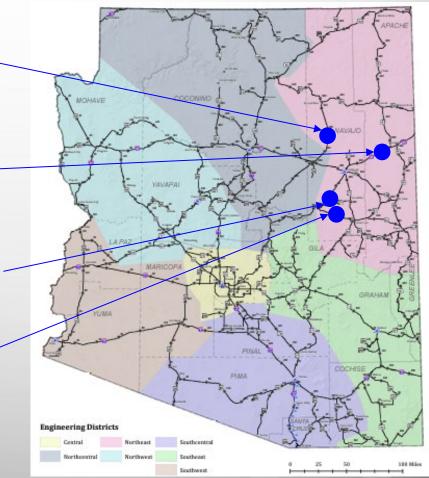

Central District Current Projects

I-17 Happy Valley to SR74 Mill and Diamond Grind 22% Complete 10% Time Spent

ADOT


SR101 Princess to Shea Loop 101 Expansion in Scottsdale 22% Complete 19% Time Spent

SR347 at Lakeview Blvd. In City of Maricopa 100% Complete 94% Time Spent

US 60X Sossaman to Meridian Old US60 Highway 18% Complete 16% Time Spent

SR202 Val Vista to SR101L Loop 202 Expansion in Chandler/Gilbert 0% Complete 0% Time Spent

I-10 Gila River BridgeBridge Replacement4% Complete 3% Time Spent

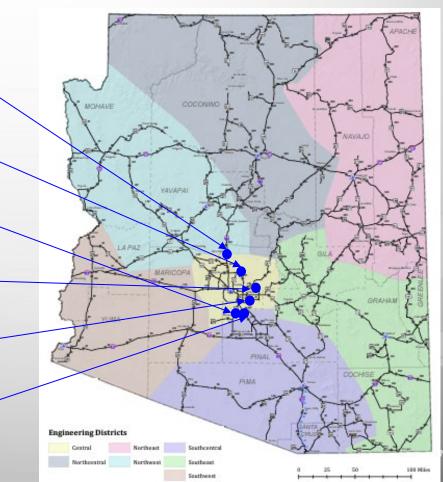

Item 9 – New Construction Contracts

ADOT

Item	Highway	Low bid	State Estimate	Difference	Percent
3c US 95 \$2		\$2,715,175.00	\$2,740,258.00	(\$25,083.00)	- 0.9 %
3d	SR 303	\$3,490,059.95	\$3,426,767.05	\$63,292.90	1.8%
TOTAL THIS MONTH		\$6,205,234.95	\$6,167,025.05	\$38,209.90	0.6 %
TOTAL FY TO DATE		\$866,027,278.63	\$935,833,694.01	(\$69,806,415.38)	- 7.5 %

Monthly Totals for Construction Contracts

ADOT

	No. of					
Month	Bids	Awards	Low bid	State Estimate	Difference	Percent
Jul-23	7	5	\$19,011,444.40	\$18,393,750.32	\$617,694.08	3.4%
Aug-23	10	8	\$15,076,259.00	\$16,327,669.15	(\$1,251,410.15)	-7.7%
Sep-23	6	5	\$21,729,234.61	\$27,909,439.00	(\$6,180,204.39)	-22.1%
Oct-23	8	6	\$182,623,916.73	\$200,304,332.20	(\$17,680,415.47)	- 8. 8%
Nov-23	4	4	\$76,384,614.80	\$79,739,806.55	(\$3,355,191.75)	-4.2%
Dec-23	7	7	\$71,621,225.17	\$85,862,952.00	(\$14,241,726.83)	-16.6%
Jan-24	6	5	\$39,038,839.50	\$43,379,338.19	(\$4,340,498.69)	-10.0%
Feb-24	7	6	\$153,699,735.61	\$162,316,494.50	(\$8,616,758.89)	-5.3%
Mar-24	10	9	\$37,454,136.92	\$39,417,472.52	(\$1,963,335.60)	-5.0%
Apr-24	11	11	\$243,182,636.94	\$256,015,414.53	(\$12,832,777.59)	-5.0%
May-24	2	2	\$6,205,234.95	\$6,167,025.05	\$38,209.90	0.6%
Jun-24						
Fiscal YTD	78	68	\$866,027,278.63	\$935,833,694.01	(\$69,806,415.38)	-7.5%

District 6

PAVEMENT REHABILITATION US 95: CASTLE DOME MINE RD - LA PAZ COUNTY LINE

Item 3c

ADOT

Low Bid	\$2,715,175	
State Estimate	\$2,740,258	
Difference	-\$25,083	
% Difference	-0.9%	

Recommendation: Award Reasons for Difference:

- Milling
- Asphalt Binder



ARIZONA DEPARTMENT OF TRANSPORTATION

District 1

INTERSECTION IMPROVEMENTS SR 303L: SR 303L & US 60 TI

Item 3d

ADOT

Low Bid	\$3,490,060	
State Estimate	\$3,426,767	
Difference	\$63,293	
% Difference	1.8%	

Recommendation: Award ReBid

Reasons for Difference:

- Mobilization
- Survey & Layout

