


Item 8 – State Engineer’s Report March 21, 2025

Summary of Active and Finalized Projects

- **92 projects under construction** **\$2.9 B**
- **6 projects finalized in February** **\$65.4 M**
- **Fiscal Year to date:** **60 projects finalized**

Current Statewide District Updates



South Central District Current Projects


**SR87 and Skousen
Traffic Signal**

**I-10 Widening:
Ina to Ruthrauff,
MP 248.03-MP 251.85**

**Country Club to Kino (Design
Build Procurement), I-10, MP
262-MP 264.5**

**Irvington TI (Design),
I-19, MP 60.83**

**Border Patrol Station to
Moson Rd., SR 90, MP
304.4-MP 325.9**

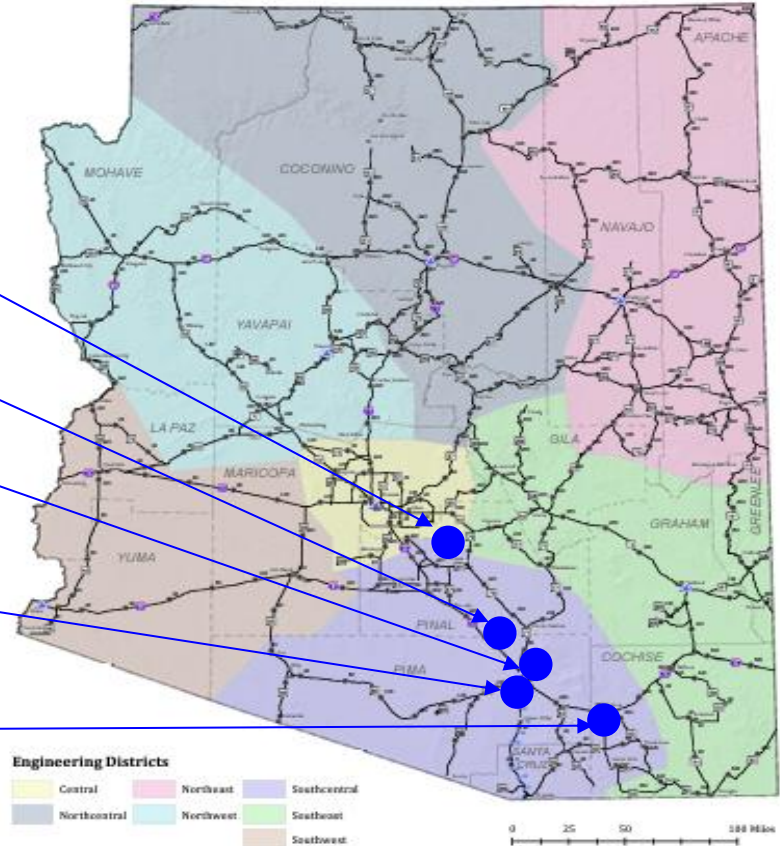

North Central District Current Projects



**Townsend Winona
to Sunset Crater
Drainage Repairs,
US 89 MP 423 - MP
432**



**Variable Speed Limit
Signs, I-40 MP 185 -
MP 195**



**Roundabout, City of
Flagstaff Fourth St/Cedar
Ave/ Lockett Rd**

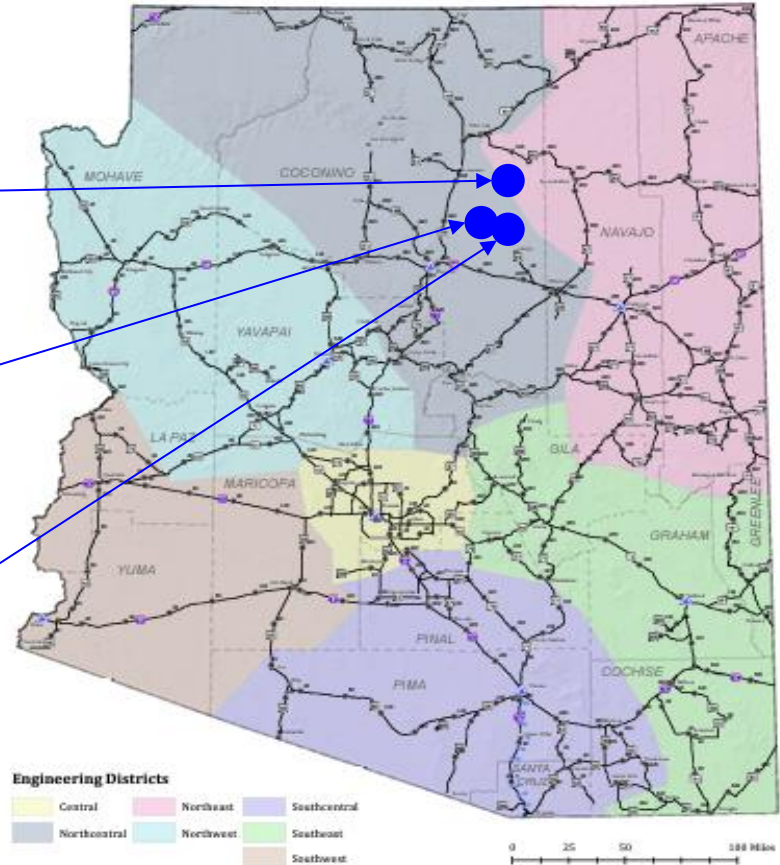

Southwest District's Current Projects


**I-10, Salome Rd-
Tonopah Pav. Pres.**

**I-10 Scaddan Wash-
Plomosa Pav. Pres.**

**SR 95, Tyson St.-N. Of
Quartzsite Pav. Pres.**

**Statewide Port of Entry
Barrier Protection**

**SR 85, I-8-MP 3.34
Drainage Improvement**

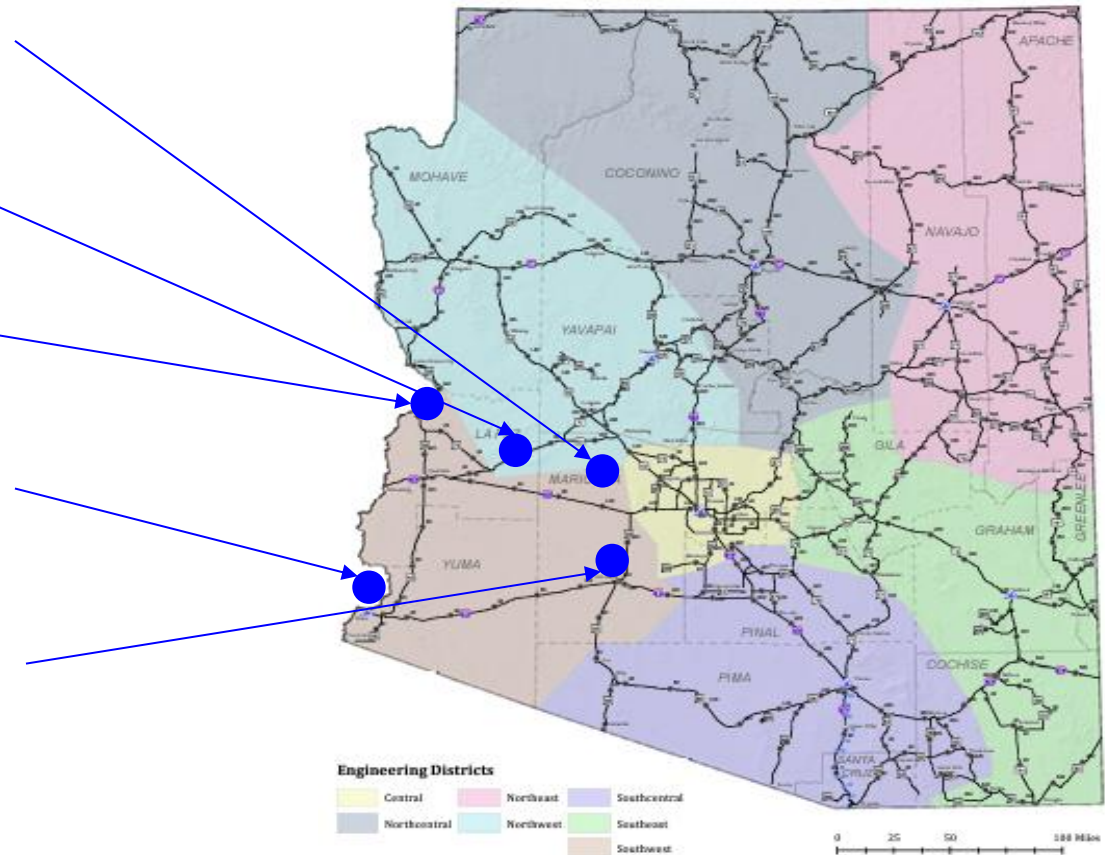


Southeast District Current Projects

Waterfall Canyon Bridge
US 60, MP 229.5
Bridge Replacement

Queen Creek Bridge
US 60, MP 227.7
Bridge Replacement

US 191 at SR 75 and SR 78
US 191, MP 154
Construct Roundabout

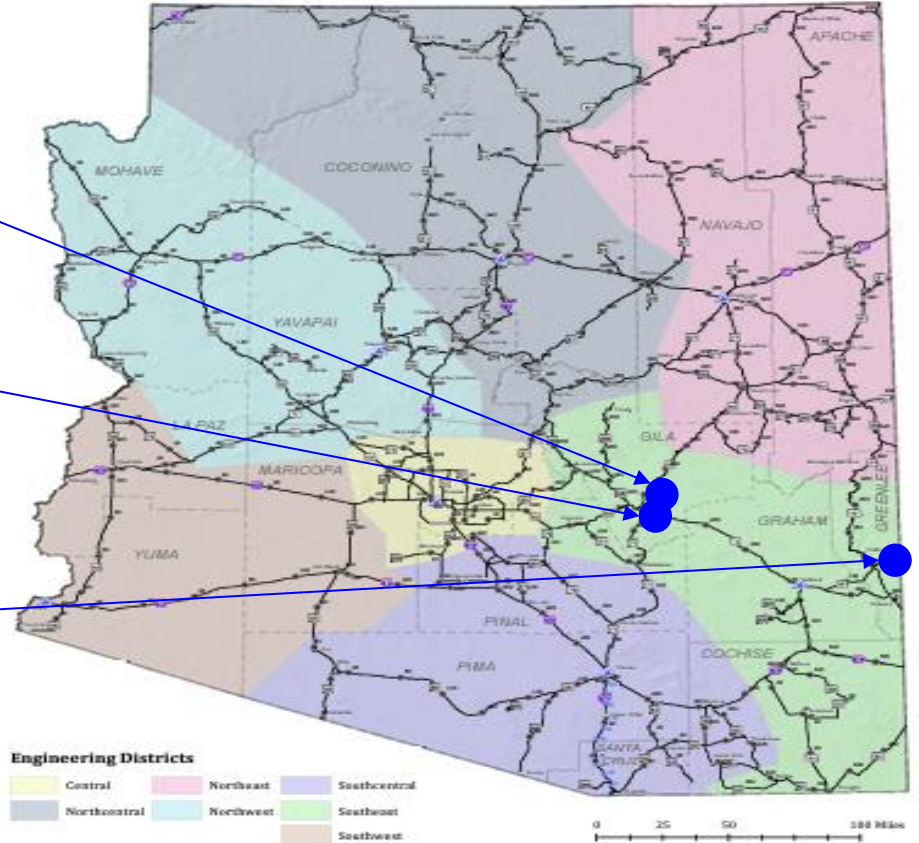

Northwest District Current Projects

Kingman POE Truck Screening

US 93, MP 64 - MP 67

Contractor: William Charles
Construction Company

2% Complete, 28% Time Spent

Needle Mountain TI - Lake Havasu TI

I-40, MP 2.5 - MP 8

Contractor: FNF Construction


80% Complete, 75% Time Spent

Prescott Lakes Parkway to Heather Heights

SR 69, MP 294 - MP 296

Contractor: Fann Contracting

52% Complete, 79% Time Spent

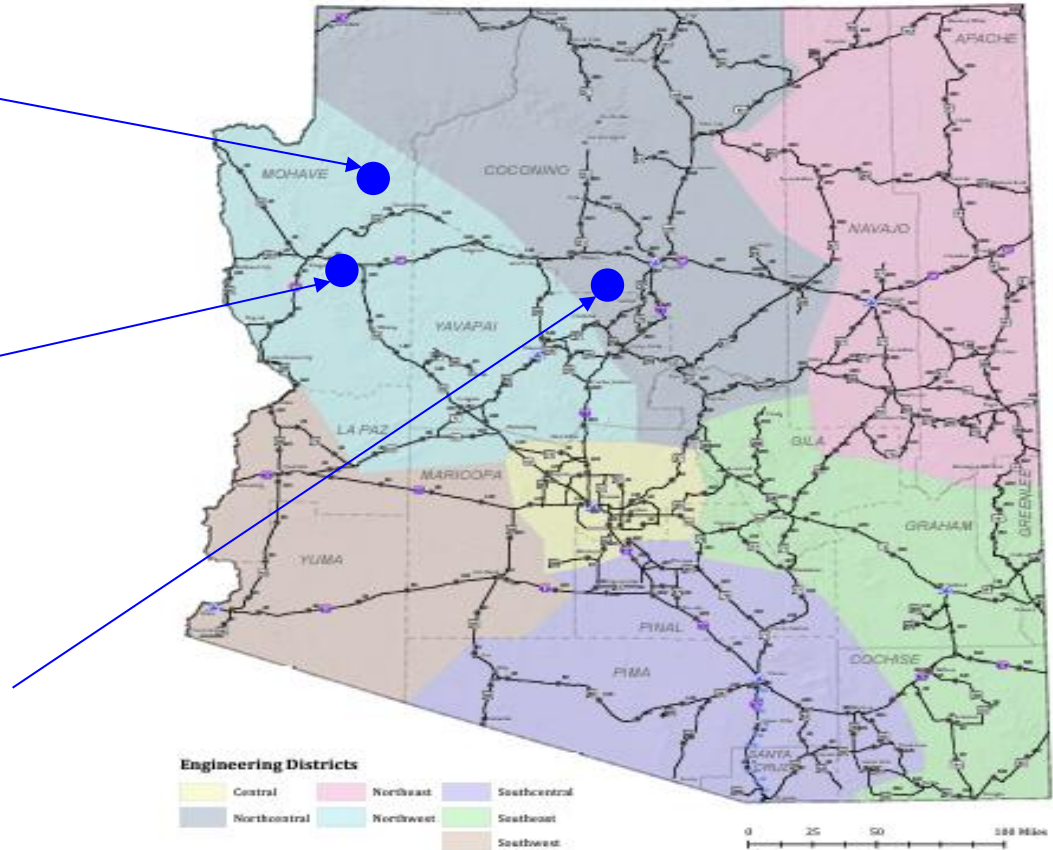


Northeast District Current Projects

**SW Dennehotso to MP 440
US 160 MP 416 - MP 440**

**Allentown TI Bridge
I 40 MP 351**

SR 73 at SR 260 Junction

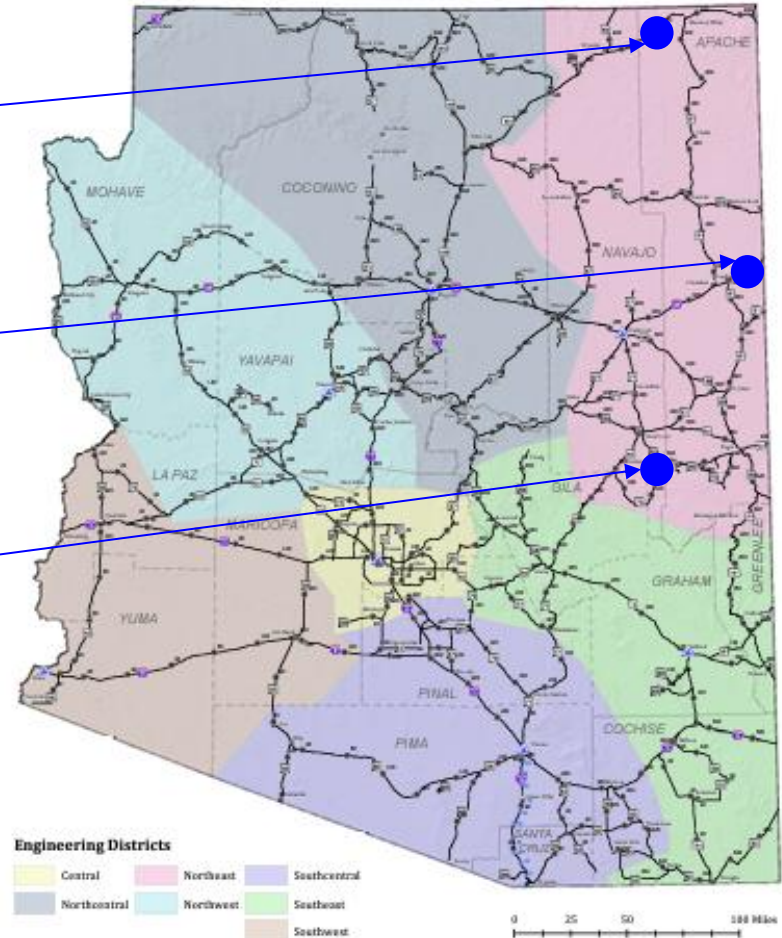

Central District Current Projects

I-17 Happy Valley to SR74
Mill and Diamond Grind
99% Complete 96% Time Spent

SR101 Princess to Shea
Loop 101 Expansion in Scottsdale
58% Complete 55% Time Spent


SR101 I-17 to 75th Ave
Loop 101 Expansion in Phoenix/Glendale
19% Complete 19% Time Spent

SR303 and US60
Interim Interchange Improvements
75% Complete 88% Time Spent

US 60X Sossaman to Meridian
Old US60 Highway
45% Complete 53% Time Spent

SR202 Val Vista to SR101L
Loop 202 Expansion in Chandler/Gilbert
25% Complete 24% Time Spent

I-10 Gila River Bridge
Bridge Replacement
42% Complete 36% Time Spent

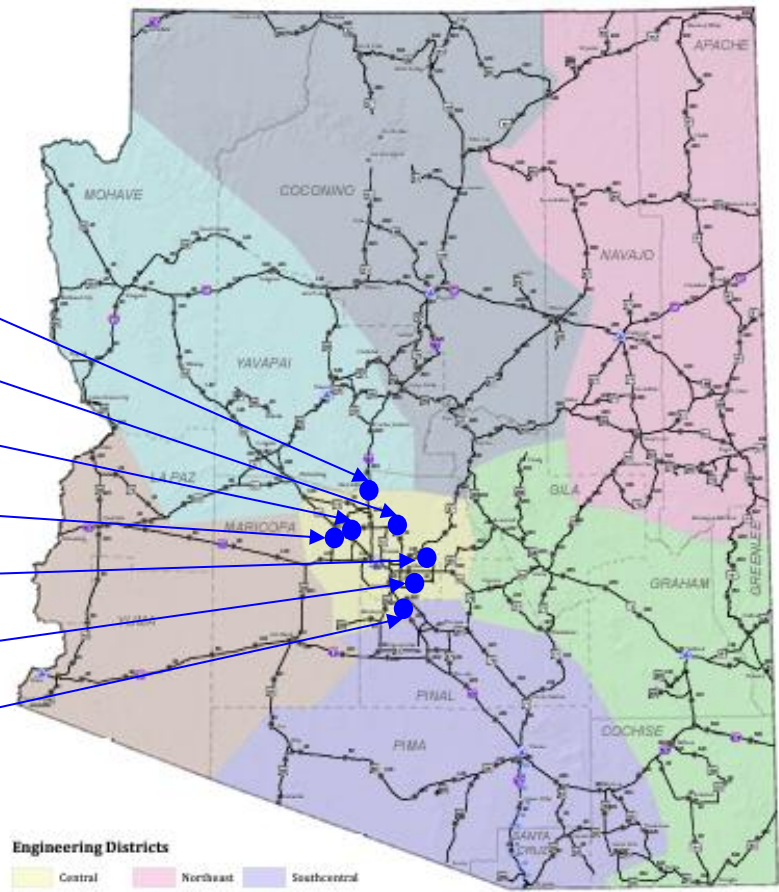

Item 9 – New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3h	I-17	\$15,821,930	\$16,282,255	(\$460,325)	-2.8%
9a	I-40	\$25,252,525	\$29,961,540	(\$4,709,014)	-15.7%
9b	US 60	\$9,517,418	\$12,056,239	(\$2,538,821)	-21.1%
9c	US 163	\$3,137,000	\$2,755,659	\$381,341	13.8%
9d	LOCAL	\$157,547	\$224,300	(\$66,753)	-29.8%
TOTAL THIS MONTH		\$50,591,874	\$58,300,034	(\$7,708,160)	-13.2%
TOTAL FY TO DATE		\$858,831,521	\$786,916,367	\$71,915,155	9.1%

Monthly Totals for Construction Contracts

Month	No. of Bids	Awards	Low bid	State Estimate	Difference	Percent
Jul-24	13	11	\$470,592,428	\$354,288,928	\$116,303,500	32.8%
Aug-24	15	15	\$145,345,707	\$141,346,079	\$3,999,628	2.8%
Sep-24	4	3	\$11,859,518	\$12,791,450	(\$931,932)	-7.3%
Oct-24	11	10	\$91,386,964	\$112,730,729	(\$21,343,765)	-18.9%
Nov-24	5	5	\$19,987,720	\$18,517,824	\$1,469,896	7.9%
Dec-24	1	1	\$19,771,771	\$21,630,643	(\$1,858,872)	-8.6%
Jan-25	6	5	\$49,295,541	\$67,310,680	(\$18,015,139)	-26.8%
Feb-25	5	5	\$50,591,874	\$58,300,034	(\$7,708,160)	-13.2%
Mar-25						
Apr-25						
May-25						
Jun-25						
Fiscal YTD	60	55	\$858,831,521	\$786,916,367	\$71,915,155	9.1%

District 6

**PAVEMENT REHABILITATION
I-40: HOLY MOSES WASH - RATTLESNAKE WASH**

Item 9a

Low Bid	\$25,252,525
State Estimate	\$29,961,540
Difference	-\$4,709,014
% Difference	-15.7%

Recommendation: Award

Reasons for Difference:

- Asphalt Binder
- Asphaltic Concrete



District 5


**PAVEMENT REHABILITATION
US 60: SR 61 - WILDCAT CREEK**

Item 9b

Low Bid	\$9,517,418
State Estimate	\$12,056,239
Difference	-\$2,538,821
% Difference	-21.1%

Recommendation: Award
Reasons for Difference:

- Cover Material
- Asphalt Binder
- Asphaltic Concrete

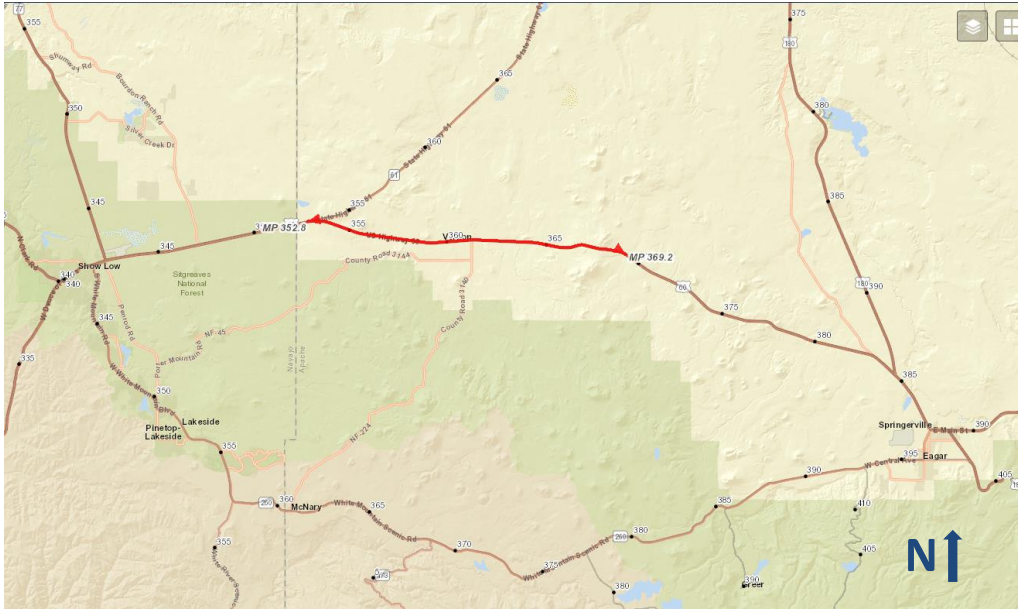

District 5

**SHOULDERS & RUMBLE STRIPS
US 163: MP 404 TO MP 406, N OF KAYENTA**


Item 9c

Low Bid	\$3,137,000
State Estimate	\$2,755,659
Difference	\$381,341
% Difference	13.8%

Recommendation: Award

Reasons for Difference:

- Asphaltic Concrete

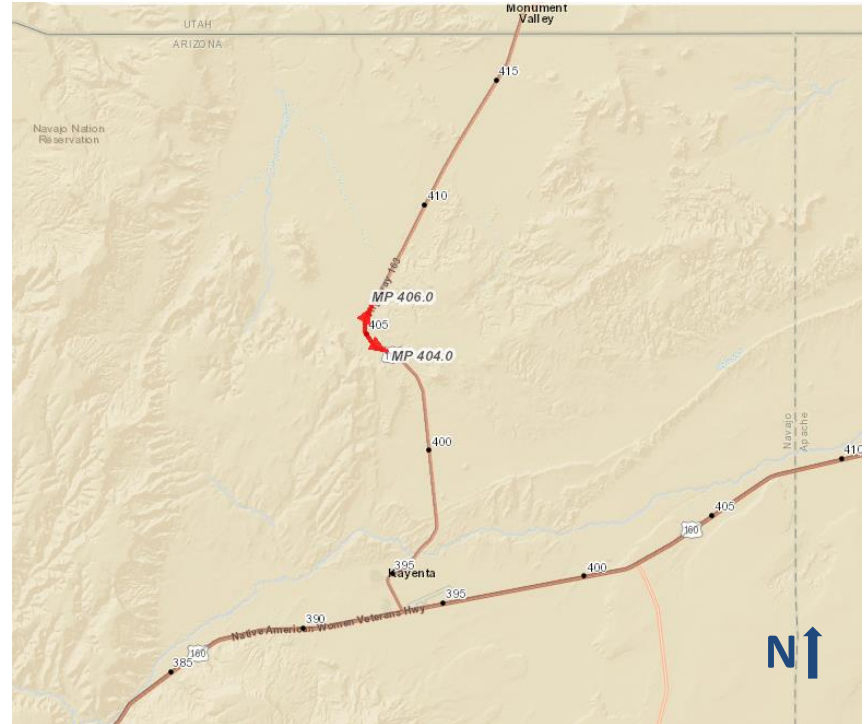

District 2

**WILDLIFE OVERPASS
1-17: WILLARD SPRINGS WILDLIFE OVERPASS**

Item 3h

Low Bid	\$15,821,930
State Estimate	\$16,282,255
Difference	-\$460,325
% Difference	-2.8%

Recommendation: Award

Reasons for Difference:

- Concrete Barrier
- Fence

