

Widening the US 95 Corridor


Presentation by: Bruce Fenske
Southwest District Administrator
October 20, 2023

US 95 Corridor, Avenue 9E to Aberdeen Road

30% Corridor Design

- The full corridor was designed to the 30% design stage
- 30% General plan was completed in 2011
- 2011 cost for right-of-way, utility relocation, and construction




\$118,154,857

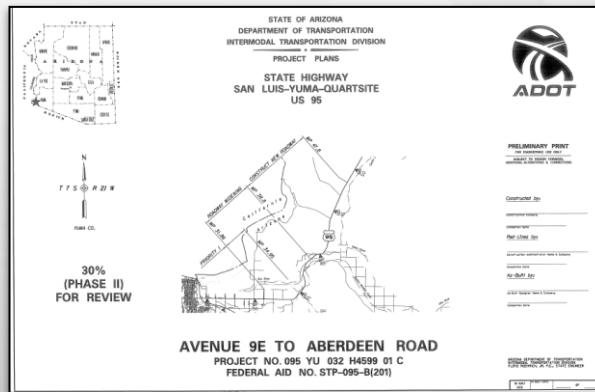

US 95, Avenue 9E to Aberdeen Road

Pre-design Stages


- DCR Completed January 2007
- Recommendation for the southern segment (MP 31.8- MP 38.8) was to widening to five lane section with 10' flush shoulders. The northern segment (MP 38.8-MP 47.8) recommendation was to construct 4 lane divided section with varying median width.
- The total project cost including design, right-of-way, utility relocations, and construction was \$82,561,000 (2006 Dollars)
- Project was segmented into smaller phases
- Environmental Assessment completed for the Corridor in October 2006

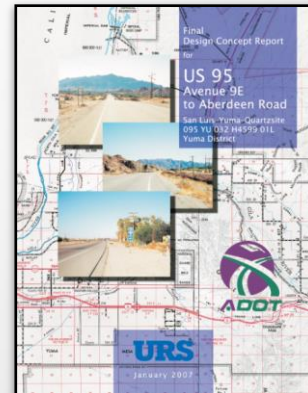

US 95, Avenue 9E to Aberdeen Road *Corridor Cost Breakdown*

Corridor Phasing Breakdown & Cost:

1. Fortuna Wash Bridges - \$10,199,573
2. Ave 9E-Rifle Range Road - \$15,611,285
3. Rifle Range Rd-Wellton Mohawk Canal Bridge - \$23,867,531
4. Wellton-Mohawk Canal Bridge- Imperial Dam Road - \$92M
5. Imperial Dam Road-Aberdeen Road - \$49,250,000

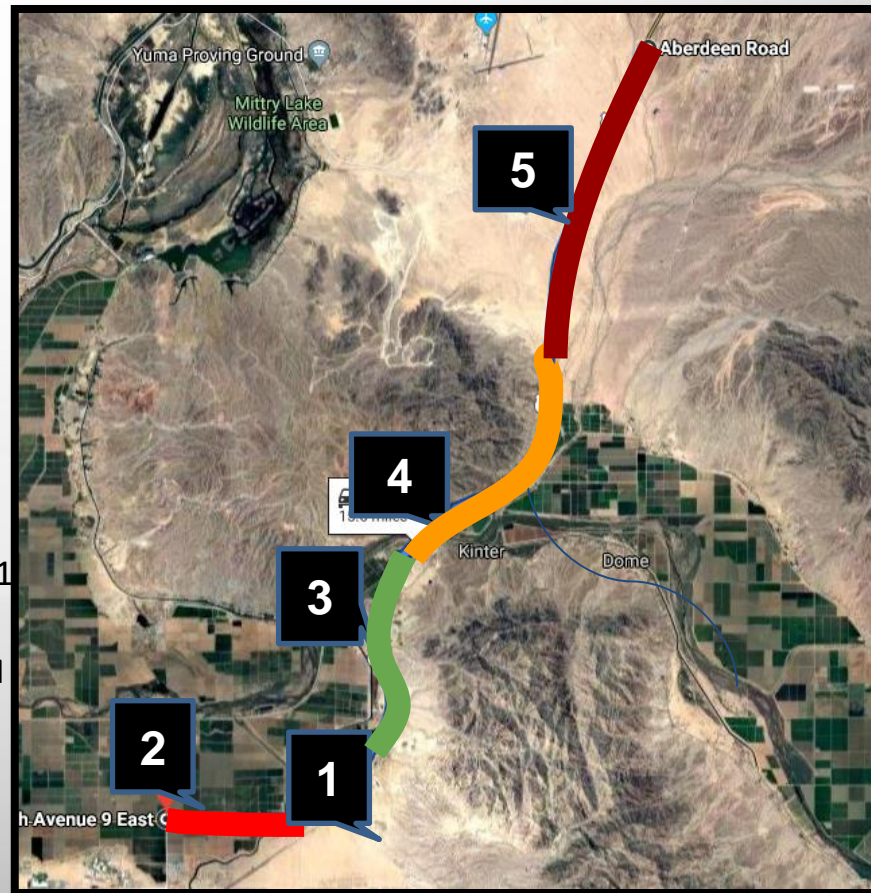

US 95, Fortuna Wash Bridge *Completed Project*

- Contractor – FNF Construction, Inc.
- Project Cost - \$10,199,573
- Start Date – 2/01/2016
- Completion Date – 5/31/2017



US 95, Avenue 9E-Rifle Range Road

Completed Project


- Contractor – Fann Contracting, Inc.
- Project Cost - \$15,611,285
- Start Date – 8/23/2021
- Completion Date – 1/11/2023



US 95, Rifle Range Road - Wellton Mohawk Canal Bridge

Under Construction

- Contractor – Fisher Sand & Gravel Co.
- Project Cost - \$23,867,531
- Start Date – 11/03/2022
- Tentative Completion - February 2024

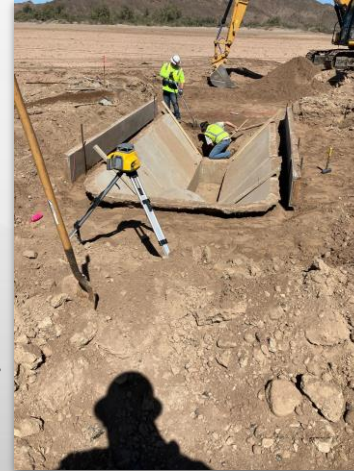

US 95 Corridor

Future

US 95 Project Location in Yuma County, Arizona



- Design & Construct remaining portions of the corridor
- Construction Funding Secured \$32M
- Construction Funding Deficit \$93M
- Continue to pursue funding for Construction through grants (e.g. RAISE & AZ Smart)

US 95, Imperial Dam Road-Aberdeen Road

Future

Project Scope – Roadway Reconstruction & Widening

Project Cost (Including Design) - \$44.25 Million

Design Fiscal Year 2024


Environmental – April 2024

R/W – October 2024

Utility – February 2025

Advertise-March 2025

Expansion

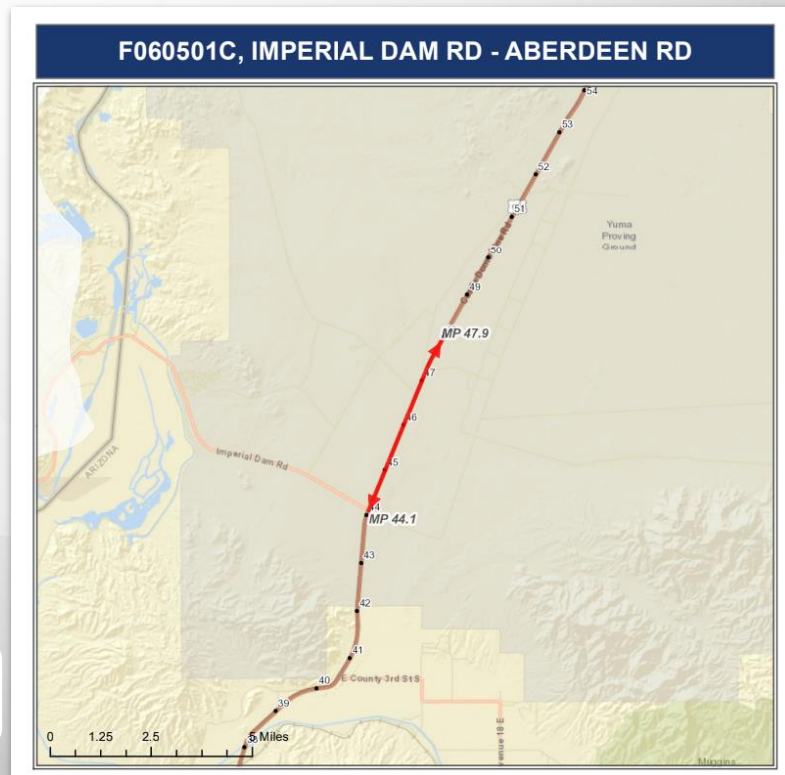

US 95, Wellton Mohawk Canal Bridge- Imperial Dam Road

Future

Project Scope – Roadway Reconstruction
& Widening

Project Cost (Including Design)- \$93
Million

Design Fiscal Year 2024

Environmental – November 2024


R/W – June 2025

Utility – December 2025

Advertise-March 2026

Expansion

F060801C, WELLTON-MOHAWK CANAL - IMPERIAL DAM RD

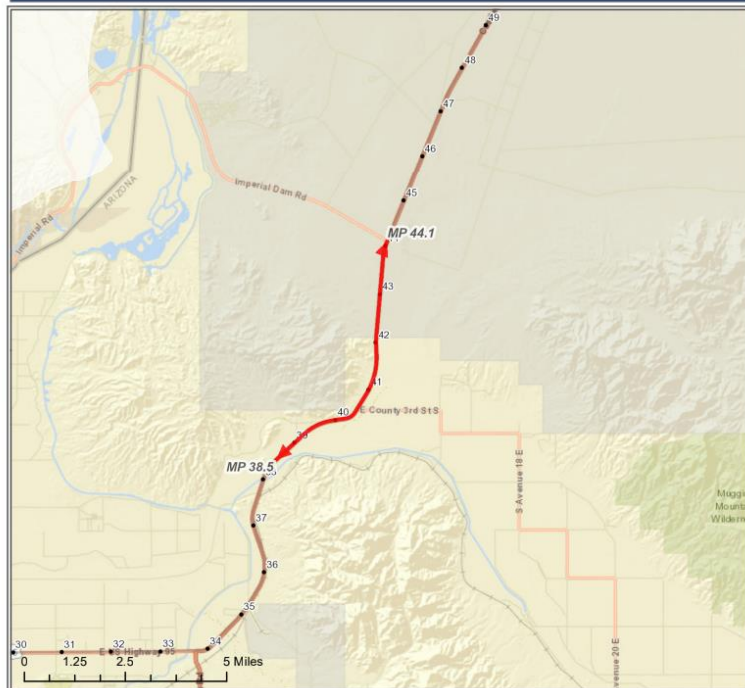

Thank you!

