

Transportation Board Meeting

Phoenix, Arizona



Central District

May 2018

Projects Under Construction


17 Projects Currently Under Construction (64+ Total in FY18)

- 17 Federally Funded Projects
 - 8 LPA Projects (Local Public Agency)

L202, South Mountain Freeway Project - \$917 Million

Overall Construction Cost - \$ 1.025 Billion

- Total Earned - \$413 Million

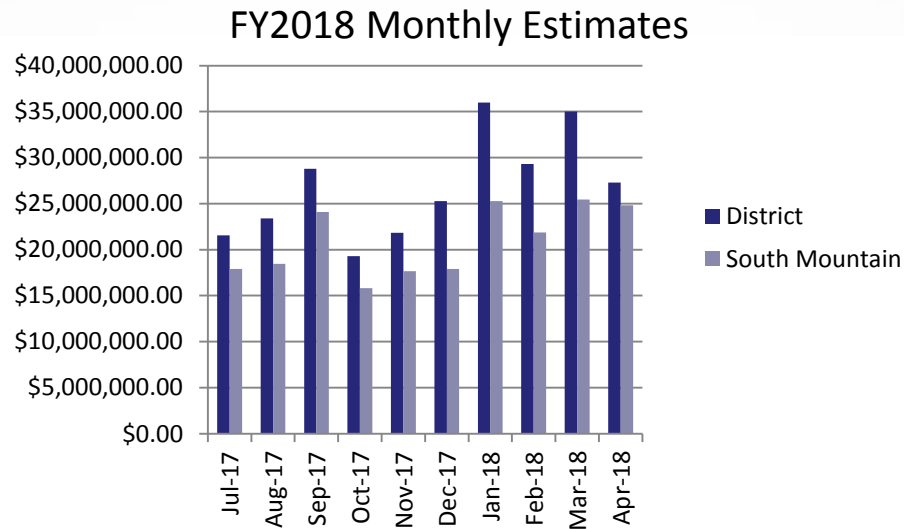


Project Milestones / Completion



I17, Wrong
Way Driver



I10/303
Phase II

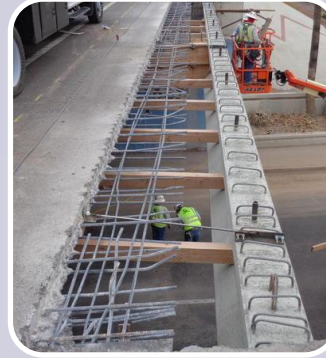

I-17 -7th
Ave Girder
Repair



SR88
Emergency
Repair

Ongoing Projects

South Mountain Freeway

- Contract Amount - \$916M
- Completed Contract Amount - \$440M
- 47% Complete / 59% Time Used



Opening of WB Access Roads between 51st Ave and 67th Ave

Elliot Rd Bridge completed; Opening to traffic.

Completion of 40th St and Roosevelt Bridges

Ongoing construction on 22 of 45 Bridges

NPTP 3 Issued allowing construction in Center Segment

SR347@UPRR

- Contract Amount - \$23.1M
- Completed Contract Amount - \$956K
- 4% Complete / 25% Time Used



ROW Demo

Removals

Drilled Shafts

Weed Control

SR88

- Contract Amount - \$6.5M
- Completed Contract Amount - \$4.36M
- 66% Complete / 62% Time Used



Ford Reconstruction

$\frac{3}{4}$ " AC Paving

Curve Construction

Shoulder Buildup

FY2019 Projects

Happy Valley/Pinnacle Peak TIs CMAR

I-10, Fairway Drive TI

101, I-17 to Princess Design Build

101, Baseline to 202 Santan Design Build

FMS Projects

Local Agency Projects

Thank you

Randy Everett
Senior Division Administrator
Central District
Phone: 602-712-8040
