

# State Transportation Board Meeting

## Northcentral District Update


### April 20, 2019



Quickly Share Snow Trivia:

- On 02/21/19, it snowed 35.9" in 24 hours in Flagstaff
- Snowiest day in recorded history
- Prev. record was 31" in 1915

## NORTHCENTRAL DISTRICT - MAP

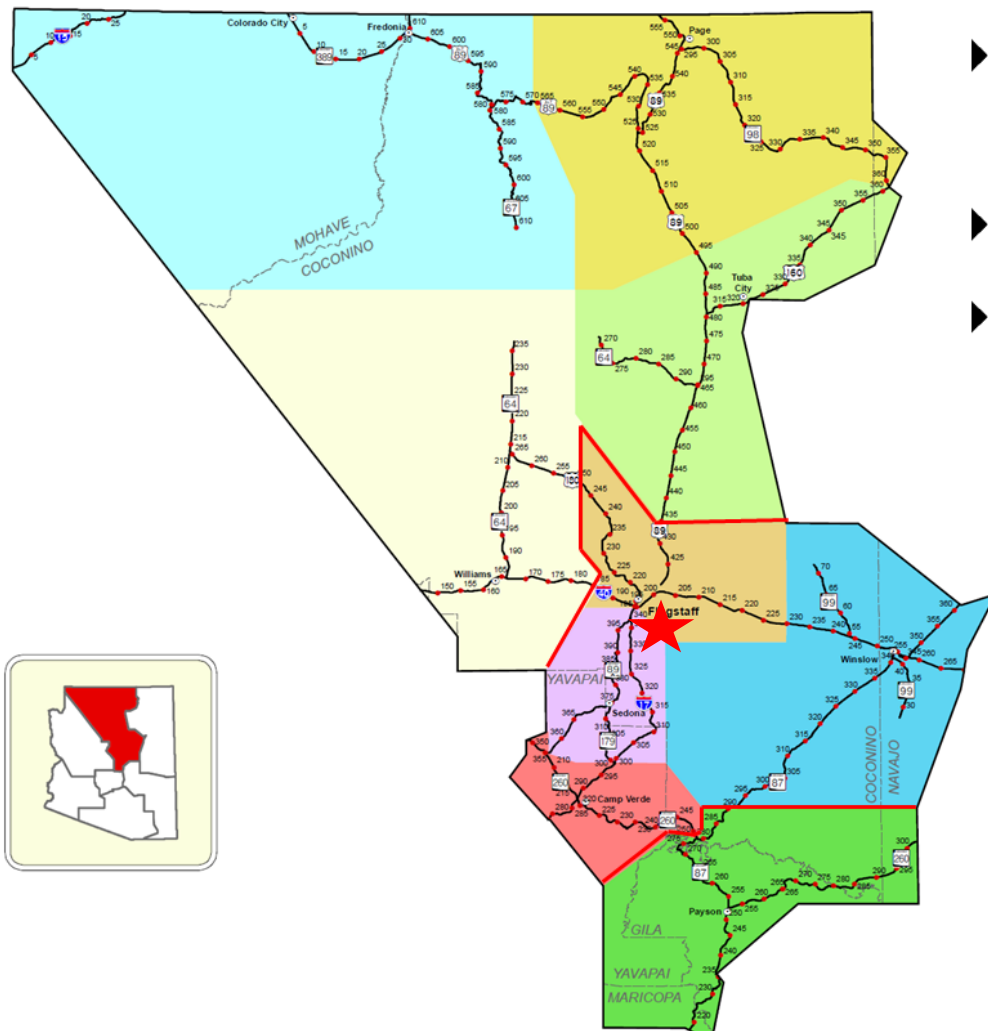

- ▶ District Area ~ 23,200 square miles
- ▶ Just under 2,800 lane miles
- ▶ Coordinate our construction & maintenance activities with over 40 Stakeholders

## MAP

---

- ▶ Quick Update on Current Construction Projects
- ▶ Partnering Awards & Opportunities

## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-40: Cataract Lake to Parks TI

- ▶ Pavement Preservation + Reconstruction area
- ▶ Award Date: Feb., 2018
- ▶ \$35.4 M contract
- ▶ ~ 60% Complete
- ▶ Fann Contracting, Inc.
- ▶ Complete: Fall 2019





## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-40: Cataract Lake to Parks TI



## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-17/I-40 Inter. Bridges



- ▶ Bridge Deck Repl. Work
- ▶ Award Date: Nov. 2017
- ▶ \$10.1 M contract
- ▶ ~ 90% Complete
- ▶ FNF Construction, Inc.
- ▶ Complete this season

## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-17/I-40 Interchange Bridges





## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-17/I-40 Interchange Bridges





## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-17: Cnty Line to I-40 (NB)



- ▶ Pavement Preservation + Bridge Work
- ▶ Award Date: March 2018
- ▶ \$24.5 M contract
- ▶ ~ 60% Complete
- ▶ Southwest Asphalt
- ▶ Complete: Late Fall 2019

## CURRENT CONSTRUCTION – ROLLOVER PROJECTS

### I-17: Cnty Line to I-40 (NB)



Taken:

8/24/18 @ 9:51am



Taken:

8/24/18 @ 2:44 pm



## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS

### I-40 Cottonwood Bridges

- ▶ Bridge Deck Repl. (EB & WB)
- ▶ Award Date: Dec., 2017
- ▶ \$4.5M contract
- ▶ ~ 50% Complete
- ▶ J. Banicki Construction, Inc.
- ▶ Complete: Fall 2019





## CURRENT CONSTRUCTION – 4 ROLLOVER PROJECTS



**I-40 Cottonwood Bridges**

## CURRENT CONSTRUCTION – 6 Add'l Just Starting

- ▶ I-17 Verde River Bridges
- ▶ I-15 Bridges 2, 4, & 5
- ▶ SR179 Ranger Station – Chapel Road





## CURRENT CONSTRUCTION – 6 Add'l Just Starting

- ▶ I-40 Bellemont TI
- ▶ I-40 Meteor City TI OP
- ▶ S40 W. Winslow Spur RR OP





## CURRENT CONSTRUCTION – 6 Add'l Just Starting



Winslow Spur RR OP

## CURRENT CONSTRUCTION – Still to Come

Advertising



- ▶ Various Fog

Advertising



- ▶ SR89A Spur OP

Pending Award



- ▶ I-40 Spot Repair

## PARTNERING AWARDS

### Arizona Transportation Partnering Excellence Award 2018

I-40 Devil Dog Project  
Fann Contracting / ADOT



I-40 Twin Arrows Bridge  
Fann Contracting / ADOT



- AZ AGC 2018 Build Arizona Award
- 2019 IPI Partnered Project of the Year



## UPCOMING LOCAL PARTNERSHIP PROJECTS

- ▶ 4<sup>th</sup> Street Bridge
- ▶ Widen/Repl. Br.
- ▶ City of Flagstaff

- ▶ US89 Horse Shoe Bend
- ▶ Left Turn Lane/Parking
- ▶ City of Page

- ▶ SR89A/SR179
- ▶ Right Slip Lanes
- ▶ City of Sedona



THANK YOU

