

Arizona State Transportation Board Meeting

District Engineer's Report

Todd Emery

December 20, 2024



Current Construction Projects

US 60, Queen Creek Bridge Bridge Replacement

Contract \$40,766,879.28 - 19% Complete

US 60, Waterfall Canyon Bridge Bridge Replacement

Contract \$3,932,694.10 - 15% Complete

US 191, 7th St to MP 173 Pavement Rehabilitation


Contract \$10,153,107.04 - 28% Complete

US 191, Table Top Road to 7th St Pavement Preservation

Contract \$1,206,384.30 - 10% Complete

US 191 At SR 75 & SR 78 Construct Roundabout


Contract \$6,519,519 - 42% Complete

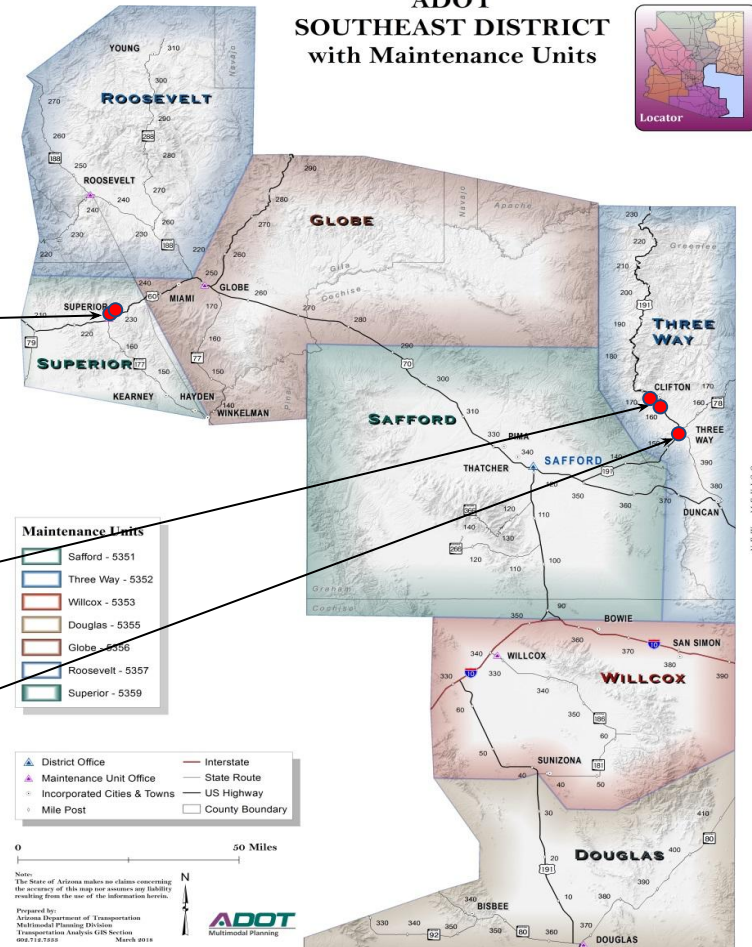

US 60, Queen Creek Bridge




US 60, Waterfall Canyon Bridge

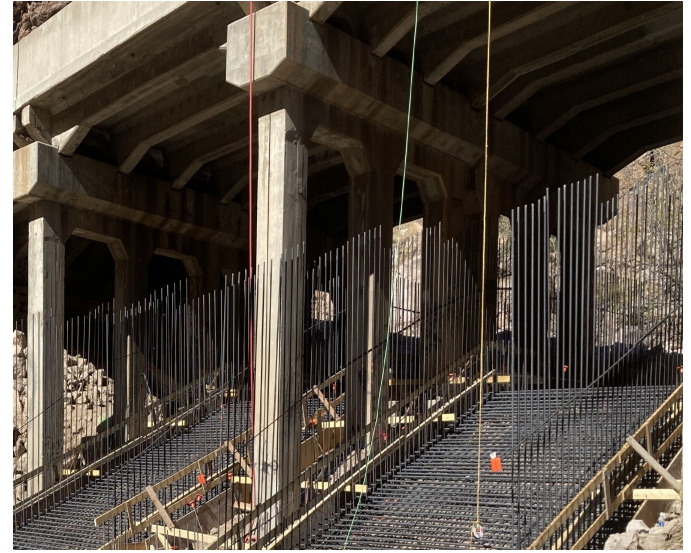

US 191 At SR 75 & SR 78 Roundabout






Current Construction Projects

**US 60, Schulze Ranch - Town of Miami
Drainage Improvements**
Contract \$4,768,811 - 0% Complete

**I-10, East Willcox TI UP Bridge
Bridge Rehabilitation**
Contract - \$1,185,850 - 2% Complete

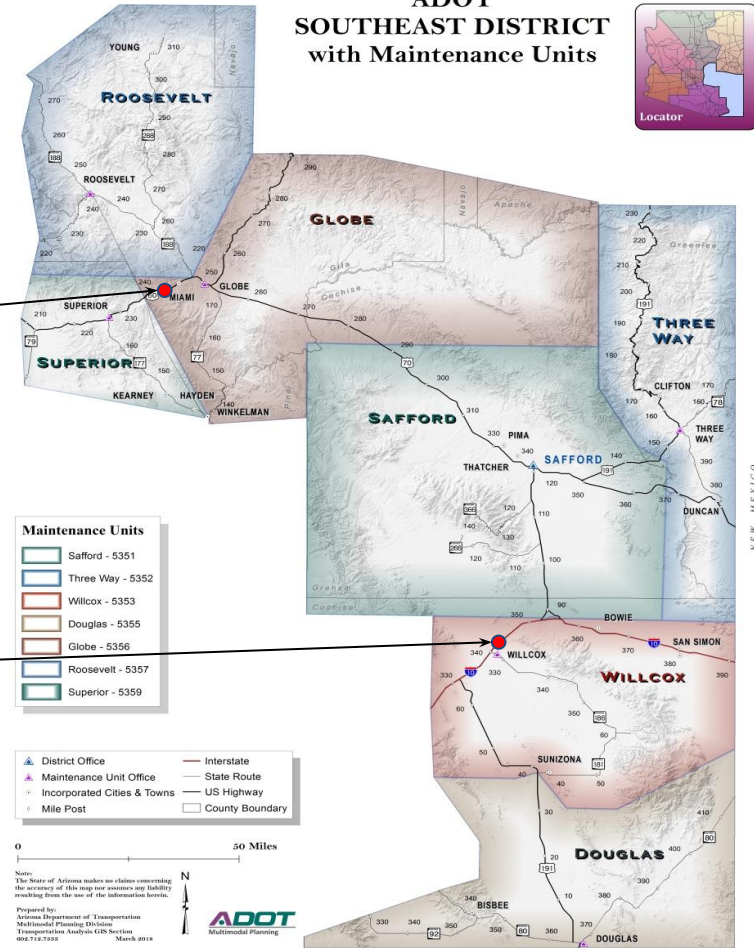

Thank You Questions?
