

Item 7 – State Engineer's Report

December 16, 2022


Summary of Active and Finalized Projects

- **105 projects under construction** **\$2.2 Billion**
- **10 projects finalized in November** **\$81.8 Million**
- **Fiscal Year to date:** **35 projects finalized**

Item 8 – New Construction Contracts

Item	Highway	Low bid	State Estimate	Difference	Percent
3g	I-10	\$21,156,815.75	\$21,378,576.65	(\$221,760.90)	-1.0%
*8a	SR 87	\$7,622,073.85	\$8,385,740.00	(\$763,666.15)	-9.1%
*8b	Local	\$1,222,201.47	\$1,047,481.00	\$174,720.47	16.7%
8c	Local	\$2,125,287.55	\$1,241,707.00	\$883,580.55	71.2%
*8d	Local	\$357,866.13	\$143,385.60	\$214,480.53	149.6%
*8e	Local	\$1,759,779.46	\$1,514,219.20	\$245,560.26	16.2%
8f	Local	\$1,982,289.00	\$1,650,703.76	\$331,585.24	20.1%
TOTAL THIS MONTH		\$25,264,392.30	\$24,270,987.41	\$993,404.89	4.1%
TOTAL FY TO DATE		\$388,466,280.00	\$373,917,787.82	\$14,548,492.18	3.9%

*Items 8a and 8d are "Postponed" and items 8b and 8e are "Reject All Bids" and are not included in the totals

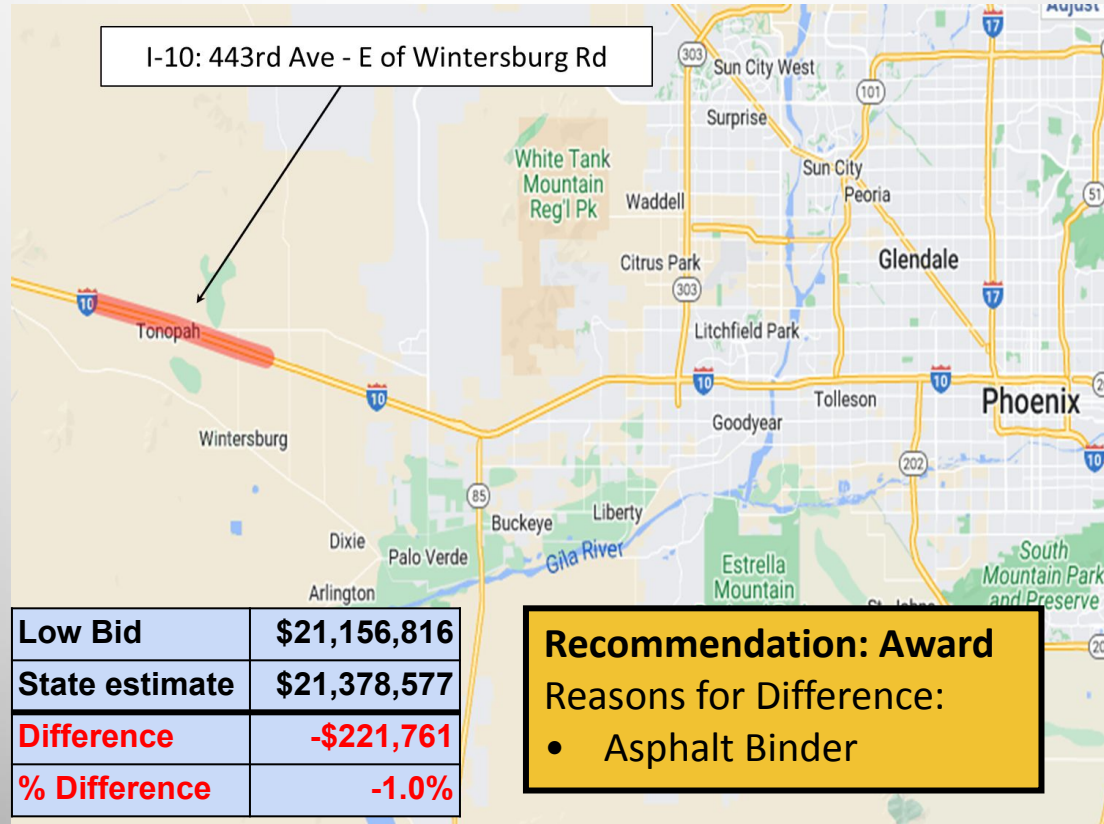


Low Bid	\$7,622,074
State estimate	\$8,385,740
Difference	-\$763,666
% Difference	-9.1%

Recommendation: Postponed

Reasons for Difference:

- Roadway Excavation
- Structural Concrete

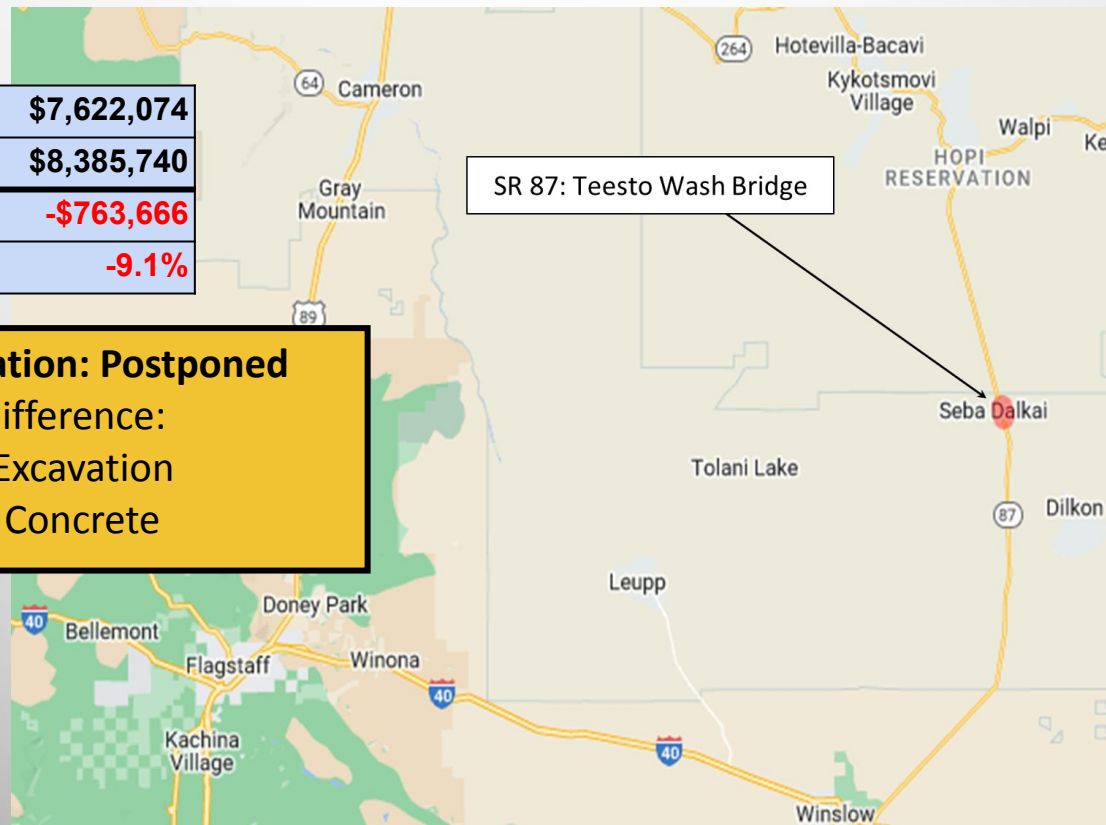


Low Bid	\$1,222,201
State estimate	\$1,047,481
Difference	\$174,720
% Difference	16.7%

Recommendation: Reject All Bids

Reasons for Difference:

- Electrical Conduit
- Fiber Optic
- Pull Box

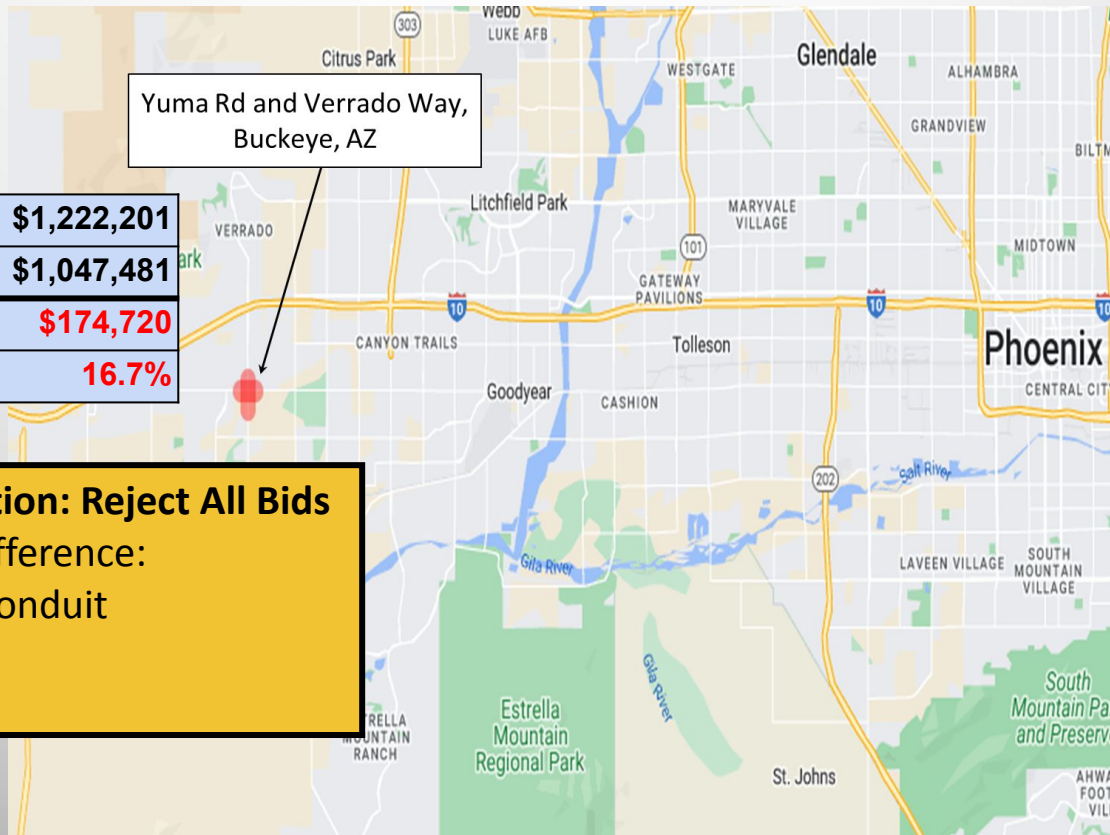

Idaho Rd : Superstition Blvd - McKellips Rd




Low Bid	\$2,125,288
State estimate	\$1,241,707
Difference	\$883,581
% Difference	71.2%

Recommendation: Award

Reason for Difference:

- Removal of Asphaltic Concrete Pavement
- Roadway Excavation
- Aggregate Base
- Electrical Poles, Conduit, Conductor
- Concrete Curb, Gutter, Sidewalk

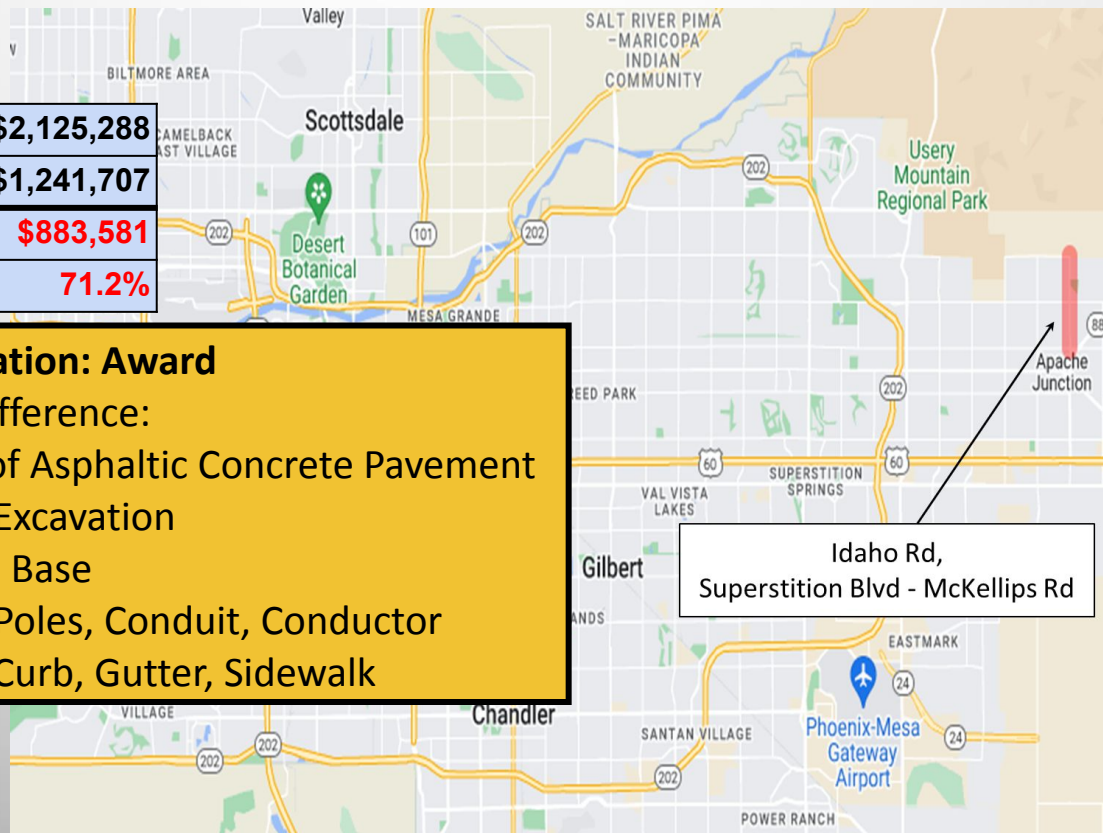

INSTALL PEDESTRIAN HYBRID BEACON


City of Casa Grande: Intersection of Cottonwood Lane and Kadota Avenue

ADOT

Low Bid	\$357,866
State estimate	\$143,386
Difference	\$214,481
% Difference	149.6%

Recommendation: Postponed**Reasons for Difference:**

- Traffic Control
- Control Cabinet
- Mobilization

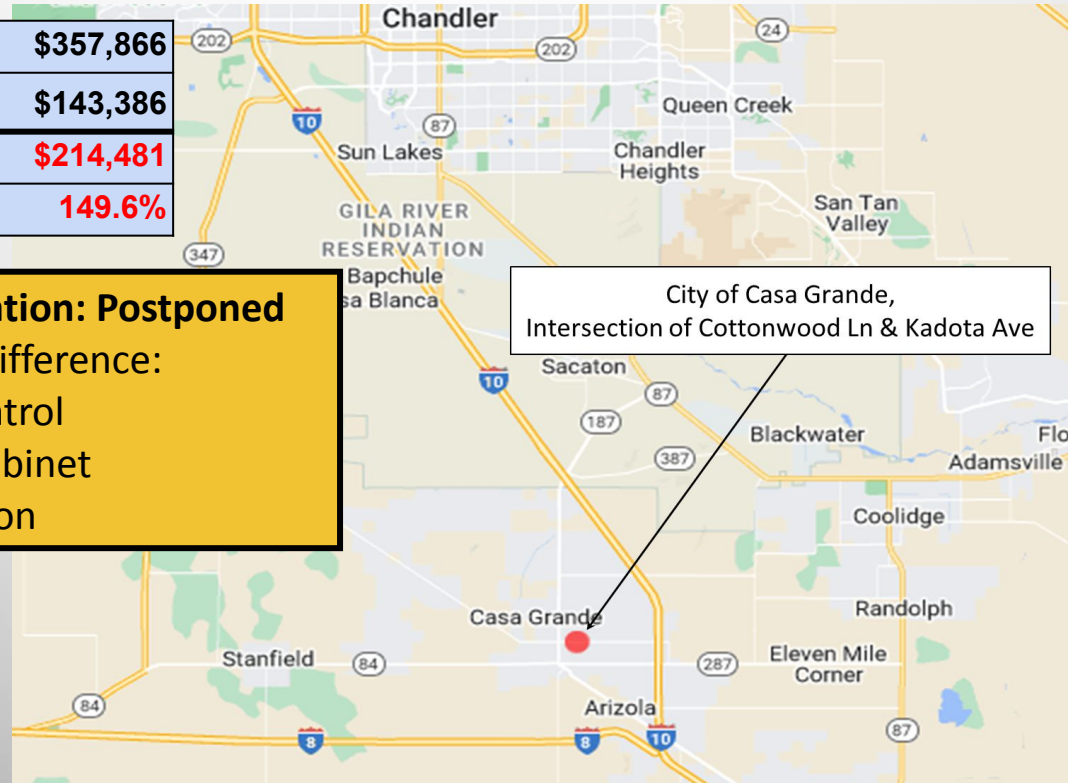


Low Bid	\$1,759,779
State estimate	\$1,514,219
Difference	\$245,560
% Difference	16.2%

Anderson Rd; N of Maricopa - Casa Grande Hwy to Peters & Nall Rd, and Peters & Nall Rd to Antone St

Recommendation: Reject All Bids

Reasons for Difference:

- Contractor Quality Control
- Surveying and Layout

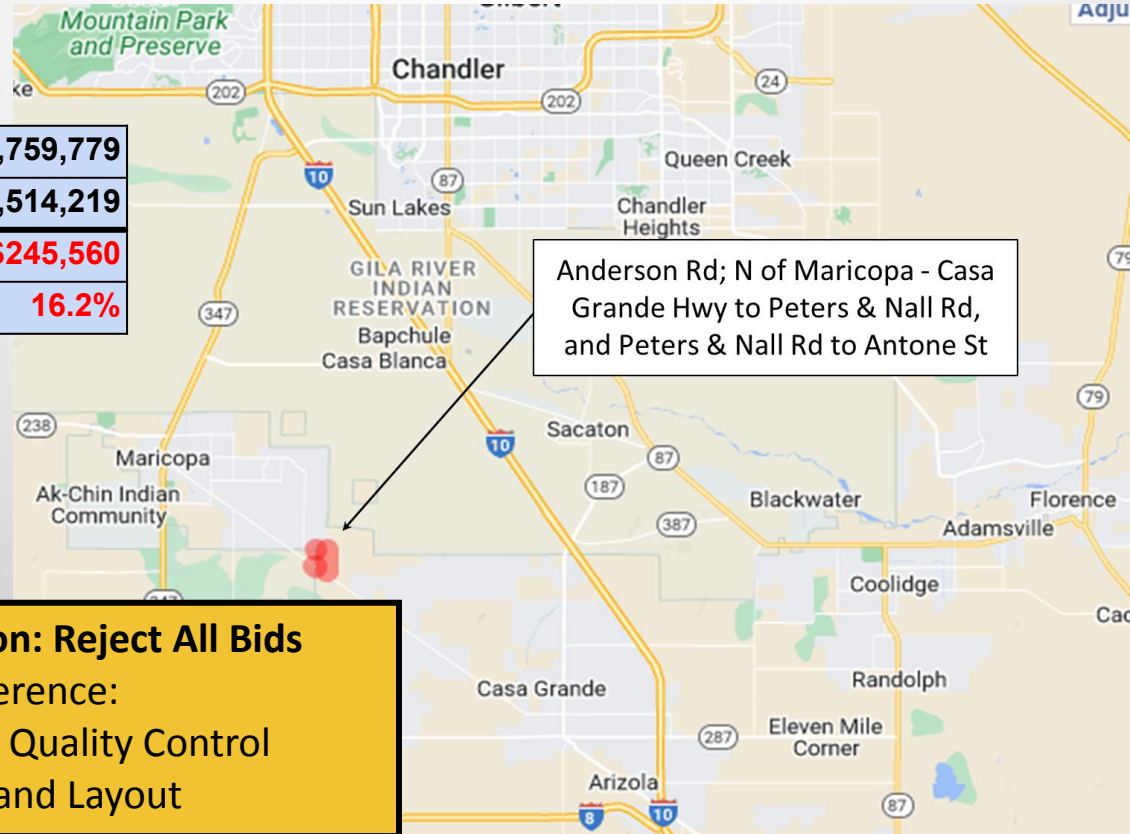

Low Bid	\$1,982,289
State estimate	\$1,650,704
Difference	\$331,585
% Difference	20.1%

Pendleton Dr Dip at
Sonoita Creek Wash

Recommendation: Award

Reasons for Difference:

- Roadway Excavation
- Pipe
- Slope Armoring
- Concrete Slab

