

Item 8 – State Engineer’s Report

June 18, 2021


Summary of Active and Finalized Projects

- **74 projects under construction \$1,523.4 Million**
- **6 projects finalized in May \$51.6 Million**
- **Fiscal Year to date: 67 projects finalized**

Item 9 – New Construction Contracts

ADOT

Item	Highway	Low bid	State Estimate	Difference	Percent
3c	US 95	\$14,877,953.77	\$14,059,307.77	\$818,646.00	5.8%
9a	SR 80	\$2,767,000.00	\$2,076,020.15	\$690,979.85	33.3%
9b	SR 89	\$983,000.00	\$1,279,168.60	(\$296,168.60)	-23.2%
TOTAL THIS MONTH		\$18,627,953.77	\$17,414,496.52	\$1,213,457.25	7.0%
TOTAL FY TO DATE		\$484,213,427.15	\$511,523,222.53	(\$27,309,795.38)	-5.3%

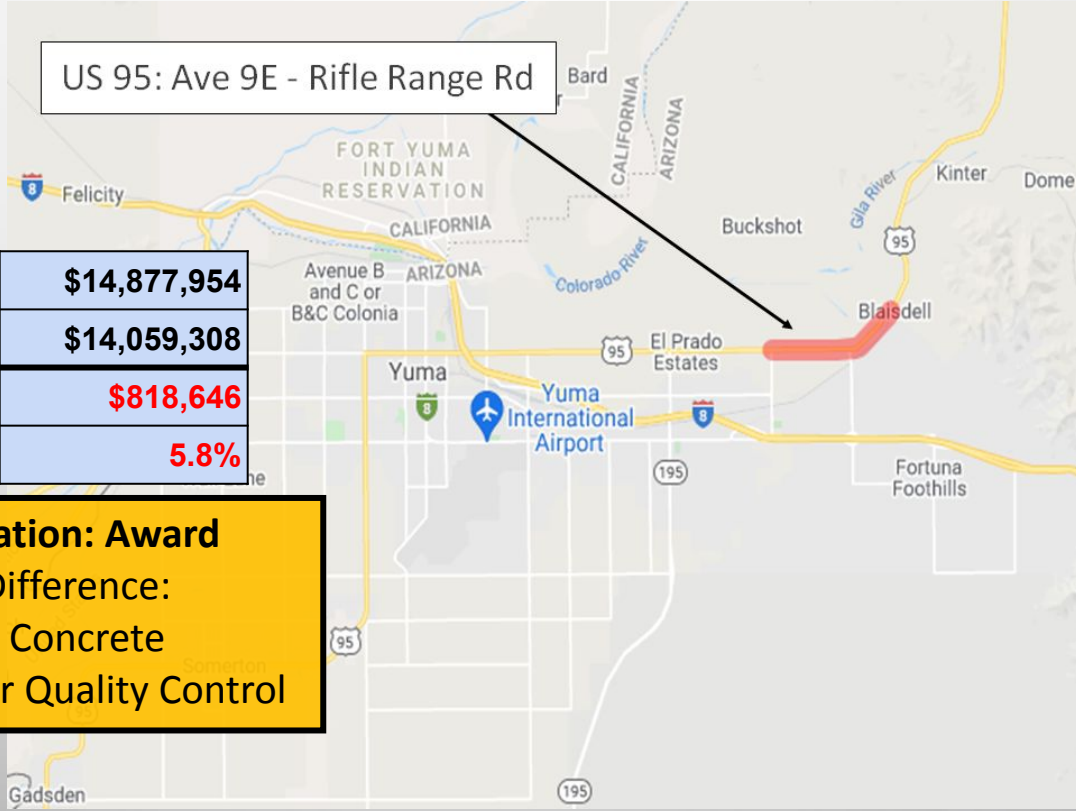


US 95: Ave 9E - Rifle Range Rd

Low Bid	\$14,877,954
State estimate	\$14,059,308
Difference	\$818,646
% Difference	5.8%

Recommendation: Award
 Reasons for Difference:


- Structural Concrete
- Contractor Quality Control

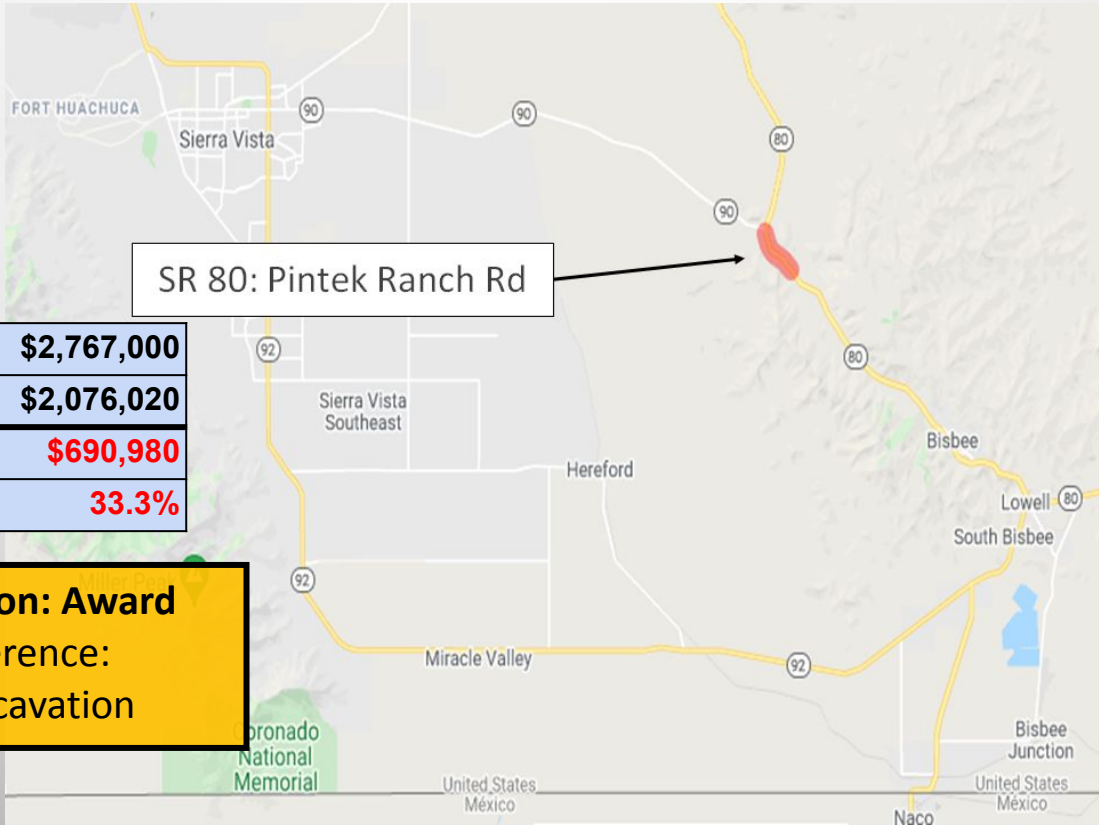

Low Bid	\$2,767,000
State estimate	\$2,076,020
Difference	\$690,980
% Difference	33.3%

Recommendation: Award
Reason for Difference:

- Roadway Excavation

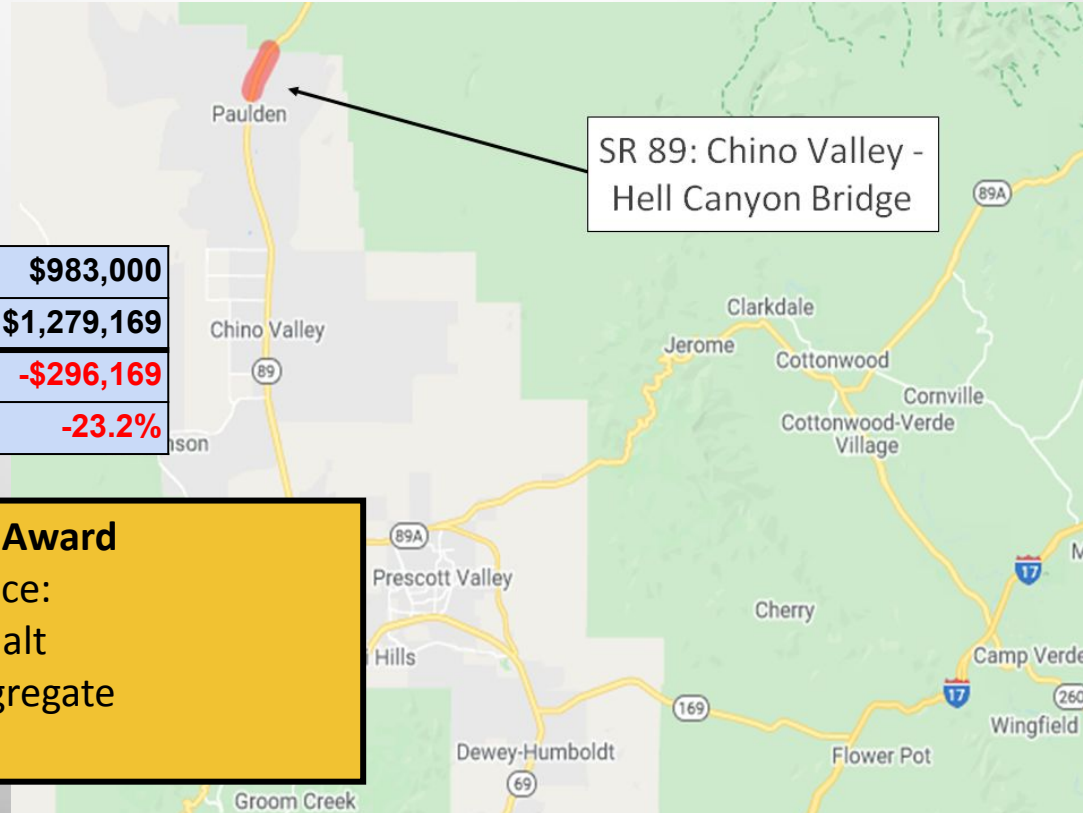

Low Bid	\$983,000
State estimate	\$1,279,169
Difference	-\$296,169
% Difference	-23.2%

Recommendation: Award

Reason for Difference:

- Emulsified Asphalt
- Dry Mineral Aggregate
- Mobilization
